

Central Registry

(120-5-18-9)

SG - building construction - General Assembly
and north parking garage - 1/82 - FTWS Inc

17 Oct. 1951

31 Oct 1951

CLEAR

AT 8/04

S - 0472

Box 28

File 2

(RAG-1)

Central Files

OREGON 9-3950

FULLER - TURNER - WALSH - SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York 17, N.Y.

RE: CONTRACT HQ 1/82 - GENERAL ASSEMBLY AND NORTH PARKING SPACE
ESTIMATE FOR CHANGE NO. 190
"Acoustical Revisions of Studios 3 to 9
Inclusive and Testing Room 1B-58 -
1st basement-G.A."

- References:
- a) Report of Meeting held at U.N.H.P.O. on 5/3/51 (FTWS report dated 5/8/51).
 - b) FTWS, Inc. Letter (Reese) to Mr. James A. Dawson dated 5/2/51
 - c) Bolt, Beranek & Newman - "Acoustics Memorandum for U. N. Permanent Headquarters" - Report on Conference of May 3, 1951 (dated 5/8/51).
 - d) Bolt, Beranek & Newman - "Acoustics Memorandum for U. N. Permanent Headquarters" - Report on Inspection of Studios 5-9 and Testing Room 1B-58 on May 21 & 22, 1951 (dated 5/24/51).
 - e) "Confirmation of Instructions to Superintendent No. 7056" - dated 5/25/51 and signed by Mr. Egan of U. N.
 - f) Mr. James A. Dawson's letter dated 5/29/51 to FTWS, Inc.
 - g) FTWS, Inc. Letter (Grogan) to United Nations dated 6/4/51 (C.O. #190).

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we claim an increase in our total guaranteed maximum cost price in the amount of ONE THOUSAND NINE HUNDRED SEVENTY EIGHT DOLLARS AND SEVENTY SIX CENTS (\$1,978.76) for the changes in the work itemized herein, which are required by the above "references".

This estimate is broken down as follows:

PART IV - SECTION 4 - CEMENT FLOOR FILL & FINISH CEMENT WORK
(Brennan & Sloan, Inc. & Knickerbocker Constr. Corp.)

Deduct

Add

- 1) Install Plywood barrier on floors of Studios 5 to 9 and Room 1B-58. B & S Extra Work Order Tickets 205, 223.

LABOR: Carpenter - 45 hrs. @ \$3.00/hr...\$135.00

Laborer - 22 hrs. @ \$2.15/hr... 47.30

182.30

6% Union Fund..... 10.94

Total Labor..... 193.24

(continued on page 2)

	DEDUCT	ADD
Total Labor.....	\$193.24	
MATERIAL:		
3040 sf. 1/4" Plywood @ \$122.40/m.s.f.....	\$372.10	
300 lf. 1" x 4" Blocking @ \$.039/lf.....	11.70	
4 rolls - Joint Sealing Tape @ \$1.95/roll.	7.80	
Total Material.....	\$391.60	
Total Labor & Material.....	\$584.84	
15% Overhead & Profit.....	87.73	
4.5% Payroll Taxes.....	8.20	
TOTAL - THIS SECTION.....	\$680.77	\$680.77

PART IV - SECTIONS 5 & 6 - MASONRY WORK & MORTARS
(John B. Kelly, Inc.)

- 1) Cut out and patch Masonry around ducts at 1B-58 as per Field Order #8 and Kelly's E.W.O. #165 copy of which is in your possession.

Bricklayer - 8 hrs. @ \$3.25/hr.....	\$ 26.00
Welfare & Pension Fund 9%.....	2.34
	<u>\$ 28.34</u>
15% Overhead and Profit.....	4.25
F.O.A.B. 4.5%.....	1.17
	<u>\$ 33.76</u>

- 2) Install fibre glass and brick at connection of floating walls and solid outer walls as per Sketch on C.I.S. #7056, Kelly's E.W.O. #157. Copies of both are in your possession.

LABOR:

Bricklayer - 35 hrs. @ \$3.25/hr.....	\$113.75
Laborer - 20 hrs. @ \$2.15/hr.....	43.00
	<u>\$156.75</u>
Bricklayer Welfare & Pension Fund 9%....	10.24
Laborers " " " 6%....	2.58

MATERIAL:

Common Brick - 85 @ \$30.50/M.....	2.59
Cement Mortar - 3 c.f. @ \$.50/cf.....	1.50
	<u>\$173.66</u>
15% Overhead and Profit.....	26.05
F.O.A.B. 4.5%.....	7.05
	<u>\$206.76</u>

- 3) Install fibre glass and block above scaffold height at Studios #5 to #9, in accordance with C.I.S. #7056 and Kelly's E.W.O. #162. Copies of both are in your possession.

Bricklayer - 15 hrs. @ \$3.25/hr.....	\$ 48.75
Laborer - 15 hrs. @ \$2.15/hr.....	32.25
	<u>\$ 81.00</u>
Bricklayers Welf. & Pension Fund 9%....	4.39
Laborers " " " 6%....	1.94
	<u>\$ 87.33</u>
15% Overhead & Profit.....	13.10
F.O.A.B. 4.5%.....	3.65
	<u>\$104.08</u>

TOTAL - THIS SECTION.....	\$344.60	\$344.60
Amounts carried forward to page (3).....		\$1025.37

Mr. James A. Dawson
Re: Contract HQ 1/82 - General Assembly
Estimate for Change No. 190

October 31, 1951
page (3)

Figures brought forward from page (2).....

DEDUCT

ADD

\$1,025.37

PART IV - SECTION 20 - FURRING & LATHING
(Jeremiah Burns, Inc.)

- 1) Install Plaster Stops at Doors to Studios
#5 to #9 as per C.I.S. #7056 & Burns E.W.O.
#1767, copies of which are in your possession.

LABOR:

Foreman Lather - 2 hrs. @ \$3.57 1/7/hr.....\$7.14
Lather - 22 hrs. @ \$3.00/hr.....66.00
73.14
Welfare & Pension Funds 6%.....4.39
77.53

MATERIAL:

200 l.f. Milcor #66 Casing @ \$106.50/M.....\$21.30
4 s.y. 3.4 Black Lath @ \$.426/sy.....1.70
100.53
15% Overhead and Profit.....15.08
F.O.A.B. - 4.5%.....3.29
118.90

- 2) Install Plaster Stops at isolated walls in
Vestibule of Studios #3 & #4 as per C.I.S.
#7056 and Burns' E.W.O. #1852, copies of which
are in your possession.

LABOR:

Foreman Lather - 1 hr. @ \$3.57 1/7/hr.....\$ 3.57
Lather - 14 hrs. @ \$3.00/hr.....42.00
45.57
Welfare & Pension Funds @ 6%.....2.73
48.30

MATERIAL:

1 s.y. 3.4 black lath @ \$.426/sy......43
150 l.f. Milcor #66 Casing @ \$106.50/M.....15.98
64.71
15% Overhead and Profit.....9.71
F.O.A.B. - 4.5%.....2.05
76.47

TOTAL - THIS SECTION.....\$195.37.....

\$ 195.37

PART IV - SECTION 22 - ACOUSTICAL TREATMENT & SOUND CONDITIONING
(Johns-Manville Sales Corp.)

- 1) Omit Bituminous Spray and Compressing Fibre
Glass.

Material:- 33 gal. Bituminous Emulsion @ \$.40/..\$13.20

Labor:- For Spreading & rolling 2500

s.f. @ \$.03/.....\$75.00
TOTAL - THIS SECTION.....\$88.20..\$88.20

Figures carried forward to Page (4).....\$ 88.20 \$1,220.74

Mr. James A. Dawson
Re: Contract HQ 1/82 - General Assembly
Estimate for Change No. 190

October 31, 1951
page (4)

	DEDUCT	ADD
Figures brought forward from page (3).....	\$ 88.20	\$1,220.74

PART V - SECTION A - HEATING, VENTILATING & AIR COND.
(Kerby Saunders, Inc.)

- 1) To sound treat ductwork and isolate ductwork
in Studios #3 to #9 incl. TOTAL THIS SECTION..... --- \$ 846.22

Attached are three (3) copies of Kerby Saunders' Summary Sheet marked E.W.O.#20 together with National Sheet Metal Works Estimate (1 sheet) and J. B. Kelly Invoices dated 6/13/51 and 7/28/51 (1 copy only) giving itemized breakdown of this change.

	\$ 88.20	\$2,066.96
		88.20
TOTAL - THIS ESTIMATE.....		\$1,978.76

Will you kindly issue a Change Order-ADDITION in the amount of \$1,978.76 to cover the costs itemized above.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan
Project Manager

MJG:CER:amc
attach.

50-52

National Sheet Metal Works Inc. \$581.63

*See Kelly
Photostat head on
SSR*
All labor and materials to
isolate ductwork in studios #3 to
#9 inclusive (John B. Kelly)

154.21 ✓

735.84

15% overhead & profit

110.38

\$846.22

COPY

National Sheet Metal Works, Inc.

General Assembly

Furnishing labor & materials required to make changes to our shop drawing 1B-1, approved as noted 6/5/51 for sound treating ductwork in testing room.

Materials

✓ 167 lbs. galv. iron @ 11.00 cwt.	18.37
✓ 49 sq.ft. 1" accoustical lining @ 27.00 per 100	13.23
✓ 18 isolation hangers @ 60¢ each	10.80
	<u>42.40</u>
10% Miscellaneous	<u>4.24</u>

46.64

Labor in shop

✓ on galv. iron	10 hrs. ✓
✓ on lining	6 hrs. ✓
✓ on 29 feet of canvas connections	

✓ 15 hrs.

✓ 31 hrs. @ 3.10 per hr. 96.10

✓ 6% Union Funds 5.77

✓ 3.784% Insurance on labor 3.64

105.51

10% Manufacturing & Plant

Overhead 10.55

116.06

Labor on job

✓ Drafting	7 hrs.
✓ On ducts, hangers, & canvas connections	

89 hrs.

96 hrs. @ 3.10 per hr. 297.60

6% Union Funds 17.86

Delivery

315.46

12.00

490.16

15% Overhead & Profit

73.52

563.68

4.56% on 393.70 labor

17.95

Total Increase

\$ 581.63

NOTIFICATION OF CHANGE

Date: October 31, 1951

TO: Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272, United Nations
New York 17, New York

N. C. # 75 Building: GENERAL ASSEMBLY & NORTH PARKING SPACE

Reference Information: a) N.C. #61, R.P. #45, dated 7/26/51
b) N.C. #71, R.P. #50, dated 10/3/51

Description of Changes: 1) This N. C. combines and supercedes N.C.'s #61 & #71.
2) Only the following are included:
a) Omission of Canopy No. 1 & Vestibule #1 complete with all doors and frames. (continued below)

The above contemplated change effects the branches of the work indicated by X marks. There is shown below a quick estimate of the approximate cost of the change merely to indicate its magnitude and to assist the Owner in determining whether or not the change should be made.

() F-T-W-S Inc. Work	() Construction Insulation	() Painting & Finish
() Structural Steel	() Metal, Doors, Frames & Trim	() Venetian Type Blinds
(x) Concrete Construction Work	() Roll-up Steel Doors	() Resilient Floor
(x) Concrete Slabs & Fireproofing	() Metal Toilet Enclosures	Covering
(x) Floor & Roof Fill	() Hollow Metal Partitions	() Miscellaneous
Finish Cement Work	() Marble Work	Accessories
Masonry-Mortars	() Ceramic Tile	() Heating, Ventilating
Waterproofing (Membrane Spondrel)	() Terrazzo Work	& Air Conditioning
Dampproofing (Mastic)	(x) Purring & Lathing	(x) Plumbing
(x) Caulking	(x) Plastering	() Sprinklers
(x) Cut Stonework	() Acoustical Treatment	(x) Electrical
Roofing (built-up)	Sound Conditioning	(x) Sheet Metal Work
Carpentry & Millwork	(x) Miscellaneous Iron	(x) Glass & Glazing
(x) Ornamental Metal Work	(x) Finish Hardware	

Approximate Total Cost of this Change is \$ 9500. (DEDUCTION)
NINETY FIVE HUNDRED DOLLARS-DEDUCTION)

and the Owner's immediate decision is required, avoiding a "Stop Order" of Field Operations and permitting the work to continue without interruption.

FULLER-TURNER-WALSH-SLATTERY, INC.

By: M. J. Gorman Date: 10/31/51
Project Manager

The Above change will not be made and the work is to proceed in accordance with the existing Contract Requirements.

You are hereby instructed to proceed with the work in accordance with this N.C. and issue P.W.O.'s as required. Price adjustments to be made under the Contract Terms.

UNITED NATIONS HEADQUARTERS

UNITED NATIONS HEADQUARTERS

Y: _____ Date: _____

By: [Signature] Date: 11/15/51

b) Add Special Door-North Public Lobby per Dwg. SK-668 dated 8/9/51.

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 316 - October 25, 1951 - Architectural Revision No. 45

- References:
- (a) U. N. Drawing A-2, Rev. No. 45, dated October 25, 1951
 - (b) U. N. Drawing A-5, Rev. No. 45, dated October 25, 1951
 - (c) Bulletin of Changes to Rev. No. 45, dated October 25, 1951
 - (d) Mr. James A. Dawson's letter of October 29, 1951
 - (e) U. N. Drawing SK-GA-H-1-6, dated October 23, 1951
 - (f) Mr. James A. Dawson's letter of October 25, 1951

Dear Mr. Dawson:

On October 26, 1951 we received prints of References (a), (b) and (c).

On October 30, 1951 we received your transmittal letter, Reference (d), which reads as follows:

"With reference to the items shown on the Bulletin of Changes, the following will cause a change to the Contract Price and you are to proceed as follows.

Item No. 2, Drawing A-2, perform the installation of the cinder block partitions, the cement base, the plaster work and painting, the installation of the doors and bucks and all hardware on a time and material basis, the daily time slips to be signed by the U. N. inspectors. Verbal instructions were given to you reference this matter on 26 October 1951.

Item No. 4, Drawing A-5, there will be a slight change caused by this item. Proceed with the work included therein and also with all of the remainder of the work shown in the rest of the items in the Bulletin of Changes.

"Submit for our consideration prices on all of the above which will affect the Contract Price."

continued...

Mr. James A. Dawson

-2-

HQ 1/82 -CHANGE NO. 316
Architectural Rev. No. 45

On October 26, 1951 we received prints of Reference (e) and October 30, 1951 we received your transmittal letter, Reference (f), which reads as follows:

"On 25 October 1951 we forwarded you twenty-one (21) copies of Drawing SK-GA-H-1-6, the revisions to the ductwork in the Maintenance Area in the 2nd Basement.


"Proceed with the work shown thereon and submit for our consideration prices which affect the Contract Price.

"The costs of this change should be included in the same change under which the costs of Revision No. 45 shall be included."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan
Project Manager

MJG/PDV/en

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Garage -
CHANGE NO. 302 - October 8, 1951 Structural Revisions

References: (a) U.N.Dwg. GA-2-CS-29C, Issued 10/8/51
(b) " " GA-2-CS-23, Rev. No. 2, 10/8/51
(c) Mr. James A. Dawson's letter 23 October 1951

Dear Mr. Dawson:

On October 8, 1951 we received prints of References (a) and (b) and on October 25, 1951 we received your transmittal letter, Reference (c) which reads, in part, as follows:

"Reference GA-2-CS-29C, the concrete base will cause a change in cost to the Contract Price. This item has already been included. For the inclusion of this item, see our letter to you dated September 28, 1951 wherein we state that drawing SK-673 was issued to you.

Proceed with the work with the understanding that there will be no change to the Contract Price. If you do not agree, please notify us promptly."

We have sent the above referenced drawings to the interested sub-contractors with the request that they advise us if these revisions affect their subcontract price.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PEV/eas

FULLER - TURNER - WALSH - SLATTERY, INC.
 UNITED NATIONS CONTRACT
 403 EAST 42ND STREET
 NEW YORK 17, N. Y.

file
 October 31, 1951

Mr. James A. Dawson
 Co-Ordinator of Construction
 Headquarters Planning Office
 Room 2272
 United Nations, New York 17, N.Y.

RE: CONTRACT HQ 1/82 - GENERAL ASSEMBLY AND NORTH PARKING SPACE
ESTIMATE FOR CHANGE NO. 224
"June 28, 1951 Structural Revisions"

References: a) United Nations Drawing GA-R-CS-25C, dated 6/25/51
 b) " " " GA-S-35C, Rev. #7, dated 6/27/51
 c) FTWS Letter (Grogan) to United Nations dated 7/5/51 (C.O.#224)
 as compared with:
 d) United Nations Drawing GA-S-36C, dated 5/3/51
 e) " " " GA-S-35C, Rev. #6, dated 4/9/51
 f) " " " GA-A-5, Rev. #15, dated 3/7/51

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we hereby claim an increase in our total guaranteed maximum cost price in the amount of NINETY ONE DOLLARS AND NINETY THREE CENTS (\$91.93) for the items of work listed herein which are required by the changes in the structural drawing in reference (a) and by our Change No. 224 which is reference (c) above. Comparison of the structural drawing in reference (b) with the drawings in references (e) and (f) reveals no change which will affect our maximum cost price.

The above increase is broken down as follows:

GA: SECTIONS 2 & 3 - CONCRETE CONSTRUCTION
(Brennan & Sloan, Inc.)

ADD

a) By reference (a) added new reinforcing in Section 36-43.

1) Add 0.26 tons of reinforcing steel @ \$301.18/ton	\$ 78.31
Labor = \$41.47	
O & P 15%	11.75
FOAB 4.5%	1.87
TOTAL ADDITION - THIS ESTIMATE	\$ 91.93

Will you kindly issue a Change Order-ADDITION in the lump sum amount of \$91.93 to cover the net additional work itemized above.

Very truly yours,
 FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan

MJG:CER:amc

M. J. Grogan
 Project Manager

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/75 - Meeting
Halls and Covering Over East
River Drive -
Change No. 350 - Expansion Joints
in Roof at 83'-0" Level

Dear Mr. Dawson:

We are attaching hereto a copy of The Tremco Manufacturing Co.'s (Mr. C. R. McNamara) letter of October 29, 1951 in which he asks us to recall and withdraw his letter of October 17, 1951 to us in which he expresses his "purely personal point of view" regarding the use of Flexcell in the bottom of the subject expansion joints and the selection of tool consistence compound.

Copies of Mr. McNamara's letter of October 17, 1951 were inadvertently attached to your copies of our Change No. 350, dated October 18, 1951, and our Proceed Work Order #10 to New York Roofing Company, dated October 18, 1951. Will you please send back to us these copies of the letter referred to in order that they may be destroyed.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/eas



THE TREMCO MFG. CO.
1607 Graybar Bldg .-420 Lexington Ave.
New York 17, N.Y.

October 29, 1951

Mr. C. E. Reese, Project Engineer
Fuller Turner Walsh Slattery, Inc.,
403 East 42nd St.
New York City 17

re: United Nations Meeting Hall-
Expansion Joints

Dear Mr. Reese:

I should like, if I may, to recall and withdraw my letter to you of October 17th in which I expressed a purely personal point of view regarding the use of Flex-cell in the bottom of the expansion joints and the selection of tool consistency compound.

The specification, as approved, certainly represented the concensus at the meeting held October 16th, and the use of Flex-cell certainly had the approval and sanction of our Mr. Gordon Hann.

Cordially yours,

C. R. McNamara /s/

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General
Assembly and North Parking
Garage -
Cut Stone Work

Dear Mr. Dawson:

On October 18, 1951 we received your letter of October 16, 1951 regarding the Liberty Mutual Insurance Co.'s complaint to Mormile & Company, Inc. that they had permitted one of their men to ride on the fall line of their crane during their stone setting operations.

For your information, we are attaching hereto four (4) copies of Mormile & Co.'s letter of October 24, 1951 to Monahan-McCann Stone Co. and four (4) copies of the Monahan-McCann Stone Co.'s letter of October 25, 1951 to FTWS, Inc.

You will note that Mormile & Co. has ordered its men never to repeat the act and will immediately dismiss anyone who does. In view of this guarantee against a recurrence of the act, we again recommend that you approve Mormile & Co., Inc. as the setter for the cut stone for the North Parking Space.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER/eas



MORMILE & CO. INC.

Stone Setters, Contractors

RECEIVED

OCT 25 1951

MAIN OFFICE
100 STEUBEN STREET
BROOKLYN 5, NEW YORK
MAIN 2-5519 - 5666 - 6575

BRANCH
MONAHAN-McCANN
14 OLD FARM ROAD
LAKE SUCCESS, L. I., NEW YORK
GREAT NECK 4-9592

Brooklyn, N.Y., October 24, 1951

Monahan McCann Stone Co.
100 Roanoke Avenue
Newark, New Jersey

Re: UNITED NATIONS HEADQUARTERS, NO. PARKING LOT
AREA, NEW YORK CITY


Gentlemen:

Confirming our telephone conversation of recent date regarding the letter from Fuller, Turner, Walsh Slattery Inc. we wish to advise you that when we were first advised on October 1st, 1951 of the workman riding on the fall line of our truck crane we immediately ordered our men never to repeat this act and if it ever happens again, the guilty person or persons will be dismissed immediately.

We have every confidence that this will not happen again in view of the above orders.

Yours very truly,

MORMILE & CO., INC.


Harold J. Suwal
Vice-President

MONAHAN-McCANN STONE Co.

SINCE 1892

Cut Stone Contractors

100 ROANOKE AVENUE, NEWARK 5, N. J.

Telephone Market 2-1872

From NEW YORK dial COntlandt 7-4770

October 25th 1951

MESSRS FULLER TURNER WALSH SLATTERY INC.,
403 East 42nd Street,
New York 17 N. Y.

Attention Mr. C. E. Reese.

Gentlemen: RE: SETTING SUBCONTRACTOR NORTH PARKING GARAGE.

We refer to your letter of October 18th requesting action on
Mormile's workmen riding the fall line of their crane.

Attached herewith is Mormile's guarantee against a recurrence
of this breach of your rules. We have personally spoken to
everyone involved and received the utmost assurance that the
offense will not be repeated.

Very truly yours,

MONAHAN-McCANN STONE COMPANY.

by


Pres.

Frank C McCann-p

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Carpentry & Millwork

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following Carpentry & Millwork shop drawings submitted by Murray Hill Woodworking Corp.:

305	Rev. 10/26/51	F. S. & Elevation - Doors Nos. 205, 207, 209, 215 to 219 incl., 260, 261, 262.
321	Dtd. 10/30/51	Plan & Elevations at Coat Room #104 - Elevator 5-6.
322	Dtd. 10/30/51	F. S. Details of Paneling- Counter at El. 41'-0".

Will you please return two (2) prints each of the above drawings marked with your approval or necessary corrections?


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



ISSUANCE OF DRAWINGS

OFFICE COPY

31 October 1951

14 November 1951


GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Murray Hill Woodworking

2 305 26Dec'50 F.S. & Elevation - Doors 205, 207, 215 to 219 etc.
(APPROVED AS NOTED 13 Nov 1951 VR RESUBMIT)

NOTE: Dwgs. 321 and 322 will follow



SV Tyler

ISSUANCE OF DRAWINGS

OFFICE COPY

31 October 1951

15 November 1951


GA & North Parking

Fuller-Turner-Walsh-Slattery

hand

Submitted by Murray Hill Woodworking

2	321	30Oct'51	Plan & Elevs. at Coat Room 104 - Elevator 5-6
2	322	"	F.S. Details of Paneling Counter at El. 41'-0"
			(NO ACTION 14 Nov 1951 SEE LETTER DATED 14 Nov'51)



L.V. Gyle

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

*Final Approved
Gen Files
11/1 LST*

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Ornamental Metal shop drawing, as
approved for field distribution:

GBA-8 Rev. 10/18/51 Door Frames & Coverings
Nos. 227-236, 239-248.

(General Bronze Corp. & C. E. Halback & Co.)
Subcontractor


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

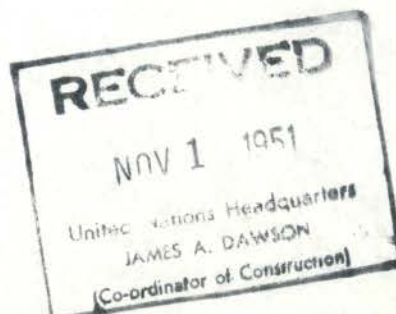

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Ornamental Metal shop drawing, as
approved for field distribution:

GBA-8 Rev. 10/18/51 Door Frames & Coverings
Nos. 227-236, 239-248.

(General Bronze Corp. & C. E. Halback & Co.)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/en

9

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Ornamental Metal shop drawing, as
approved for field distribution:

GBA-8 Rev. 10/18/51 Door Frames & Coverings
Nos. 227-236, 239-248.

(General Bronze Corp. & C. E. Halback & Co.)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MM/cm

-9✓

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Ornamental Metal shop drawing, as
approved for field distribution:

GBA-8 Rev. 10/18/51 Door Frames & Coverings
Nos. 227-236, 239-248.

(General Bronze Corp. & C. E. Halback & Co.)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MM/cm

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

*Final Approved
Gen Files 11/1
LOT*

Re: Contract HQ 1/82 - General Assembly
and North Half Parking Space
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1) print of the following Miscellaneous Iron shop drawings, as approved for field distribution:

HGP-13-10	Dtd. 9/24/51	Ladder at Elev. Machine Room - El. 85'-0"
HGP-44-6	Rev. 10/5/51	Inserts & Gratings on Roof Wells Nos. 1 & 2
HGP-49-11	Rev. 10/9/51	Steel & Glass Screen 302/GM & 313/GM
HGP-105-1	Rev. 10/22/51	Circular Steel Skylight at Cols. 32-J
HGP-109-1	Rev. 10/22/51	Six fixed Glass Frames in East Wall-With Lintels
HGP-114-1	Dtd. 10/22/51	Steel Ring for Glass Eye in Dome.

(General Bronze Corp. & C. E. Halback & Company)
Subcontractor


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/en

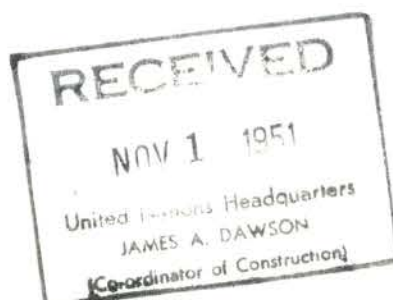

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly
and North Half Parking Space
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1) print of the following Miscellaneous Iron shop drawings, as approved for field distribution:

HGP-13-10	Dtd. 9/24/51	Ladder at Elev. Machine Room - El. 85'-0"
HGP-44-6	Rev. 10/5/51	Inserts & Gratings on Roof Wells Nos. 1 & 2
HGP-49-11	Rev. 10/9/51	Steel & Glass Screen 302/GM & 313/GM
HGP-105-1	Rev. 10/22/51	Circular Steel Skylight at Cols. 32-J
HGP-109-1	Rev. 10/22/51	Six fixed Glass Frames in East Wall-With Lintels
HGP-114-1	Dtd. 10/22/51	Steel Ring for Glass Eye in Dome.

(General Bronze Corp. & C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/en

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly
and North Half Parking Space
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1) print of the following Miscellaneous Iron shop drawings, as approved for field distribution:

HGP-13-10	Dtd. 9/24/51	Ladder at Elev. Machine Room - El. 85'-0"
HGP-44-6	Rev. 10/5/51	Inserts & Gratings on Roof Wells Nos. 1 & 2
HGP-49-11	Rev. 10/9/51	Steel & Glass Screen 302/GM & 313/GM
HGP-105-1	Rev. 10/22/51	Circular Steel Skylight at Cols. 32-J
HGP-109-1	Rev. 10/22/51	Six fixed Glass Frames in East Wall-With Lintels
HGP-114-1	Dtd. 10/22/51	Steel Ring for Glass Eye in Dome.

(General Bronze Corp. & C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/en

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly
and North Half Parking Space
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1) print of the following Miscellaneous Iron shop drawings, as approved for field distribution:

HGP-13-10	Dtd. 9/24/51	Ladder at Elev. Machine Room - El. 85'-0"
HGP-44-6	Rev. 10/5/51	Inserts & Gratings on Roof Wells Nos. 1 & 2
HGP-49-11	Rev. 10/9/51	Steel & Glass Screen 302/GM & 313/GM
HGP-105-1	Rev. 10/22/51	Circular Steel Skylight at Cols. 32-J
HGP-109-1	Rev. 10/22/51	Six fixed Glass Frames in East Wall-With Lintels
HGP-114-1	Dtd. 10/22/51	Steel Ring for Glass Eye in Dome.

(General Bronze Corp. & C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

GER/MM/em

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

*Final Approved
Gen Files
11/1
LW*

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Ornamental Metal shop drawing, as
approved for field distribution:

GBA-36 Rev. 10/12/51 Alum. Loud Speaker Frames.

(General Bronze Corp. & C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

*Final Approved
Gen Files
11/1
LW*

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Ornamental Metal shop drawing, as
approved for field distribution:

GBA-36 Rev. 10/12/51 Alum. Loud Speaker Frames.

(General Bronze Corp. & C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Ornamental Metal shop drawing, as
approved for field distribution:

GBA-36 Rev. 10/12/51 Alum. Loud Speaker Frames.

(General Bronze Corp. & C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

-9

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (CA)
Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Ornamental Metal shop drawing, as
approved for field distribution:

GBA-36 Rev. 10/12/51 Alum. Loud Speaker Frames.

(General Bronze Corp. & C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

**UNITED NATIONS CONTRACT
NEW YORK**

October 31, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Ornamental Metal shop drawing, as
approved for field distribution:

GBA-36 Rev. 10/12/51 Alum. Loud Speaker Frames.

(General Bronze Corp. & G. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

G. E. Reese
Project Engineer

CER/MH/em

120-5-18-9
31 October 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Samples - North Parking Space Cut Stone
Anchoring Devices

Gentlemen:

Reference is made to your letter of the 24th instant, wherewith you transmitted for our consideration and/or approval samples in triplicate of various anchoring devices you propose to provide for use in conjunction with the Cut Stone Work of the North Parking Space. These samples are as follows:

3/16" x 3" Slot Anchor Galvanized
3/16" x 3" Anchor Clip Galvanized
3/16" x 8" Cramp Anchor Galvanized
5/8" x 2-3/4" Lag Screw and Shield
1 1/16" O.D. (approx.) x 4" Brass Pipe Dowels.

Please be advised that the materials forming the various types of devices you submitted for consideration, all as illustrated by the samples here submitted, are approved for use as satisfying the applicable requirements of the Construction Trades Specifications, Part IV, Section 8, paragraph 4, sub-paragraph (d). In so far as we can determine from visual inspection, the galvanizing of the units so finished generally appears to be acceptable. However, we wish to reiterate that the necessary galvanizing shall be accomplished after fabrication of the several units. In no way shall the Contractor construe the foregoing approval as an acknowledgment or verification on the part of this office that the shapes and/or dimensions of the samples submitted are therefore necessarily accurate, correct and appropriate for securing the Cut Stone Work.


This approval in no way relieves the Contractor of his responsibility for the satisfactory performance of the work in accord with the Specifications of the Contract Documents.

31 October 1951

Returned herewith, marked "Approved", are two (2) of each type of sample submitted.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

HEW:js 

cc: Nelson

Weigel

Healy

Harris

Hopper

Zunser

VanName

Ryer

Scilipoti

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 30, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 318 - Structural Revisions

References: (a) GA-S-20c Rev. 10/9/51 Roof Plan and Sections
(b) GA-S-62c Rev. 10/9/51 Misc. Concrete Details of Dome.
(c) Mr. James A. Dawson's letter, dated October 17, 1951

Dear Mr. Dawson:

On October 17, 1951 we received prints of References (a) and (b).

On October 19, 1951 we received your transmittal letter, Reference (c) which reads in part as follows:

"The revisions to these drawings were discussed at a meeting held in the U. N. Headquarters Planning Office, at which meeting Mr. Kearney of Brennan & Sloan was present, and the decision was that these revisions would cause no change to the Contract Price. Proceed with the work."

We have also sent the above-referenced drawings to the other interested subcontractors with the request that they advise us if these revisions affect their subcontract price.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/BK/em

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 30, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 317 - Structural Revisions

References: (a) GA-2-CS-33c, issued October 24, 1951, Alteration to Slab
Thickness and Wire Mesh For One Panel.
(b) Mr. James A. Dawson's Letter, dated October 26, 1951

Dear Mr. Dawson:

On October 24, 1951 we received prints of Reference (a).

On October 29, 1951 we received your transmittal letter, Reference (b)
which reads in part as follows:

"Reference GA-2-CS-33c, there will be a change in concrete
thickness and wire mesh for one panel.

"Proceed with the work shown on the above drawings and sub-
mit for our consideration prices which affect the Contract
Price."

Under the authority and requirements of the contract, we hereby request
that proper adjustment of the contract price and contract time be dealt
with under the terms and conditions of the contract. This change will
be analyzed with all interested subcontractors and detailed estimates
will be submitted to you as quickly as possible. Definite extension of
contract time for completion will be requested as soon as determination
can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/BK/en

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 30, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Garage -
CHANGE NO. 301 - October 4, 1951 Architectural Revisions No. 43

- References: (a) List of Drawings and Bulletin Contained on the Attached Table
(b) Mr. James A. Dawson's letter 9 October 1951 to FTWS, Inc.

Dear Mr. Dawson:

On October 8, 1951 we received prints of the drawings contained in Reference (a), and on October 15, 1951 we received your transmittal letter, Reference (b), which reads, in part, as follows:

"None of the revisions listed above should affect the Contract Price with the possible exceptions of:

- (a) Item 3 of Drawing RA-126 on Page 1 of the Bulletin, the detail section through the curtain pocket. Since this item was deleted as per your letter to us dated 3 July 1951, and our letter of 11 July 1951 to you, it will now be an addition to the Contract.
- (b) Item 4 of Drawing RA-126 on page 1 of the Bulletin.
- (c) Item 1 of Drawing RA-149 on Page 2 of the Bulletin. Reference this item the detail of the eye of the dome has been added on this drawing but the first appearance of this addition of the eye was on Drawing A-10, Item 2, Bulletin of Changes, Revision No. 37. Therefore include the cost of this item in Revision No. 37 using the detail on Drawing RA-149 of Revision No. 43.
- (d) Item 1 of Drawing RA-166 on Page 2 of the Bulletin. This item has already been covered by our letter to you dated 4 September 1951 and by previous Notification of Change No. 58, approved in our letter to you dated 29 August 1951.

Submit for our consideration the prices which will affect the Contract Price and proceed with the work."

Continued

Mr. James A. Dawson

-2-


October 30, 1951

re: Change No. 301 - October 5, 1951 Architectural Revision No. 43

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan
Project Manager

MJG/PDV/eas

LIST OF DRAWINGS & BULLETIN INCLUDED IN REV. NO. 43 - CHANGE NO. 301

A-6	Rev. No. 43	dated October 5, 1951
RA-126	"	"
RA-127B	"	"
RA-127D	"	"
RA-134	"	"
RA-149	"	"
RA-166	"	"
RA-174	"	"
Bulletin of Changes, Rev . No. 43, dated October 5, 1951		

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

October 30, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Garage -
CHANGE NO. 294 - September 27, 1951 Structural Revisions

References: (a) U.N.Dwg. GA-4-CS-29 Issued September 27, 1951
(b) Mr. James A. Dawson's letter 27 September 1951 to FTWS, In

Dear Mr. Dawson:

On September 27, 1951 we received prints of Reference (a) and on October 2, 1951 we received your transmittal letter, Reference (b), which reads, in part, as follows:

"This drawing shows added plates and wells for beams on the 4th floor level near Columns O 27 and J 27.

Proceed with the work shown thereon with the understanding that there is no change to the Contract Price since only steel work is affected."

We have sent the above referenced drawing to the interested subcontractors with the request that they advise us if this revision affects their sub-contract price.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/eas

Shopper
Healy

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

October 30, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

To Mr. Dawson

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawings submitted by General Bronze Corp. and C. E. Halback & Company:

HGP-101-1	Rev. 10/29/51	Developed Elevations of East and West Walls and Schedule of Brackets.
HGP-101-3	Dtd. 10/26/51	Angle Wall Supports - Below Booths & Bent Plate Brackets from Booth to Cheeks.

Drawing HGP-101-1 revised is being forwarded to you to be reviewed with the previous issue which was sent to you October 19, 1951.

Will you please return two (2) prints each of the above drawings marked with your approval or necessary corrections?

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer



ISSUANCE OF DRAWINGS

OFFICE COPY

30 October 1951

7 November 1951


GA & North Parking
Fuller-Turner-Walsh-Slaterry

hand

Submitted by General Bronze & Halback

2	HGP-101-1	18 Oct '51	Developed Elevations of E & W Walls & Schedule of Brackets
2	101-3	26 Oct '51	Angle Wall Supports - Below Booths & Bent Plate Brackets from Booth to Checks

(APPROVED AS NOTED 7 Nov 1951 HEN RESUBMIT)



L. V. Eyles

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 30, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

RECEIVED

OCT 31 1951

United Nations Headquarters
JAMES A. DAWSON
(Co-ordinator of Construction)

Re: Contract HQ1/82 - General
Assembly and North Half
Parking Space (CA)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one print
each of the following Miscellaneous Iron shop drawings, as
approved for field distribution:

HGP-56-1	Rev. 10/15/51	Framing & Sash for Booths in East Wall
HGP-56-2	" "	Framing & Sash for Booths in West Wall
HGP-56-3	" "	F. S. Plan Sections of Assembly Hall Booths
HGP-56-4	" "	F. S. Vertical Sections of Assembly Hall Booths
HGP-56-5	" "	Scale Details of Typical Bay for Upper & Lower Booths.

(General Bronze Corp. & C. E. Halback & Co.)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer



COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

October 30, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ1/82 - General
Assembly and North Half
Parking Space (GA)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one print
each of the following Miscellaneous Iron shop drawings, as
approved for field distribution:

HGP-56-1	Rev. 10/15/51	Framing & Sash for Booths in East Wall
HGP-56-2	" "	Framing & Sash for Booths in West Wall
HGP-56-3	" "	F. S. Plan Sections of Assembly Hall Booths
HGP-56-4	" "	F. S. Vertical Sections of Assembly Hall Booths
HGP-56-5	" "	Scale Details of Typical Bay for Upper & Lower Booths.

(General Bronze Corp. & C. E. Halback & Co.)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

October 30, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ1/52 - General
Assembly and North Half
Parking Space (GA)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one print
each of the following Miscellaneous Iron shop drawings, as
approved for field distribution:

HGP-56-1	Rev. 10/15/51	Framing & Sash for Booths in East Wall
HGP-56-2	" "	Framing & Sash for Booths in West Wall
HGP-56-3	" "	F. S. Plan Sections of Assembly Hall Booths
HGP-56-4	" "	F. S. Vertical Sections of Assembly Hall Booths
HGP-56-5	" "	Scale Details of Typical Bay for Upper & Lower Booths.

(General Bronze Corp. & G. E. Halback & Co.)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

-9-

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
NEW YORK

October 30, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ1/82 - General
Assembly and North Half
Parking Space (GA)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one print each of the following Miscellaneous Iron shop drawings, as approved for field distribution:

HQP-56-1	Rev. 10/15/51	Framing & Sash for Booths in East Wall
HQP-56-2	" "	Framing & Sash for Booths in West Wall
HQP-56-3	" "	F. S. Plan Sections of Assembly Hall Booths
HQP-56-4	" "	F. S. Vertical Sections of Assembly Hall Booths
HQP-56-5	" "	Scale Details of Typical Bay for Upper & Lower Booths.

(General Bronze Corp. & G. E. Halback & Co.)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CKR/MH/em

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 29, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Heating, Ventilating and
Air Conditioning - Shop
Drawings

Dear Mr. Dawson:

We are submitting to you herewith six (6) prints of National Sheet Metal Drawing GA-1B-16, 1st Basement Duct Layout, as forwarded to us by Kerby Saunders, Inc.

Kindly review the above drawing and return three (3) copies with your comments and/or approval.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese *psb*
C. E. Reese
Project Engineer

CER/PLB/em



ISSUANCE OF DRAWINGS

OFFICE COPY

29 October 1951

16 November 1951

GA & North Parking

Fuller-Turner-Walsh-Slattery

hand

Submitted by Kerby Saunders (Nat'l Sheet Metal Dwg.)


3 GA-1B-16 2 Oct '51 1st Smt. Duct Layout

(APPROVED AS NOTED 8 Nov 1951 VR RESUBMIT)

NOTE: FROM SYSKA & HENNESSY

"This drawing is approved, except as noted in yellow crayon."

"All approvals are subject to strict compliance with the Contract Plans and Specifications and to all Authorities having Jurisdiction."



*Hopper
Dealy*

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

October 29, 1951

To Gen. Fick

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

RE: HQ 1/82 Contract - General Assembly & North Parking Space
General Assembly - Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following ornamental metal shop drawings submitted by General Bronze Corporation and C. E. Halback & Company:

<u>NO.</u>	<u>DATE</u>	<u>TITLE</u>
GBA 41	10/25/51	Alum. Enclosure at Vestibule #2
GBA 42	10/25/51	F.S.D. Alum. Enclosure at Vestibule #2

Please note that these two drawings supersede drawings GBA-4, GBA-22, and GBA-23.

Will you please return two (2) prints each of the above drawings marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/lbr
Encl. - dwgs.



ISSUANCE OF DRAWINGS

OFFICE COPY

29 October 1951

14 November 1951


GA & North Parking
Fuller-Turner-Walsh-Slaterry

hand

Submitted by General Bronze & Halback

2 GBA-41 25Oct'51 Alum. Enclosure at Vestibule #2
(APPROVED AS NOTED 9 Nov 1951 VR RESUBMIT)

NOTE: Dwg. GBA-42 will follow

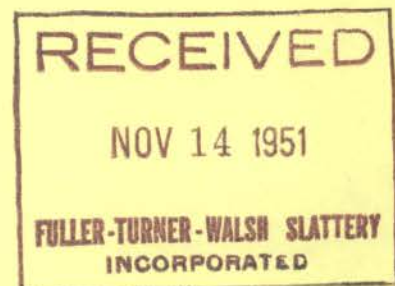

L. V. Tyler

ISSUANCE OF DRAWINGS

OFFICE COPY

29 October 1951


15 November 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by General Bronze & Halback

2 GBA-42 25Oct'51 F.S.D. Alum. Enclosure at Vestibule #2
(APPROVED AS NOTED 9 Nov 1951 REN RESUBMIT)

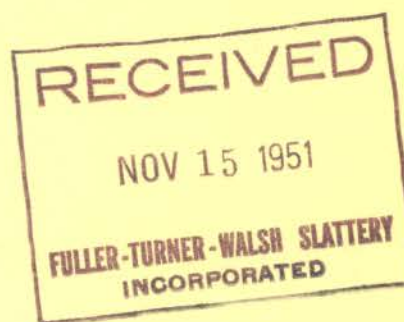

SV Tyler

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 29, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

RE: HQ 1/82 Contract - General Assembly & North Parking Space
Electric Shop Drawings

Dear Mr. Dawson:

We are submitting to you herewith six (6) prints of Trumbull Electric Company's dwg. ENY-150-33 - Dimmer Panels 4B, 4C, 4D and 4E, as forwarded to us by Fischbach & Moore, Inc.

Will you kindly review the above mentioned drawings and return three (3) copies with your comments and/or approval.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

CER/PIB/lbr
Encls. - dwgs.

C. E. Reese *CRB*
C. E. Reese
Project Engineer



ISSUANCE OF DRAWINGS

OFFICE COPY

29 October 1951

7 November 1951

GA & North Parking

Fuller-Turner-Walsh-Slaterry

hard


Submitted by Fischbach & Moore (Trumbull Elec. Dwg.)

3 ENY-150-33 17Oct'51 Dimmer Panelboards 4B, 4C, 4D and 4E
(APPROVED 5 Nov 1951 REN)

NOTE: FROM SYSKA & HENNESSY

"This drawing is approved."

"All approvals are subject to strict compliance with the Contract Plans and Specifications and to all Authorities having Jurisdiction."



SVI

120-5-18-9✓
cc: Harrison
McLeod
Zunser
Healy
Hopper
Van Name

29 October 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, N.Y.

Re: Contract HQ 1/82 - General Assembly and
North Parking Garage - Notification of
Change No. 66 (R. P. 52) - Furnish and
Install 3 Copper Expansion Joints in
Cement Plaster Soffit at South Porch

Gentlemen:

Attached hereto is one copy of Notification of Change No.
66 (R. P. 52) approved by James A. Dawson for the United Nations.

This approval is given for you to proceed with the work re-
quired by the modification with reference to furnishing and installing
3 copper expansion joints in cement plaster soffit at south porch.

It is understood that this approval does not include the
cost of this change as indicated in the Notification of Change No. 66,
which is solely an approximation. It is understood, also, that the
actual price adjustment will be made as required by the terms of the
contract.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

Enclosure
JZ:ml

120-3-18-7
29 October 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Miscellaneous Changes

Gentlemen:

On 25 October 1951 we forwarded you twenty-five (25) copies of each of the following documents:

Drawing A-2, Revision No. 45, dated 25 October 1951
Drawing A-5, Revision No. 45, dated 25 October 1951
Bulletin of Changes to Revision No. 45, dated 25 October 1951.

With reference to the items shown on the Bulletin of Changes, the following will cause a change to the Contract Price and you are to proceed as follows.

Item No. 2, Drawing A-2, perform the installation of the cinder block partitions, the cement base, the plaster work and painting, the installation of the doors and bucks and all hardware on a time and material basis, the daily time slips to be signed by the U.N. inspectors. Verbal instructions were given to you reference this matter on 26 October 1951.

Item No. 4, Drawing A-5, there will be a slight change caused by this item. Proceed with the work included therein and also with all of the remainder of the work shown in the rest of the items in the Bulletin of Changes.

Submit for our consideration prices on all of the above which will affect the Contract Price.

JJHe:js

cc: Bohanon Hopper
Nelson Zunser
Weigel VanName
Healy McLeod
Harris Ryer

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

26 October 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly
Portion of Parking Garage
Contract HQ 1/82 - Electrical
Conference Room No. 4 Ceiling

Gentlemen:

In confirmation of verbal advice given to
Mr. Arthur Schumer of Fischback & Moore, Inc. by our
Mr. Paul Bohanon this morning, we hereby advise you
that the cold cathode tubing above the eggcrate panels
in Conference Room No. 4 ceiling is to be of the
"Warm Tone" type, at no additional cost to the contract.

Very truly yours,

HBW:js
cc: Bohanon
Nelson
Weigel
Healy
Harris
Hopper
Zunser
VanName
McLeod
Hannegan
Seelman
S & H-2

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

Ⓢ

26 October 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Structural Steel and Concrete

Gentlemen:

On 23 October 1951 we forwarded you twenty-five (25) copies of Drawings Nos. GA-3-CS-32 dated 22 October 1951 and GA-3-CS-35 dated 19 October 1951. On 24 October 1951 we forwarded you twenty-five (25) copies of Drawing No. GA-2-CS-33C dated 23 October 1951.

Reference GA-3-CS-32 and GA-3-CS-35, there are no cost changes involved, these changes being only steel field changes. These drawings are for your records.

Reference GA-2-CS-33C, there will be a change in concrete thickness and wire mesh for one panel.

Proceed with the work shown on the above drawings and submit for our consideration prices which affect the Contract Price.



JJHe:js
cc: Bohanon
Nelson
Weigel
Healy
Harris
Hopper
Zunser
VanName
McLeod
Ryer

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

On files

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

October 25, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York 17, N.Y.

Re: CONTRACT HQ 1/82 - GENERAL ASSEMBLY AND NORTH PARKING SPACE
PARTIAL ESTIMATE #1 FOR CHANGE NO. 194
"Revisions to Electrical Work Originating
in the field"

References: a) PTTS Letter (Reese) to United Nations dated June 14, 1951
b) " " (Grogan) to United Nations dated June 15, 1951

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we claim an increase in our total guaranteed maximum cost price in the amount of THREE HUNDRED SIXTY TWO DOLLARS AND TWO CENTS (\$362.02) for the revisions in electrical work originating in the field as listed herein which are required by the above "references".

The above increase covers the costs indicated for the items listed below:

Item No. 1 - C.I.S. #7052 -

ADD

"Erect U. N. Engineers Field Office located in 1st basement-north parking Cols. L to N on 36 Line. To be built of 2 x 4 and homasote and to include necessary utilities."

Fischbach & Moore, Inc. (Invoice #15841A)..... \$ 362.02

TOTAL ADDITION-THIS PARTIAL ESTIMATE.. \$ 362.02

One copy of Fischbach & Moore's Invoice #15841A and two copies of each time ticket included therein are attached hereto. Other copies of these time slips are already in your files.

Will you kindly issue a Change Order-ADDITION in the amount of \$362.02 covering the items of work listed above.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan

M. J. Grogan
Project Manager

MJG:CER:amc
attach.

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file
October 25, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York 17, N.Y.

RE: CONTRACT HQ 1/82 - GENERAL ASSEMBLY AND NORTH PARKING SPACE
ESTIMATE FOR CHANGE NO. 152
"December 13, 1950 Structural Revisions"

References: a) FTWS, Inc. Notification of Change No. 41, dated 4/13/51
b) Mr. James A. Dawson's letter dated 4/19/51 to FTWS, Inc.
c) List of Drawings attached to Change No. 152
d) FTWS, Inc. letter (Grogan) to United Nations dated 5/14/51-
(C.O. #152).

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we claim an increase in our total guaranteed maximum cost price in the amount of SEVENTY FIVE DOLLARS AND EIGHTY FIVE CENTS (\$75.85) for the changes in the work itemized herein, which are required by the above "references".

This estimate is broken down as follows:

PART IV - SECTIONS 2, 3 & 4 - CONCRETE
(Brennan & Sloan, Inc.)

Examination of the drawings listed above indicates no change which will affect this contract. Several of these drawings have been incorporated in "S" drawings which are included in Change No. 132 issued on 4/4/51. Since proper charges will be made for the "S" drawings in the Estimate for Change No. 132 no charges can be considered in this Estimate. Following is a list of such drawings:

<u>U. N. Drawing "S" -</u>	<u>Reference Drawing of this</u> <u>Change Incorporated therein-</u>
S-55-C	(GA-WS-165C 164C 174C
S-56-C	(GA-WS-178C 173C
S-57-C	(GA-WS-166C 183C
S-58-C	GA-WS-182C

(continued on page 2)

Mr. James A. Dawson
Re: Contract HQ 1/82 - General Assembly & North Parking
Space - Estimate for Change No. 152

October 25, 1951
page (2)

PART IV - SECTIONS 5 & 6 - MASONRY WORK & METALS
(John B. Kelly, Inc.)

ADD

a) On Drawing GA-PS-S-11, add brick.

Interior Exposed Common brick - 530 @ \$124.50/M.....	\$ 65.99
15% O & P	9.86

TOTAL ADDITION - THIS ESTIMATE... \$ 75.85

Will you kindly issue a Change Order-ADDITION in the amount of \$75.85 to cover the costs itemized herein.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan
Project Manager

MJG:CER:amc

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 25, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

Re: HQ 1/82 Contract - General Assembly and
North Parking Space -
Brennan & Sloan, Inc. and Knickerbocker
Construction Corporation

Dear Mr. Dawson:

Our subcontractor for the concrete work and cement finish, Brennan & Sloan, Inc. and Knickerbocker Construction Corporation, find that because of the fact that they have contracts for this work in force at present on both the Meeting Halls and General Assembly the cash reserve has mounted so high that they find it necessary to ask for relief by means of an interim payment of part of the reserve.

The present reserve on the General Assembly account amounts to \$142,369.12. In view of the fact that their work is 82% complete, and our general contract work is over 51% complete, may we have your approval to submit a requisition for payment of half of this reserve, thus reducing it from 10% to 5%.

We have attached, for your information, copy of Brennan & Sloan, Inc. and Knickerbocker Construction Corporation's letter dated October 23, 1951 requesting the favor of this payment.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/lbr
Enclosure



BRENNAN & SLOAN, INCORPORATED
AND
KNICKERBOCKER CONSTRUCTION CORPORATION

403 EAST 42ND STREET
NEW YORK 17, N. Y.

October 23, 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly

Gentlemen:

As of October 15, 1951 there has accumulated on the United Nations Headquarters retained percentages aggregating over \$250,000.00 which amount is exclusive of large sums which we have been expending on extra work for which we have not yet been reimbursed.

On the General Assembly account the retained percentage amounts to \$142,369.12. In view of the fact that this job is 80% complete we request that the retained percentage be reduced from 10% to 5% and that payment of the difference be made to us at this time.

Yours very truly,

BRENNAN & SLOAN, INCORPORATED AND
KNICKERBOCKER CONSTRUCTION CORPORATION
A JOINT VENTURE,

F. P. Sloan

*Stopper
Healy*

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Mr. Wigel

October 25, 1951

To Mr. Fick

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Hall
Parking Space (GA)
Cut Stone

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following Cut Stone shop drawing submitted by Monahan-McCann Stone Company:

5 EZ Dtd. 10/23/51 East Wall - Between Cols.
25 - 27.

Will you please return two (2) prints of the above drawing marked with your approval or necessary corrections?


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/NH/em

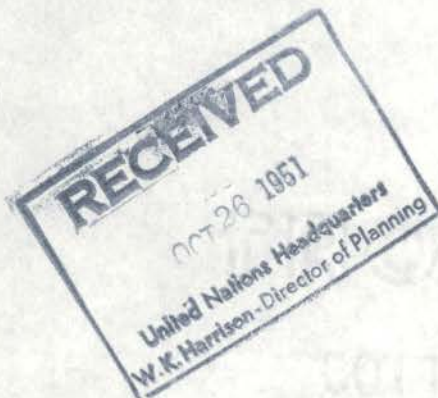

FULLER - TURNER - WALSH - SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 25, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York 17, N.Y.

file

RE: CONTRACT HQ 1/82 - GENERAL ASSEMBLY AND NORTH PARKING SPACE
PARTIAL ESTIMATE #1 FOR CHANGE NOS. 204 & 204A
"Revisions to Work of Architectural Trades
Originating in the Field"

References: a) ^{FTWS.} ~~United Nations~~ Letter (^{REESE} ~~Dawson~~) to FTWS dated June 14, 1951
b) FTWS Letter (Grogan) to United Nations dated June 15, 1951
c) United Nations Letter (~~Dawson~~) to FTWS dated Sept. 20, 1951
d) FTWS Letter (~~Grogan~~) to United Nations dated Oct. 4, 1951

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82 we claim an increase in our total guaranteed maximum cost price in the amount of EIGHT HUNDRED SIXTY NINE DOLLARS AND FIFTY ONE CENTS (\$869.51) for the revisions to work of architectural trades originating in the field, as listed herein which are required by the above "references".

The above increase covers the costs indicated for the items listed below:

Item No. 1 - C.I.S. #7052 -ADD

"Erect U. N. Engineers Field Office located in 1st basement-North Parking Cols. L to N on 36 Line. To be built of 2 x 4 and homasote and to include necessary utilities."

FTWS, Inc. - D.W.R. No. 014568.....	\$132.85	
" " " " 014569.....	137.42	
" " " " 014570.....	69.72	75.45
" " " " 014571.....	35.48	
Total Addition - This Item.....	\$375.47	\$ 375.47 381.20

Item No. 2 - C.I.S. #7054 - P.O. #2 & #3:

"Cut cinder block partition and erect H.M. Buck and door in partition between Space 1B57 and Space 1B59. Buck and Door to be taken from U. N. surplus stock of Secretariat (23rd floor).

Hardware: Latch and 1 1/4 pr. butts to be furnished by U. N. from surplus stock. All Labor and material to be signed for as work progresses."

J. B. Kelly, Inc. (Invoice dated 5/15/51).....	\$48.85	
Atlantic Metal Products, Inc. (Invoice #3949)....	19.55	
Total Addition - This Item.....	\$68.40	\$ 68.40
Figures carried forward to page (2).....		\$ 143.87

Mr. James A. Dawson
Re: Contract HQ 1/82 - General Assembly & North Parking
Space - Partial Estimate #1 for Change Nos. 204 & 204A

October 25, 1951
Page (2)

Figures brought forward from page (1).....\$ ^{ADD} 443.87

Item No. 3 - C.I.S. #7059 - F.O. #5:

"At east end of brick wall 1st basement on 32A Line
tear down cracked portion and replace. Point up
horizontal crack from east end to Col. Q' 32A. This
work to be done on T/M basis. At approximately 4'-0"
from East Podium Wall change location of brick wall by
4" as shown."

J. B. Kelly, Inc. (Invoice dated 6/27/51).....\$48.56.... \$ 48.56

Item No. 4 - C.I.S. #7060 - F.O. #7:

in
"On the 1st basement/Corridor 1B64 install trench
cover and frame 3'-0" north of Col. 24 instead of
2'-0" north of 24. Do the necessary cutting and
welding of frame and plate to make this change on
a T/M basis."

General Bronze Corp. (Invoice dated 8/9/51).....\$31.01.... \$ 31.01

Item No. 5 - C.I.S. #7061 - F.O. #9:

"Build a 3" block wall in sound lock near Col. O' 25
on 1st basement as shown on sketch below. This work
to be done on a T/M basis."

J. B. Kelly, Inc. (Invoice dated 7/23/51).....\$29.26.... \$ 29.26

Item No. 6 - C.I.S. #7063 - F.O. #10:

"Furr out with 3" cinder block around duct in South West
corner of Lounge 2B2 and move North wall of Locker Room
2B4 to 24'-4" South of 28 Line.

J. B. Kelly, Inc. (Invoice dated 7/26/51).....\$18.36

" " " (" " 8/2/51).....108.75

Total Addition - This Item.....\$127.11.... \$ 127.11

Item No. 7 - C.I.S. #7065 - F.O. #14 & #15:

"Install door, buck and hardware (supply by U.N.) about
10'-0" north of O' 21 in westmost duct wall in existing
opening. (Betw. Cols. 21 & 22-3rd basement level). Also
door, buck and hardware from attic stock between Cols.
35 and 36 on F Line from Snow Melting Room to Duct Space
(1st basement)."

Atlantic Metal Products, Inc. (Invoice #4306).....\$77.50

J. B. Kelly, Inc. (Invoice dated 9/14/51).....\$76.32

Total Addition - This Item.....\$153.82.... \$ 153.82

Figures carried forward to page (3).....\$ 833.63

Mr. James A. Dawson
Re: Contract HQ 1/82 - General Assembly & North Parking
Space - Partial Estimate #1 for Change Nos. 204 & 204A

October 25, 1951
page (3)

Figures brought forward from page (2) \$ ^{ADD} 833.63

Item No. 8 - C.I.S. #7069 - F.O. #22:

"Paint Room No. 1B65A same as 1B65."

Shatz Painting Co.:-

Paqua finish - 416 SF @ \$.07½/sf. \$31.20

15% O & P. \$ 4.68

Total Addition - This Item. \$ 35.88


TOTAL ADDITION - THIS PARTIAL ESTIMATE.... \$ 869.51

Attached hereto is one copy each of all invoices included in this estimate and one copy each of all daily work reports covering work by FTWS, Inc. which is included in this estimate. One copy of all subcontractors time and material tickets is already in your file.

Will you kindly issue a Change Order-ADDITION in the amount of \$869.51 to cover the items of work listed above.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan
Project Manager

MJG:CER:amc
attach.

ISSUANCE OF DRAWINGS

OFFICE COPY

25 October 1951


31 October 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Monahan McCann

2 5-EZ 23Oct'51 East Wall - Between Cols. 25 - 27
(APPROVED AS NOTED 31 Oct 1951 PB RESUBMIT)



SV Dyer

25 October 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York


Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Heating, Ventilating, Air Conditioning
Revision to Ductwork, 2nd Basement
Maintenance Area

Gentlemen:

On 25 October 1951 we forwarded you twenty-one (21) copies of Drawing SK-GA-H1-6, the revisions to the ductwork in the Maintenance Area in the 2nd Basement.

Proceed with the work shown thereon and submit for our consideration prices which affect the Contract Price.

The costs of this change should be included in the same change under which the costs of Revision No. 45 shall be included.

 JJHe:js
cc: Bohanon
Nelson
Weigel
Healy
Harris
Hopper
Zunser
VanName
McLeod
Hannegan
Rumpelstin
S & H-2
Ryer

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

22 October 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly
Portion of Parking Garage
Contract HQ 1/82 - Concrete and
Miscellaneous Metal
Dome Catwalk Inserts

Gentlemen:

On 16 October 1951 we forwarded you ten (10) copies of
Drawing SK-680 dated 16 October 1951, the location drawing
of the inserts for the catwalks in the dome.

Proceed with the purchasing and installing of the inserts
as shown on this drawing and furnish for our consideration
the prices which affect the Contract Price.

Very truly yours,

JJHe:js
cc: Bohanon
Nelson
Weigel
Healy
Harris
Hopper
Zunser
VanName
McLeod
Ryer

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 313 - Structural Revisions

- References (a) GA-2-CS-30, dated 10/16/51, Extension of Lintel 2-L-10
@ 2nd Floor
(b) GA-5-CS-18c, issued 10/19/51, Alternate Reinforcing for
6" Penthouse Walls
(c) GA-5-CS-19c, issued 10/19/51, Added Access Opening in
Cone Wall
(d) GA-5-CS-17c, issued 10/19/51, North Facade Column Re-
inforcing at Bond Stones

Dear Mr. Dawson:

On October 22, 1951 we received prints of References (a) to (d) inclusive.

On October 22, 1951 we received your transmittal form covering these drawings, which advised us to "Proceed with the work."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/en

FULLER - TURNER - WALSH - SLATTERY, INC.
 UNITED NATIONS CONTRACT
 403 EAST 42ND STREET
 NEW YORK 17, N. Y.

file

Mr. James A. Dawson
 Co-Ordinator of Construction
 Headquarters Planning Office
 Room 2272 - United Nations
 New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Garage -
 CHANGE NO. 311 - Changes of Columns under the East and West Ramps of
 the General Assembly

References: (a) U.N.Dwg. DSK-429 - Balcony Column Details - dated 8/20/51
 (b) " " DSK-430 - " " " "
 (c) " " DSK-432 - Exterior Balcony Pier - dated 9/12/51
 (d) " " DSK-433 - " " " "
 (e) FTWS, Inc. Notification of Change No. 73, dated 10/4/51
 (f) Mr. James A. Dawson's letter 15 October 1951 to FTWS, Inc.

Dear Mr. Dawson:

On September 18, 1951 we received copies of References (a) thru (d), inclusive with a request for price for the revisions shown on these drawings.

On October 4, 1951 we sent you our Notification of Change No. 73, Reference (e), which gave an approximation of the additional cost involved. This estimate was based on the following:

- a) Aluminum column covering was based on the use of aluminum sheets and stock channels, rather than extruded sections.
- b) The Portland Stone required for the Balcony Pier, shown on DSK-432 and 433 is to be 4" thick, except for the cap base which is to be 8" thick.
- c) The Granite base shown on the drawings is to be Norwegian Silver Granite with a coarse steel finish.
- d) The inclusion of suitable anchorage devices to anchor the sculpture to be provided in the future on the Balcony Pier.

On October 22, 1951 we received your letter of approval, Reference (f), authorizing us to proceed with the work as shown on these drawings.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,
 FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
 M. J. Grogan
 Project Manager

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Garage -
CHANGE NO. 310 - Changes in Rolling Steel Doors at Meeting Halls Neck

References: (a) FTWS, Inc. letter 1 October 1951
(b) J.G. Wilson Corp. Shop Drawing 89840-7, revised 3/27/51
(c) Mr. James A. Dawson's letter 17 October 1951 to FTWS, Inc.

Dear Mr. Dawson:

In our letter of October 1, 1951, Reference (a) we advised you of certain changes which are necessary at the Three (3) Rolling Steel Shutters between the General Assembly Building and the Meeting Halls.

In Reference (c) you advised us to proceed as follows:

"In your letter to use of 1 October 1951 you requested our advice reference proceeding with the following modifications:

Refer to J.G. Wilson Corp. shop drawing No. 89840-7, revised 27 March 1951, details of the Rolling Shutter Doors between the Meeting Hall Neck and the General Assembly.

- a. On Detail "X" of this drawing, two 3" x 3-1/2" x 5/16" angles at the head are shown. They cannot be installed because of space limitations. Further, the slats of the door will catch in the angle when the door is lowered.

Answer: Omit these angles.

- b. In the Plan View at the gear box recess, a 3-1/2" x 3-1/2" angle, which is supposed to run from slab to slab, is shown. However the head of the door does not allow this angle to run to the slab above, and your representatives have instructed us to omit the angle and substitute two (2) inch block furring.

Answer: Proceed as instructed.

- c. Your field inspector has also requested that we provide some means of lubricating the grease cup at the top of the crankshaft.

Answer: Install a tube or pipe so that the grease cup will be accessible from the access door.

Continued

Mr. James A. Dawson

-2-

October 24, 1951


re: Contract HQ 1/82 - CHANGE NO. 310

"Submit for our consideration prices which affect the Contract Price."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan
Project Manager

MJG/PDV/eas

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Garage -
CHANGE NO. 297-a - Omission of Woven Wire Mesh Screens at Roof Gratings

References: (a) FTWS, Inc. Notification of Change #72, dated 10/3/51
(b) Mr. James A. Dawson's letter 10 October 1951 to FTWS, Inc.

Dear Mr. Dawson:

This Change is supplemental to our Change No. 297, dated October 10, 1951.

On October 3, 1951 we sent you our Notification of Change No. 72 which gave an approximation of the credit involved in deleting the wire mesh guard screens at the roof well gradings as described in our Change No. 297.

On October 15, 1951 we received your letter of approval, Reference (b), which authorized us to proceed with the deletion of these items.

Our Estimate for Change No. 297 will be based on this deletion.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/sas

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 296 - September 28, 1951 - Architectural Revision No. 41

References (a) **List** of Drawings & Bulletin included in the Attachment.
(b) Mr. James A. Dawson's letter of October 3, 1951.

Dear Mr. Dawson:

On October 1, 1951 we received prints of the drawings and Bulletin included in Reference (a).

On October 4, 1951 we received your transmittal letter, Reference (b) which reads, in part, as follows:

"Proceed with the work indicated on the above listed documents and submit for our consideration the prices which affect the Contract Price."

As instructed by your letter of October 10, 1951 we will exclude any costs in connection with the circular loudspeaker frames from this Change and include these costs in our Estimate for Change No. 261.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

HJG/PDV/cn

LIST OF DRAWINGS AND BULLETIN
INCLUDED IN ARCHITECTURAL REV. NO. 41
CHANGE 296

<u>Drawing No.</u>	<u>Rev. No.</u>	<u>Date</u>
RA-106B	41	9/28/51
A-121	41	"
A-125	41	"
RA-145	41	"
RA-170	41	"
RA-171	41	"
RA-172	41	"
RA-173	41	"

Bulletin of Changes, Rev. No. 41, dated September 28, 1951.

FULLER - TURNER - WALSH - SLATTERY, INC.
 UNITED NATIONS CONTRACT
 403 EAST 42ND STREET
 NEW YORK 17, N. Y.

file

October 24, 1951

Mr. James A. Dawson
 Co-Ordinator of Construction
 Headquarters Planning Office
 Room 2272 - United Nations
 New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 261A - August 8, 1951 - Architectural Revision No. 37

Reference (a) Mr. James A. Dawson's letter of October 10, 1951.

Dear Mr. Dawson:

This Change is supplemental to our Change No. 261, dated August 22, 1951.

The above-referenced letter recapitulated the total requirements for circular loudspeaker frames, as follows:

1st Basement	5	Drawing RA-170	Rev. No. 29
1st Floor	10	" RA-172	Rev. No. 29
2nd Floor	13	" RA-173	Dated 9/28/51
3rd Floor	2	" RA-174	Dated 8/23/51
1st Floor Lobby Walls	2	" RA-126	Rev. No. 43
Total	32		

The above letter requests that we include all thirty-two (32) of the added frames in our Estimate for Change No. 261.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
 M. J. Grogan
 Project Manager

HJG/PDV/em

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

RE: HQ 1/82 Contract - General Assembly & North Parking Space
ESTIMATE FOR CHANGE NO. 248
July 25, 1951 Structural Revisions

References:

- (a) U.N. Dwg. GA-4-CS-26, Issued July 23, 1951
- (b) Mr. James A. Dawson's letter of July 23, 1951
- (c) FTWS, Inc. letter (Grogan) to U.N. dated 8/9/51 (C.O.248)

Dear Sir:

Please be advised that there will be no change in our total guaranteed maximum cost price for our Contract HQ 1/82 due to changes required by references (a) to (c) noted above.

Will you kindly acknowledge receipt of and acceptance of this estimate.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan

M. J. Grogan
Project Manager

MJG/CER/lbr

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

RE: HQ 1/82 Contract - General Assembly & North Parking Garage
ESTIMATE FOR CHANGE NO. 229
Added Holes in 3rd Floor Beams

References:

- (a) U.N. Dwg. GA-2-CS-22, dated June 29, 1951
- (b) Mr. James A. Dawson's letter 3 July 1951 to FTWS, Inc.
- (c) FTWS, Inc. letter (Grogan) to U.N. dated 7/16/51 (C.O.229)

Dear Sir:

Please be advised that there will be no change in our total guaranteed maximum cost price for our Contract HQ 1/82 due to changes required by references (a) to (c) noted above.

Will you kindly acknowledge receipt of and acceptance of this estimate.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/CER/lbr

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

RE: HQ 1/82 Contract - General Assembly & North Parking Space
ESTIMATE FOR CHANGE NO. 206
June 14, 1951 Structural Revisions

References:

- (a) U.N.Dwg. GA-4-CS-24, issued 6/13/51
- (b) Mr. James A. Dawson's letter of June 15, 1951
- (c) FTWS, Inc. letter (Grogan) to U.N. dated 6/19/51 (C.O.206)

Dear Sir:

Please be advised that there will be no change in our total guaranteed maximum cost price for our Contract HQ 1/82 due to changes required by references (a) to (c) noted above.

Will you kindly acknowledge receipt of and acceptance of this estimate.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan

M. J. Grogan
Project Manager

MJG/CER/lbr

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

RE: HQ 1/82 Contract - General Assembly & North Parking Garage
ESTIMATE FOR CHANGE NO. 195
June 4, 1951 Structural Revision

References:

- (a) U.N.Dwg. GA-4-CS-22, issued June 1, 1951
- (b) Mr. James A. Dawson's letter of June 5, 1951
- (c) FTWS, Inc. letter (Grogan) to U.N. dated 6/19/51 (C.O.195)

Dear Sir:

Please be advised that there will be no change in our total guaranteed maximum cost price for our Contract HQ 1/82 due to changes required by references (a) to (c) noted above.

Will you kindly acknowledge receipt of and acceptance of this estimate.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/CER/lbr

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

RE: Contract HQ 1/82 - General Assembly & North Parking Space
ESTIMATE FOR CHANGE NO. 183
May 25, 1951 Structural Revisions

References:

- (a) U.N. Dwg. GA-4-CS-19, Rev. No.1, dated 5/24/51
- (b) " " GA-4-CS-20, " " " " "
- (c) " " GA-PS-CS-19, dated May 18, 1951
- (d) " " GA-PS-CS-20, " May 24, 1951
- (e) Mr. James A. Dawson's letter 25 May 1951
- (f) FTWS, Inc. letter (Grogan) to U.N. dated 6/4/51 (C.O.183)

Dear Sir:

Please be advised that there will be no change in our total guaranteed maximum cost price for our Contract HQ 1/82 due to changes required by references (a) to (f) noted above.

Will you kindly acknowledge receipt of and acceptance of this estimate.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan

M. J. Grogan
Project Manager

MJG/CER/lbr

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

RE: Contract HQ 1/82 - General Assembly & North Parking Space
ESTIMATE FOR CHANGE NO. 180
May 23, 1951 Structural Revisions

References:

- (a) U.N. Dwg. GA-4-CS-19 dated May 21, 1951
- (b) " " GA-4-CS-20 " May 22, 1951
- (c) Mr. James A. Dawson's letter 25 May 1951 to FTWS, Inc.
- (d) FTWS, Inc. letter (Grogan) to U.N. dated 6/4/51 (C.O.180)

Dear Sir:

Please be advised that there will be no change in our total guaranteed maximum cost price for our Contract HQ 1/82 due to changes required by references (a) to (d) noted above.

Will you kindly acknowledge receipt of and acceptance of this estimate.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan

M. J. Grogan
Project Manager

MJG/CER/lbr

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, N. Y.

RE: HQ 1/82 Contract - General Assembly & North Parking Space
ESTIMATE FOR CHANGE NO. 166
Booth Wall Structural Details

References:

- (a) U.N. Dwg. GA-WS-187B, Rev.No.1, dated 5/3/51
- (b) " " GA-WS-187C, issued 5/4/51
- (c) Mr. James A. Dawson's letter of 10 May 1951
- (d) FTWS, Inc. letter (Grogan) to U.N. dated 5/15/51 (C.O.166)


Dear Sir:

Please be advised that there will be no change in our total guaranteed maximum cost price for our Contract HQ 1/82 due to changes required by references (a) to (d) noted above.

Will you kindly acknowledge receipt of and acceptance of this estimate.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan
Project Manager

MJG/CER/lbr

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

RE: Contract HQ 1/82 - General Assembly & North Parking Garage
ESTIMATE FOR CHANGE NO. 165
May 3, 1951 Structural Revisions

References:

- (a) U.N. Dwg. GA-2-CS-20 dated 4/30/51, Rec'd. 5/3/51
- (b) " " GA-3-CS-22 " " " "
- (c) " " GA-3-CS-23 " " " "
- (d) " " GA-2-CS-20, revised 5/4/51, Rec'd. 5/8/51
- (e) " " GA-3-CS-24, dated 5/7/51, Rec'd. 5/10/51
- (f) " " GA-WS-223, issued 5/4/51, Rec'd. 5/7/51
- (g) " " GA-S-31, Rev. No. 2, 5/3/51, " "
- (h) " " GA-S-37, " " 3, " " "
- (i) Mr. James A. Dawson's letter of 10 May 1951
- (j) FTWS, Inc. letter (Grogan) to U.N. dated 5/15/51 (C.O. 165)

Dear Sir:

Please be advised that there will be no change in our total guaranteed maximum cost price for our Contract HQ 1/82 due to changes required by references (a) to (j) noted above.

Will you kindly acknowledge receipt of and acceptance of this estimate.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/CER/lbr

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

RE: Contract HQ 1/82 - General Assembly & North Parking Space
ESTIMATE FOR CHANGE NO. 154
April 19, 1951 Structural Revisions

References:

- (a) U.N.Dwg. GA-CS-B7, issued 4/20/51
- (b) " " GA-CS-B8, " 4/19/51
- (c) " " GA-3-CS-21, dated 4/19/51
- (d) " " GA-PS-CS-16 issued 4/19/51
- (e) Mr. James A. Dawson's letter dated 4/24/51
- (f) FTWS, Inc. letter (Grogan) to U.N. dated 4/27/51 (C.O.154)

Dear Sir:

Please be advised that there will be no change in our total guaranteed maximum cost price for our Contract HQ 1/82 due to changes required by references (a) to (f) noted above.

Will you kindly acknowledge receipt of and acceptance of this estimate.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan
Project Manager

MJG/CER/lbr

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General
Assembly and North Parking
Garage -
Release of Information for
Construction Purposes

Dear Mr. Dawson:

On Friday, October 19, 1951 a meeting was held in your Conference Room to discuss the release of "HOLDS" for various items on the General Assembly drawings so that the work could progress without delay. Those present at the meeting were:

Messrs. Dawson	}	United Nations
Zunser		
Harris		
Grogan	}	FTWS, Inc.
Bartley		
Reese		

The items discussed and the decisions reached were as follows:

1) CHANGES IN NORTH LOBBY:

This discussion mainly involved the omission of the hung ceiling, the addition of cat-walks, changes in lighting and possible changes in duct work due to added wattage of lights. The changes are shown on UN Dwgs. DSK-442, to 446, inclusive. These drawings are included in our Request for Price #65. To date we have not been able to prepare a Notification of Change due to uncertainties with regard to the electrical work.

Mr. Harris stated that the decision regarding the electrical work depended upon the mock-up of lighting to be made in the South Lobby. He requested that the Notification of Change be submitted with a notation that it did not include the cost of any revisions in electrical work or in ventilating work resulting therefrom.

Mr. Dawson instructed us to proceed at once with the fabrication of the duct work for this ceiling in accordance with the layout shown on drawing DSK-442. This layout, with possible small modifications, will work whether the hung ceiling is retained or omitted.

2) CHANGES IN SOUTH LOBBY:

The problems here are somewhat similar to those of the North Lobby. After discussion Mr. Dawson instructed us to proceed at once with the work in the

October 24, 1951

re: Contract HQ 1/82 - Release of Information for Construction Purposes -

South Lobby, disregarding the design sketches for the omission of the hung ceiling and using the latest revisions of architectural, mechanical and electrical drawings which show the hung ceiling. He also advised us that the cement plaster soffit of the South Porch is to be installed and that we are to provide copper expansion joints in it, as contemplated by our Notification of Change No. 66. This decision cancels our Request for Price No. 60.

3) TREATMENT OF DOME CEILING:

The United Nations had advised us that they were contemplating removing the hung ceiling under the dome. No drawings have been issued to us except an insert plan for three circular catwalks which will be required if the ceiling is omitted.

Mr. Harris informed us, at the meeting, that the United Nations has not reached a decision on this matter. Mr. Dawson instructed us to install the inserts for the catwalks in accordance with the plan we now have. A decision regarding the treatment of the ceiling will be given at a later date.

4) CHANGES IN DOME DRUM:

The United Nations had advised us that they were considering omitting the standing seam, copper sheathing on the conical portion and cupola of the Dome, and adding a 1" hydrolethic parge coat and terra cotta.

Mr. Dawson instructed us at the meeting to forget this revision and to proceed with the copper sheathing. This decision will cancel our Request for Price No. 55.

5) REVISIONS TO RAMP COLUMNS: as covered by our Notification of Change No. 73, dated October 4, 1951 (Change No. 311).

Mr. Zumser advised us that this Notification of Change has been approved and is awaiting Mr. Harrison's signature. We may proceed.

The following items were discussed briefly but no decisions were made regarding them.

6) OMISSION OR RETENTION OF HUNG CEILING IN NORTH LOBBY:

This depends on Notification of Change to be submitted (See Item #1 above.)

7) OMISSION OR RETENTION OF HUNG CEILING UNDER THE DOME: (No drawings have been issued to us for this possible revision). (See also Item #3 above).

Mr. James A. Dawson

-3-

October 24, 1951

re: Contract HQ 1/82 - Release of Information for Construction Purposes.

8) SEVEN DOORS AT CANOPY NO. 2:

On July 23, 1951 you authorized us to proceed with the application of hammered aluminum panels to the existing doors (Change No. 243). On August 7, 1951 we stopped all work on these doors at your request. We understand that new nickel doors may be supplied by the Canadian Government.

9) STAIR NO. 28:

On May 28, 1951 you advised us that we might proceed with the form work for Stair #28, but that no concrete was to be poured until the form work had been inspected, for a possible design change. (Mr. Reese will settle this matter with Mr. Healy.)

- 10) SELECTION OF MARBLE for Screen in the 1st Floor Lobby. A decision on this matter was held in abeyance pending the selection of the finish of the 1st Floor Lobby. Subsequently we were informed that a gray and white Terrazzo floor pattern was to be used, but we have not yet had a decision on the marble screen.

11) CATWALK LAYOUTS:

We have your Drawing RA-9 which shows a schematic payout for the catwalks over the north half of the Assembly Hall, and your Dwg. DSK-443 which shows a schematic layout for those over the North Lobby. The Catwalk layout shown on DSK-436 at the South Lobby will probably have to be revised because of the retention of the hung ceiling. We have no construction details for any of the above drawings, and no layouts for the balance of the catwalk system in the building.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese.

C. E. Reese
Project Engineer

CER/eas

120-5-18-9
OREGON 9-3950

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Mr. Weigel
4

8
9/2

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Cut Stone-Anchor Samples

Dear Mr. Dawson:

We are sending you herewith for approval three (3) samples each of the following stone anchors submitted by Monahan-McCann Stone Co., and supplied by Republic Stone Corp.:

3/16" x 3" Slot Anchor Galvanized
3/16" x 3" Anchor Clip Galvanized
3/16" x 8" Cramp Anchor Galvanized
5/8" x 2-3/4" Lag Screw and Shield
1 1/16" O.D. (approx.) x 4" Brass Pipe Dowels.

These anchors and dowels are to be used for securing the stone work for the North Parking Space as shown on Monahan-McCann Stone Company's shop drawings Nos. 20. 21. 22 and 23, all prepared by Republic Stone Corp.

Please return two (2) samples of each type of the above anchors marked with your approval and/or comments.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/BK/em



FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following
Miscellaneous Iron shop drawings submitted by General Bronze
Corp. and C. E. Halback & Company:

HGP-14-1	Dtd. 8/26/51	Miscellaneous Pipe Railings
HGP-14-2	Dtd. 9/28/51	Miscellaneous Pipe Wall Rails
HGP-14-3	Dtd. 10/23/51	Scale Plans - Stair #24, #29, #30, #31 and #32
HGP-105-1	Rev. 10/22/51	Circular Steel Skylight at Cols. 32-J.

Will you please return two (2) prints each of the above draw-
ings marked with your approval or necessary corrections?

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Electric Shop Drawing

Dear Mr. Dawson:

We are forwarding to you herewith six (6) prints of Cole drawing H-1169, Rev. 2, showing audio duct layout, as submitted by Fischbach & Moore, Inc.


Kindly review the above drawing and return three (3) copies with your final approval.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese *per*
C. E. Reese
Project Engineer

CER/PLB/em



ISSUANCE OF DRAWINGS

OFFICE COPY

24 October 1951

20 November 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand


Submitted by Fischbach & Moore (Cole Elec. Dwg.)

3 H-1169 4 Jan '51 Audio Duct Layout
(APPROVED AS NOTED 7 Nov 1951 VR RESUBMIT)

NOTE: FROM SYSKA & HENNESSY

"This drawing is approved."

"All approvals are subject to strict compliance with the Contract Plans and Specifications and to all Authorities having Jurisdiction."



SV Tyler

170-5-18-9
OREGON 9-3950

*Happen
Healy*

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Wingell

October 24, 1951

To Gen. Fick

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Acoustical Treatment

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following
Acoustical Treatment shop drawing submitted by Johns-Manville
Sales Corporation:

103 Rev. 10/19/51 Reflected Ceiling Plans -
Booths & Passages - 1st
Basement.

Will you please return two (2) prints of the above drawing
marked with your approval or necessary corrections?

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

RECEIVED
OCT 24 1951
United Nations Headquarters
W.K. Harrison - Director of Planning

RECEIVED
OCT 24 1951
Headquarters Planning
Office

ISSUANCE OF DRAWINGS

OFFICE COPY

24 October 1951

26 October 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Johns-Manville

2	103	20Mar'51	Reflected Ceiling Plan - Booths & Passages, 1st Bmt. (APPROVED AS NOTED 26 Oct 1951 RHN RESUBMIT)
---	-----	----------	--



FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

*Final Approved
Gen Files
10/25
LWS*

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Acoustical Treatment

Dear Mr. Dawson:

We are sending you herewith, for your information, one
(1) print of the following Acoustical Treatment shop
drawing as approved for field distribution:

100-A Rev. 10/19/51 Miscellaneous Details - Studios,
Committee Rooms & Testing Room.

(Johns-Manville Sales Corp., Subcontractor)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C.E. Reese

C. E. Reese
Project Engineer

CER/MH/em



COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Acoustical Treatment

Dear Mr. Dawson:

We are sending you herewith, for your information, one
(1) print of the following Acoustical Treatment shop
drawing as approved for field distribution:

100-A Rev. 10/19/51 Miscellaneous Details - Studios,
Committee Rooms & Testing Room.

(Johns-Manville Sales Corp., Subcontractor)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Acoustical Treatment

Dear Mr. Dawson:

We are sending you herewith, for your information, one
(1) print of the following Acoustical Treatment shop
drawing as approved for field distribution:

100-A Rev. 10/19/51 Miscellaneous Details - Studios,
Committee Rooms & Testing Room.

(Johns-Manville Sales Corp., Subcontractor)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

October 24, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/52 - General
Assembly and North Half
Parking Space (GA)
Acoustical Treatment

Dear Mr. Dawson:

We are sending you herewith, for your information, one
(1) print of the following Acoustical Treatment shop
drawing as approved for field distribution:

100-A Rev. 10/19/51 Miscellaneous Details - Studios,
Committee Rooms & Testing Room.

(Johns-Manville Sales Corp., Subcontractor)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

120-5-18-9

24 October 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Electric - Special Fixtures at Stair
#36 - First Floor


Gentlemen:

On 24 September 1951 we forwarded you twenty-one (21) prints of Drawing SK-GA-E-3L-5 dated 19 September 1951, the lighting layout around Stair #36.

You will note there is no change in the number of outlets but there is a change in the fixture types. Due to the fact that there was not enough space under the escalator for the #932 Century fixture, originally specified and designated as No. 103, these eight fixtures were changed to #38 and #38B, 150 watt and 200 watt respectively. Since the issuing of these prints the lamp size of fixture Type #38B has been changed to 150 watt lamps.

Twelve fixtures, six on each side of the escalator, were changed to Wendel type #105, 150 watt, in lieu of twelve #932 Century fixtures. Two type #103, i.e. Century #932, were retained.

Proceed with the work indicated on Drawing SK-GA-E-3L-5 and submit for our consideration the prices which may affect the Contract Price.

 JJHe:js
cc: Bohanon
Nelson
Weigel
Healy
Harris
Hopper
Zunser
VanName
McLeod
Hannegan
Seelman
S & H-2

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

120-5-18-7
cc: Zunser
Hopper
Harris
Healy
Walther (M-H)

24 October 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, N.Y.

Re: Contract HQ 1/82 - General Assembly and
North Parking Space - Concrete Construction

Gentlemen:

Attached, for your information and guidance, is a copy of letter received from Madigan-Hyland, dated 24 October 1951, stating that they have restudied the pouring procedure desired by the contractor and have come to the conclusion that this method may be followed, although they would have preferred the sequence suggested in their letter of 17 October 1951, copy of which was forwarded to you under date of 19 October 1951.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

Enclosure
JZ:ml

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 23, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 500B - Additional Costs Involved in Early Occupancy of
the North Parking Space and General Assembly

Reference (a) Mr. James A. Dawson's letter of October 15, 1951

Dear Mr. Dawson:

This change is supplemental to our Change No. 500, dated June 14, 1951, and our Change No. 500-A, dated October 1, 1951.

On October 16, 1951 we received the above referenced letter which enclosed a copy of your Buildings Management Service Work Order, dated October 4, 1951, covering Item No. 3, in this Change Order.

This item covers the provision of temporary lighting in the area adjacent to Ramp No. 5 from 5:00 P. M. to 8:00 P. M. daily, starting October 8, 1951 and continuing for two weeks.

We will take these costs into account in preparing our Estimate for Change No. 500.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

LJG/PDV/em

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 23, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Garage -
CHANGE NO. 307 - Deletion of Temperature Terminal Boxes in the
Elevator Machine Rooms

Reference (a): Mr. James A. Dawson's letter 17 October 1951 to FTWS, Inc.

Dear Mr. Dawson:

On October 19, 1951 you advised us to proceed with the following change:

- " a. Omit two (2) Temperature Terminal Boxes, wiring, and conduit in each of the two Elevator Machine Rooms at the north end of the building at Elevation ~~1051.9~~".

For location see Drawing GA-E-9.

Submit for our consideration the deduction from the Contract Price due to the above deletions."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/eas

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 23, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Garage -
CHANGE NO. 271 - Chopping of Concrete Slab in Studios 3 and 4

Reference (a) Verbal Instructions of your Mr. W. Seelman on 8/31/51

Dear Mr. Dawson:

On August 31, 1951 Mr. Seelman authorized us to chop the concrete slab in the Control Rooms for Studios 3 and 4 where necessary to install the audio troughs at the proper elevation. Daily time vouchers on this work was signed by Mr. Seelman and our Mr. Brady and we have issued Field Order M-1 to Fischbach & Moore, Inc. for this work.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. ~~Definite~~ extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/ODV/eas

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 23, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Garage
CHANGE NO. 262-A - August 14, 1951 Structural Revisions

Reference: (a) Mr. James A. Dawson's letter 10 October 1951 to FTWS, Inc.

Dear Mr. Dawson:

This Change is supplemental to our Change No. 262, dated August 22, 1951. In Change No. 262 one of the reference drawings showed the deletion of the furring, lathing and cement plaster soffits on the east and west ramps of the General Assembly Building. When these soffits were omitted there were certain areas under the exit doors and on the north wall of the Meeting Halls neck in which no finish was provided.

In the above referenced letter you advised us to proceed as follows:

"Due to the delation of the cement plaster soffits under the east and west balconies and ramps a space of about three inches in height and the width of the exit door has been left open under each of the ten exit doors on both the east and west sides of the building.

These spaces shall be filled with brick to within one (1) inch of the face of the stone and cement plaster applied over the brick, the Tuxtone finish face of which shall be flush with the adjoining stone. Refer to our Drawing No. 657 and Monahan-McCann's Drawing 2B, "etail 1-1, for these conditions.

Also the space on the north side of the neck over the aluminum and glass spandrel must be filled in with metal furring, lath and one (1) inch of cement plaster.

The installation shall be as per discussion between your Mr. P. DelVecchio and Messrs. Aussem and Healy of the U.N.H.P.O. A sketch showing the details of these two installations will be issued shortly

Reference the cement plaster, the final coat shall be Silver Gray Tuxtone No. 94, the same color as approved for the Meeting Halls, shall be applied as per manufacturer's printed instructions. The Tuxtone shall finish flush with the stone face under the exit doors and two (2) inches beyond the face of the aluminum head section as per the detail.

Include all the above changes in the breakdown for General Assembly Change No. 262 which change includes the deletion of the cement

Mr. James A. Dawson

-2-

October 23, 1951

re: Contract HQ 1/82 - CHANGE NO. 262-A


In addition to the spaces mentioned above we were advised to provide a cement plaster facia on the east wall immediately north of the Meeting Halls neck which is a similar condition to those described.

We will take this supplemental instruction in account in preparing our Estimate for Change No. 252.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.


M. J. Grogan
Project Manager

MJG/PDV/eas

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 23, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, N.Y.

RE: Contract HQ 1/82 - General Assembly & North Parking Space
ESTIMATE FOR CHANGE NO. 246
Electrical Revisions at Bar, Elevation 68'-4"

References:

- (a) U.N. Dwg. SK-GA-E-5P dated 7/20/51
- (b) Mr. James A. Dawson's letter dated 7/23/51 to FTWS, Inc.
- (c) U.N. Interiors Dwg. No. 8, dated 11/24/50
- (d) FTWS, Inc. letter (Grogan) to U.N. dated 8/9/51 (C.O. 246)

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we claim an increase in our total guaranteed maximum cost price in the amount of ONE HUNDRED FIFTY-FIVE DOLLARS (\$155.00) for the changes in the work itemized herein, which are required by the above references.

Attached are three (3) copies of Fischbach & Moore's Pricing Sheet dated 8/23/51 giving itemized breakdown of this change.

No charge is included in this estimate for any patching by architectural trades.

Will you kindly issue a Change Order-Addition in the amount of \$155.00 covering the changes itemized herein.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan

M. J. Grogan
Project Manager

MJG/CER/lbr
Attachments

PRICING SHEET

JOB U. N. General Assembly

LOCATION _____

Job
Estimate No. 9130OWNER C.O. No. 246

ARCHITECT _____

SHEET No. _____

BID TO Per Letter July 30, 1951

OF _____ SHEETS

ESTIMATED BY C.A. & A.S.

PRICED BY _____

EXTENDED BY _____

CHECKED BY N.A.DATE 8/23/51

MATERIAL	QUANTITY	MATERIAL LIST PRICE	PER	DISC.	EXTENSION	LABOR UNIT PRICE	PER	EXTENSION
<u>Omit</u>								
Duplex Receptacles	2	20 48	C		- -			
1" Box & Lg. Cover	2	25 76	C		1 1			
plex Recep. Plate	2	27 85	C		1 1			
					<u>2</u>			6 00
<u>Add</u>								
Fluorescent Strip - 16'	1	63 20	ea		63 00	1		63 00
Gotham No. 2151								
1" Sq. Box Blank Cover	2	22 30	C		- -			
1" " " 2 g "	1	26 00	C		- -			
S.P. Toggle Sws.	2	90 30	C		2 1			
Toggle Sw. Plates 20	1	55 70	C		1			
3/4" Black Cond.	60'	13 35	C		8 1			
40 Watt Fluor. Lamps	4	73	ea		3 1			
#12 R.C. Wire	70'	12 43	M		1 1			
Incidentals	Allow				<u>5</u>			
					83 00	1		84 00
Material Net Add		81 00						
Sales Tax 2%		2 00						
Labor & Superv.		38 00						
13.75 % Insurance		5 00						
Job Expense		<u>7 00</u>						
		133 00						
15% O.H. & P.F.		20 00						
6% F.O.A.B. & V.L.		<u>2 00</u>						
		155 00						
No Patching								

FULLER - TURNER - WALSH - SLATTERY, INC.
 UNITED NATIONS CONTRACT
 403 EAST 42ND STREET
 NEW YORK 17, N. Y.

file
 October 23, 1951

Mr. James A. Dawson
 Co-Ordinator of Construction
 Headquarters Planning Office
 Room 2272
 United Nations, New York

RE: Contract HQ 1/82 - General Assembly & North Parking Space
 ESTIMATE FOR CHANGE NO. 228
Hollow Metal Partitions in Master Control Room

References:

- (a) U.N. Dwg. SK-663, dated 7/2/51
- (b) Mr. James A. Dawson's letter dated 7/3/51 to FTWS, Inc.
- (c) FTWS, Inc. letter (Grogan) to U.N. dated 7/16/51 (C.O.228)

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we claim an INCREASE in our total guaranteed maximum cost price in the amount of EIGHT HUNDRED FORTY DOLLARS AND FIFTY-TWO CENTS (\$840.52) for the changes in work itemized herein, which are required by the above references.

This estimate is broken down as follows:

HOLLOW METAL PARTITIONS
 (E.F. Hausman Co.)

To erect partitions at 1st Basement Level, as called for by reference (a):

Quantity	Description	Contract Unit	Total
41½ l.f.	Erect 9' 2½" Partitions	3.78	156.87 ✓
43½ "	Furnish & Erect D.M.B.	2.22	96.57 ✓
14 "	39 oz. Crystal Glass (for pairs of doors)	3.32	46.48 ✓
3	Furnish & Erect Masonite ends	18.81	56.43 ✓
2	Make up pairs of doors	72.80	145.60 ×
2	Pair flush bolts for above pr. doors	11.07	22.14 ×
3	Panel cuts	13.50	40.50
41½ l.f.	Sand and Paint (2 coats)	2.50	103.75 × 14¢ per ft
33 hours	Remove 41½ l/f partition from stock, hoist and distribute to job 33 hrs @ \$3.00 = \$99.00, plus ins. @ 11.051% = \$109.94, plus 15% profit		126.43

(cont'd. on Page 2)

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

- Page 2 -

Oct. **23**, 1951

RE: HQ 1/82 - ESTIMATE FOR CHANGE NO. 228

<u>Quantity</u>	<u>Description</u>	<u>Contract Unit</u>	<u>Total</u>
120 1/f	Wood mould for pairs of doors	.07	8.40
<i>std cost</i> 41½ 1/f	Repair Panels	.90	<u>37.35</u>
TOTAL - THIS ESTIMATE			<u><u>\$840.52</u></u>

Will you kindly issue a Change Order-ADDITION in the amount of \$840.52 to cover the costs itemized above.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan

M. J. Grogan
Project Manager

MJG/CER/lbr

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

October 23, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Garage -
CHANGE ORDER NO. 215 - May 23, 1951 Architectural Revision #27

References: (a) List of Drawings included in Attached Table
(b) FTWS, Inc. Notification of Change No. 65, dated 9/20/51
(c) Mr. Wallace K. Harrison's letter of 17 October 1951

Dear Mr. Dawson:

On May 23, 1951 we received the drawings contained in Reference (a) with instructions not to proceed with the revisions shown on these drawings until we had notified you what costs would be involved.

On September 20, 1951 we sent you our Notification of Change No. 65, Reference (b) which gave an approximation of the additional costs exclusive of:

- a) Any changes for Acoustical Plastered and Fissured Acoustical Tile on the dome and ceilings in the Assembly Hall
- b) Any changes to the main roof gutter and permalite insulation on the main roof
- c) Any electrical changes

On October 19, 1951 we received your letter of approval, Reference (c) which reads as follows:

"This approval is given for you to proceed with the work required by the modification with reference to Architectural Revision #27, dated May 23, 1951".

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,
FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/eas

LIST OF DRAWINGS & BULLETIN INCLUDED IN ARCHITECTURAL REV. NO. 27
(GENERAL ASSEMBLY CHANGE NO. 215)

<u>Dwg. No.</u>	<u>Rev. No.</u>	<u>Date</u>	<u>Title</u>
Door Schedule	27	5/23/51	Title Sheet
"	"	"	Sheet 2
"	"	"	" 3
"	"	"	" 4
"	"	"	" 5
"	"	"	" 6
"	"	"	" 7
"	"	"	" 8
"	"	"	" 9
"	"	"	" 10
"	"	"	" 11
"	"	"	" 13
A 2	"	"	2nd basement Plan
A 3	"	"	1st "
A 4	"	"	1st Floor Plan
A 5	"	"	2nd "
A 6	"	"	3rd "
A 7	"	"	Booth Plan
A 8	"	"	4th Floor Plan
A 11	"	"	Longitudinal Sections
A 12	"	"	Cross Sections
A 16	"	"	Finish Schedule
RA 101	"	"	Exterior Wall Sections
A 109	"	"	North Elevation Details
A 111	"	"	Roof Details
A 119	"	"	Conf. Room No. 4
RA 119A	"	"	Plan-Conf. Rm. No. 4
RA 119B	"	"	Batten Spacing-Conf. Rm. 4
RA 120	"	"	Details-Conf. Rm. No. 4
A 120A	"	"	Booth Details-Conf. Rm. 4
A 120B	"	"	" " "
A 124	"	"	Details-Radio Studios
A 137	"	"	Door Details
RA 145	"	"	Plan of Assembly Hall
RA 154	"	"	Misc. Conc. Stairs
RA 155	"	"	Elev. #1&2-Plans & Sects.
RA 156	"	"	" #3&4- "
RA 158	"	"	Telephone Booth Details

170-5-18-9
OREGON 9-3950

10/24/51
W. K. Harrison
10/24/51
W. K. Harrison

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

W. K. Harrison

October 23, 1951

Gen Files

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, N. Y.

RE: HQ 1/82 Contract - General Assembly
Electrical Shop Drawing

Dear Sir:

We are resubmitting to you herewith six (6) copies
of Kliegl Bros. drawing 842R, as forwarded to us by Fischbach
and Moore, Inc.

Will you kindly review the above drawing and return
three (3) prints to us with your final approval.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese *PSB*
C. E. Reese
Project Engineer

CER/PIB/lbr
Encl. - Dwg.



ISSUANCE OF DRAWINGS

OFFICE COPY

23 October 1951

7 November 1951

GA & North Parking
Fuller-Turner-Walsh-Slaterry

hand


Submitted by Fischbach & Moore (Kliegl Bros. Dwg.)

3 842R 31 Aug '51 Typical Diagram of Directional Sign Control Panel
(APPROVED AS NOTED 5 Nov 1951 REN) (RESUBMIT)

NOTE:FROM SYSKA & HENNESSY

"This drawing is approved, except as noted in red crayon."

"All approvals are subject to strict compliance with the Contract Plans and Specifications and to all Authorities having Jurisdiction."



SV Lyle

*Toppen
ready*

140-5-18-9
OREGON 9-3950

Mr. Højel
to James Fick

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

October 23, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following
Miscellaneous Iron shop drawing submitted by General Bronze
Corp. and C. E. Halback & Company:

HGP-109-1 Rev. 10/22/51 Six fixed Glass Frames in
East Wall with Lintels.

Will you please return two (2) prints of the above drawings
marked with your approval or necessary corrections?

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



ISSUANCE OF DRAWINGS

OFFICE COPY

24 October 1951

25 October 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery


hand

Submitted by General Bronze & Halback

2	HGP-105-1	15Oct'51	Circular Steel Skylight at Cols. 32-J
2	109-1	12Oct'51	6 fixed Glass Frames in East Wall with Lintels

(APPROVED 25 Oct 1951 PB.)

NOTE: Dwgs. HGP-14-1, 14-2 and 14-3 will follow



L. V. Byler

ISSUANCE OF DRAWINGS

OFFICE COPY

24 October 1951

5 November 1951

GA & North Parking

Fuller-Turner-Walsh-Slattery


hand

Submitted by General Bronze & Halback

2 HGP-14-1 26 Aug'51 Miscellaneous Pipe Railings

(APPROVED AS NOTED 5 Nov 1951 RHN RESUBMIT)

NOTE: Dwg. HGP-14-2 and 14-3 will follow

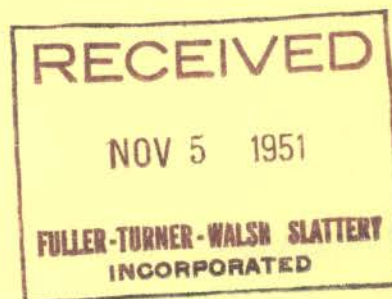

SV Tyler

ISSUANCE OF DRAWINGS

OFFICE COPY

24 October 1951

8 November 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery


hand

Submitted by General Bronze & Halback

2 HGP-14-2 28Sept'51 Miscellaneous Pipe Wall Rails
(APPROVED AS NOTED 7 Nov 1951 REM)

NOTE: STAIR 10 & 11 SHOULD BE OMITTED FROM THIS DRAWING, THEY WERE APPROVED
ON DWG. HGP-46-4 IN MARCH YL.

NOTE: Dwg. HGP-14-3 will follow



L.V. Tyler

ISSUANCE OF DRAWINGS

OFFICE COPY

24 October 1951


9 November 1951

GA & North Parking
Fuller-Turner-Walsh-Slaterry

hand

Submitted by General Bronze & Halback

2 HGP-14-3 23Oct'51 Scale Plans - Stair #24, 29, 30 to 32
(APPROVED AS NOTED 8 Nov 1951 A.D. RESUBMIT)

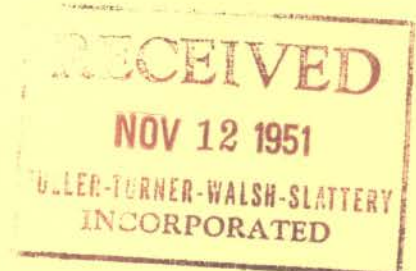

L V Tyler

170-5-18-9 ✓
OREGON 9-3950

Handwritten: ~~Arthur~~
~~Wiley~~

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Handwritten: Mr. Heigel

Handwritten: To Gmo. Fick

October 23, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters Planning Office
Room 2272
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Hollow Metal Doors, Frames &
Trim

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following
Hollow Metal Doors, Frames & Trim shop drawing, submitted by
Atlantic Metal Products Co., Inc.:

- 1 Rev. 10/22/51 Access Panel in Ceiling of
3rd Floor Elevator Lobby.

Will you please return two (2) prints of the above drawing
marked with your approval or necessary corrections?

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

Handwritten: C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



ISSUANCE OF DRAWINGS

OFFICE COPY

23 October 1951

30 October 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Atlantic Metal

2 1 22Oct'51 Access Panel in Ceiling 3rd Fl. Elevator Lobby
(APPROVED 30 Oct 1951 A.D.)

RECEIVED

OCT 30 1951

FULLER-TURNER-WALSH SLATTERY
INCORPORATED

S. V. Tyler

*Hopper
Ready*

140-5-18-91
OREGON 9-3950

Mr. Neigel

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

To Gen. Fick

October 23, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Hollow Metal Doors, Frames &
Trim

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following
Hollow Metal Doors, Frames & Trim shop drawing submitted by
Atlantic Metal Products Co., Inc.:

- 1 Dtd 10/22/51 Schedule Sheet - Three Doors in
Vent. Duct.

Will you please return two (2) prints of the above drawing
marked with your approval or necessary corrections?

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



ISSUANCE OF DRAWINGS

OFFICE COPY

23 October 1951


29 October 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Atlantic Metal

2	1	27Sept'51	Schedule Sheet - 3 doors in Vent. Duct
			(APPROVED 29 Oct 1951 P.B.)



SV Tyle
