

CENTRAL Registry (120-5-18-9) S G Building Construction - Working Project - General Assembly & North parking (1/22) - 1 Nov 1951
Fuller-Turner-Walsh-Slatery Inc.

16 Nov 1951

CLEAR
7/04
S.E.

S-0472

Box-28

File-3

(RAG-1)

En File

-9
OREGON 9-3950

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 16, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 330 - Revision to North Column Ducts

Reference (a) Mr. James A. Dawson's letter of November 13, 1951

Dear Mr. Dawson:

On November 15, 1951 we received the above referenced letter, which reads as follows:

"This will confirm verbal instructions by our Mr. M. Harris to your Mr. C. Bartley to proceed with the fabrication and installation of the ducts at the North Columns in No. 18 gauge steel. The slotted outlets shall also be 18 gauge.

"This work shall be performed at the approximate addition in cost of \$2,400.00.

"Submit for our consideration prices which affect the Contract Price."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/em

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 16, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272,
United Nations, New York 17, N.Y.

RE: CONTRACT HQ 1/82 - GENERAL ASSEMBLY AND NORTH PARKING SPACE
ESTIMATE FOR CHANGE NO. 164
"Substitution of Oversize Waylite Brick
for Common Brick-North Parking Space"

- References:
- a) Paragraph 5-03B, Construction Trade Specifications-North Half Parking Space - dated May 11, 1949.
 - b) FTWS, Inc. Letter (Reese) to United Nations dated February 12, 1951.
 - c) Mr. James A. Dawson's letter of 27 April 1951 to FTWS, Inc.
 - d) FTWS, Inc. Letter (Grogan) to United Nations dated May 15, 1951.

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we are pleased to advise you that there will be no change in our total guaranteed maximum cost price for the changes in work required by the above "references".

Will you kindly acknowledge receipt of and acceptance of this estimate.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan

MJG:CH:amc

M. J. Grogan
Project Manager

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

November 16, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 324 - Structural Revisions

References: (a) GA-4-CS-31c, issued 10/30/51 - "Slab Extended to 10WF25
as shown in Shaded Area, 4th Floor"
(b) GA-4-CS-32, issued 11/2/51 - "Alteration to South Cheek
Wall Cross Bracing to Clear New Light Cove"
(c) GA-4-CS-33, issued 11/5/51, "4 $\frac{1}{2}$ " Diameter Hole Cut in
Beam - 4th Floor
(d) Mr. James A. Dawson's letter, dated 11/5/51
(e) Mr. James A. Dawson's letter, dated 11/8/51

Dear Mr. Dawson:

On October 29, 1951 we received prints of Reference (a). On November 5, 1951 we received prints of References (b) and (c).

On November 12, 1951 we received your transmittal letter, Reference (d), regarding Drawings GA-4-CS-31c and GA-4-CS-32, which reads in part as follows:

"The work shown on all the above drawings should cause no change in price to the concrete and/or reinforcing costs.

"As per our transmittals you have already been instructed to proceed with the work."

On November 12, 1951 we received your transmittal letter, Reference (e) concerning drawing GA-4-CS-33, which reads in part as follows:

"This work has already been accomplished in the field and there will be no change to the Contract Price."

We have sent the above referenced drawings to all the interested subcontractors with the request that they advise us if these revisions affect their subcontract price and we will inform you of their replies as soon as they are received.

continued....

Mr. James A. Dawson


-2-

November 16, 1951
CHANGE NO. 324

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan
Project Manager

MJG/BK/em

Asper
Healy

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

1 Healy

November 16, 1951

General File

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Granite

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following
Granite shop drawings submitted by Joseph Weiss Co., Inc.:

- 3 Rev. 11/13/51 Granite Details - North & South Wall
- 4 Rev. 11/13/51 Granite Details - Granite Curb - West
Podium.

Although approved by you on May 28, 1951, drawing #3 has been
revised to conform with the latest architectural drawings
which indicate the omission of doors #153 and #154 and the
addition of door #160 at the North Elevation of the General
Assembly Building.

Will you please return two (2) prints each of the above draw-
ings marked with your approval or necessary corrections?


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



ISSUANCE OF DRAWINGS

OFFICE COPY

16 November 1951


21 November 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Jos. Weiss

2	3	20Feb'51	Granite Details - North & South Wall (APPROVED AS NOTED 21 Nov 1951 JCB RESUBMIT)
2	4	27Sept'51	Granite Details - Granite Curb - West Podium (APPROVED 21 Nov 1951 REN)



SV Tyler

*Wagner
Healy*

GA

120-5-18-7
OREGON 9-3950

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Healy

General File

November 16, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Acoustical Treatment

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following
Acoustical Treatment shop drawing submitted by Johns-Manville
Sales Corp.

109 Rev. 11/13/51 Conference Room No. 4.

Will you please return two (2) prints each of the above draw-
ings marked with your approval or necessary corrections?

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



ISSUANCE OF DRAWINGS

OFFICE COPY

16 November 1951

26 November 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Johns-Manville

2 109

27Sept'51

Conference Room #4

(APPROVED AS NOTED 23 Nov 1951 RB. RESUBMIT)



L.V. 5/26

Can file

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 16, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272,
United Nations, New York 17, N.Y.

RE: CONTRACT HQ 1/82 - GENERAL ASSEMBLY AND NORTH PARKING SPACE
ESTIMATE FOR CHANGE NO. 208
"June 18, 1951 Structural Revisions"

References: a) U. N. Drawing GA-3CS-26 issued 6/14/51
b) " " " GA-2CS-21 " 6/15/51
c) FTWS Letter (Grogan) to United Nations dated 6/19/51 (C.O.#208)

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we hereby claim an increase in our maximum guaranteed cost price in the lump sum amount of ONE HUNDRED DOLLARS AND NO CENTS (\$100.00) for the items listed herein which are required by the changes in the structural drawing in reference "b" above and by our Change No. 208 which is reference "c". Examination of the structural drawing in reference "a" reveals no change which will affect our maximum guaranteed cost price.

The above increase is broken down as follows:

<u>GA - SECTION 5 - MASONRY WORK (John B. Kelly, Inc.)</u>	<u>Add</u>
a) Add brick on lintel angles.	
1) Add - 500 Jumbo Sand Lime Brick @ \$200.00/M.....	\$ 100.00
TOTAL ADDITION - THIS ESTIMATE.....	\$ 100.00

Will you kindly issue a Change Order-ADDITION in the lump sum amount of \$100.00 to cover the additional work itemized above.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan

M. J. Grogan
Project Manager

MJG:CER:amc

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 16, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Heating, Ventilating, and
Air Conditioning Shop Drawings

Dear Mr. Dawson:

We are submitting to you herewith six (6) prints each of the following drawings as forwarded to us by Kerby Saunders, Inc.:

- 1) Vibration Eliminator Co.'s drawing 368-^S - Vibration Eliminator for systems 404-11, -12, and 403-10, -11.
- 2) National Sheet Metal Works' drawing GA-RJ-4, Ductwork Risers in West Wall (cols. 31 & 32)
- 3) National Sheet Metal Works' drawing GA-1-6, Ductwork - Booths & Conference Room #4 (El. 41'-0").

Kindly review the above-mentioned drawings and return three (3) copies of each with your comments and/or approval.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese p18
C. E. Reese
Project Engineer



RECEIVED

DEC 10 1951

FULLER-TURNER-WALSH-SLATTERY
INCORPORATED

ISSUANCE OF DRAWINGS

OFFICE COPY

16 November 1951

10 December 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Kerby Saunders

3	368-3	None	Vibration Elim. Sys. 404-11-12 & 403-10 - 11. (Vibration Eliminator Co. Dwg.) (DISAPPROVED 6 Dec 1951 REN RESUBMIT)
3	GA-RJ-4	2 Oct '51	Ductwork Risers West Wall (cols. 31&32) (Nat'l Sheet Metal Dwg.) (APPROVED 7 Dec 1951 REN)
3	GA-1-6	7 Sept '51	Ductwork Booths & Conference Room 4 (El. 418-0") (Nat'l Sheet Metal Dwg.) (APPROVED AS NOTED 7 Dec 1951 REN RESUBMIT)

NOTE: FROM SYSKA & HENNESSY

"Dwg. 368-3 is disapproved. These eliminators are not adaptable for the type of units which they serve. We are planning a new type of foundation for these units."

"Dwg. GA-RJ-4 is approved."

"Dwg. GA-1-6 is approved, except as noted in yellow crayon."

"All drawings are subject to strict compliance with the Contract Plans and Specifications and to all Authorities having Jurisdiction."

SV Tyle

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 16, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

*Finaly Approved
Gen. Files
11/19/51*

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Reinforced Concrete Details

Gentlemen:

We are sending you herewith, for your information, one (1)
print of the following Reinforcing Steel shop drawings,
as approved for field distribution:

702	Rev. 10/15/51	Reinforcing Details - Roof
704	Rev. 10/16/51	" " - Roof Wells,
	Nos. 6, 7, 8, 9, 10	
705	Rev. 10/15/51	Reinforcing Details - Roof Wells
904	Rev. 10/16/51	" " - Elevator
		Machine Floors.

(Brennan & Sloan, Inc.-Knickerbocker Construction Corp.)
Subcontractor


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/BK/em



COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 16, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Reinforced Concrete Details

Gentlemen:

We are sending you herewith, for your information, one (1)
print of the following Reinforcing Steel shop drawings,
as approved for field distribution:

702	Rev. 10/15/51	Reinforcing Details - Roof
704	Rev. 10/16/51	" " - Roof Wells,
		Nos. 6, 7, 8, 9, 10
705	Rev. 10/15/51	Reinforcing Details - Roof Wells
904	Rev. 10/16/51	" " * Elevator
		Machine Floors.

(Brennan & Sloan, Inc.-Knickerbocker Construction Corp.)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



C. E. Reese
Project Engineer

CER/BK/em

-9-

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 16, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Reinforced Concrete Details

Gentlemen:

We are sending you herewith, for your information, one (1)
print of the following Reinforcing Steel shop drawings,
as approved for field distribution:

702	Rev. 10/15/51	Reinforcing Details - Roof
704	Rev. 10/16/51	" " - Roof Wells, Nos. 6, 7, 8, 9, 10
705	Rev. 10/15/51	Reinforcing Details - Roof Wells
904	Rev. 10/16/51	" " - Elevator Machine Floors.

(Brennan & Sloan, Inc.-Knickerbocker Construction Corp.)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/BK/em

-2

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 16, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Reinforced Concrete Details

Gentlemen:

We are sending you herewith, for your information, one (1)
print of the following Reinforcing Steel shop drawings,
as approved for field distribution:

702	Rev. 10/15/51	Reinforcing Details - Roof
704	Rev. 10/16/51	" " - Roof Wells,
	Nos. 6, 7, 8, 9, 10	
705	Rev. 10/15/51	Reinforcing Details - Roof Wells
904	Rev. 10/16/51	" " - Elevator
		Machine Floors.

(Brennan & Sloan, Inc.-Knickerbocker Construction Corp.)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/BK/em

-9

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
NEW YORK

November 16, 1951

Mr. James A. Dawson
Co-ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/32 - General
Assembly and North Half
Parking Space
Reinforced Concrete Details

Gentlemen:

We are sending you herewith, for your information, one (1) print of the following Reinforcing Steel shop drawings, as approved for field distribution:

702	Rev. 10/15/51	Reinforcing Details - Roof
704	Rev. 10/16/51	" " - Roof Wells,
	Nos. 6, 7, 8, 9, 10	
705	Rev. 10/15/51	Reinforcing Details - Roof Wells
904	Rev. 10/16/51	" " - Elevator
		Machine Floors.

(Brennan & Sloan, Inc.-Knickerbocker Construction Corp.)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese, Jr.

C. E. Reese
Project Engineer

CER/BK/cm

-9-

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 16, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract No 1/52 - General
Assembly and North Half
Parking Space
Reinforced Concrete Details

Gentlemen:

We are sending you herewith, for your information, one (1)
print of the following Reinforcing Steel shop drawings,
as approved for field distribution:

702	Rev. 10/15/51	Reinforcing Details - Roof
704	Rev. 10/16/51	" " - Roof Wells,
		Nos. 6, 7, 8, 9, 10
705	Rev. 10/15/51	Reinforcing Details - Roof Wells
904	Rev. 10/16/51	" " - Elevator
		Machine Floors.

(Brennan & Sloan, Inc.-Knickerbocker Construction Corp.)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CHH/RE/en

120-5-18-9

cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
Van Name
McLeod
Seelman
Hannegan
S & H-2

16 November 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, N.Y.

Re: Contract HQ 1/82 - General Assembly
and North Parking Garage - Electric
Change No. 316 and Miscellaneous Changes


Gentlemen:

Please omit from the above change the work required by Paragraphs
C. (1) and C. (2) of our letter dated 15 November 1951, as follows:

- C. Maintenance Area - 2nd Basement
1. At column T-29 move the 24" x 24" x 8" communication box on the north face of Column T-29 east to clear the new partition.
 2. Provision must be made for access to the 20" x 10" x 3" telephone strip box located on the east face of Column T-28. This box was not installed in accordance with Mechanical Drawing GA-E-1C.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office



JZ:ml:eh

120-5-18-9-
cc: Harrison
McLeod
Zunser
Van Name
Hopper
Healy
Seelman

16 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, N.Y.

Re: Contract HQ 1/82 - General Assembly
and North Parking Garage
Estimate for Change No. 251 - Revised
Lighting Layout in Master Control Room

Gentlemen:

You are hereby directed to omit the work required by Change Order No. 251, dated 8 November 1951, in which you claim an increase in the guaranteed maximum cost price in the amount of \$93.00. This work has not and will not be done.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

JZ:eh

⑤ LR

- 9 -

Fuller-Turner-Walsh-Slaterry, Inc.
General Contractors
United Nations Permanent Headquarters

R.P. #31

NOTIFICATION OF CHANGE

Date: November 15, 1951

TO: Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272, United Nations
New York 17, New York

N. C. # 79

Building: GENERAL ASSEMBLY & NORTH PARKING SPACE

Reference Information:

a) GA-NS-215 - 3/13/51;	e) GA-NS-215 - 3/22/51;	i) GA-S-190 - 3/27/51
b) 212 - 3/16/51;	f) 219C - 3/27/51;	j) 208 - 3/27/51
c) 213 - 3/16/51;	g) 220C - 3/28/51;	k) 360 - 3/27/51
d) 214 - 3/16/51;	h) GA-S-170 - 3/27/51	

Description of Changes: Structural Details: (see below)

The above contemplated change effects the branches of the work indicated by X marks. There is shown below a quick estimate of the approximate cost of the change merely to indicate its magnitude and to assist the Owner in determining whether or not the change should be made.

<input type="checkbox"/> F-T-W-S Inc. Work	<input type="checkbox"/> Construction Insulation	<input type="checkbox"/> Painting & Finish
<input type="checkbox"/> Structural Steel	<input type="checkbox"/> Metal, Doors, Frames & Trim	<input type="checkbox"/> Venetian Type Blinds
<input checked="" type="checkbox"/> Concrete Construction Work	<input type="checkbox"/> Roll-up Steel Doors	<input type="checkbox"/> Resilient Floor
<input type="checkbox"/> Concrete Slabs & Fireproofing	<input type="checkbox"/> Metal Toilet Enclosures	<input type="checkbox"/> Covering
<input type="checkbox"/> Floor & Roof Fill	<input type="checkbox"/> Hollow Metal Partitions	<input type="checkbox"/> Miscellaneous
<input type="checkbox"/> Finish Cement Work	<input type="checkbox"/> Marble Work	<input type="checkbox"/> Accessories
<input type="checkbox"/> Masonry-Mortars	<input type="checkbox"/> Ceramic Tile	<input type="checkbox"/> Heating, Ventilating
<input type="checkbox"/> Waterproofing (Membrane Spondrel)	<input type="checkbox"/> Terrazzo Work	<input type="checkbox"/> & Air Conditioning
<input type="checkbox"/> Dampproofing (Mastic)	<input type="checkbox"/> Furring & Lathing	<input type="checkbox"/> Plumbing
<input type="checkbox"/> Caulking	<input type="checkbox"/> Plastering	<input type="checkbox"/> Sprinklers
<input type="checkbox"/> Cut Stonework	<input type="checkbox"/> Acoustical Treatment	<input type="checkbox"/> Electrical
<input type="checkbox"/> Roofing (built-up)	<input type="checkbox"/> Sound Conditioning	<input type="checkbox"/> Sheet Metal Work
<input type="checkbox"/> Carpentry & Millwork	<input type="checkbox"/> Miscellaneous Iron	<input type="checkbox"/> Glass & Glazing
<input type="checkbox"/> Ornamental Metal Work	<input type="checkbox"/> Finish Hardware	

Approximate Total Cost of this Change is \$ No Change in Price for Work shown on drawings references "g" thru "e". Those in references "f" thru "k" are excluded from this N.C. (see below)

and the Owner's immediate decision is required, avoiding a "Stop Order" of Field Operations and permitting the work to continue without interruption.

FULLER-TURNER-WALSH-SLATERRY, INC.

By: M. J. Grogan Date: 11/15/51
Project Manager

The Above change will not be made and the work is to proceed in accordance with the existing Contract Requirements.

You are hereby instructed to proceed with the work in accordance with this N.C. and issue P.E.O.'s as required. Price adjustments to be made under the Contract Terms.

UNITED NATIONS HEADQUARTERS

UNITED NATIONS HEADQUARTERS

By: _____ Date: _____
By: M. J. Grogan Date: 11/26/51

A. The drawings in "f" & "g" are included in GA-S-610, which is in Change No. 167.
B. The next revision (#5) of the drawings in references "h" & "i" is in Change No. 160.
C. A subsequent revision (#6) of the drawing in reference "j" is in Change No. 158.
D. A subsequent revision (#6) of the drawing in reference "k" is in Change No. 171.

FULLER - TURNER - WALSH - SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 15, 1951

file

Mr. James A. Dawson
 Co-Ordinator of Construction
 Headquarters Planning Office
 Room 2272,
 United Nations, New York 17, N.Y.

RE: CONTRACT HQ 1/82 - GENERAL ASSEMBLY AND NORTH PARKING SPACE
CHANGE NO. 8 $\frac{1}{2}$ and ESTIMATE FOR CHANGE NO. 8 $\frac{1}{2}$ - COMBINED
"Rental of Pumps and Compressor Used in Cleaning Billet
Pockets"

Reference: Confirmation of Instructions to Superintendent No. 4674 dated 8/9/51,
 re: "Clean Out all Billet Pockets in Div. #1 and Div. #2."

Dear Sir:

In order to clean the billet pockets as required by the above reference, FTWS, Inc. rented pumps and a compressor from Slattery Contracting Co. to remove the water and chips.

The cost of the rental of the pumps and the compressor is broken down as follows

Slattery Contracting Company:

Date:	1 $\frac{1}{2}$ " Pump:	2" Pump:	Pump Operator:	105 Compressor:	Air Hose(250 ft.):
7-24-50	8	8	-	-	-
8-20-50	4	-	8*	-	-
8-21-50	16	-	8	-	-
8-22-50	8	-	8	-	-
8-24-50	8	-	8	-	-
8-25-50	8	-	8	-	-
8-28-50	8	-	8	-	-
8-29-50	8	-	8	-	-
8-30-50	8	-	8	-	-
8-31-50	8	-	8	-	-
9-5-50	8	-	4	8	8
9-6-50	8	-	4	8	8
9-7-50	8	-	4	8	8
9-8-50	8	-	4	8	8
9-11-50	8	-	2 $\frac{2}{3}$	8	8
9-12-50	8	-	2 $\frac{2}{3}$	-	-
9-13-50	8	-	3	-	-
9-14-50	8	-	4	-	-
9-15-50	8	-	2 $\frac{2}{3}$	-	-
9-18-50	8	-	2 $\frac{2}{3}$	-	-
9-19-50	8	-	2 $\frac{2}{3}$	-	-
9-20-50	8	-	2 $\frac{2}{3}$	-	-
9-21-50	8	-	2 $\frac{2}{3}$	-	-
9-22-50	8	-	3	-	-
9-25-50	8	-	2 $\frac{2}{3}$	-	-
9-26-50	8	-	4	-	-
9-27-50	8	-	4	-	-
9-28-50	8	-	4	-	-
9-29-50	8	-	4	-	-
TOTAL:	236 hrs.	8 hrs.	135 $\frac{1}{3}$ hrs.	40 hrs.	40 hrs.

* Sunday

(continued on page 2)

Mr. James A. Dawson
Re: Change No. 8 $\frac{1}{2}$ & Estimate for Change No. 8 $\frac{1}{2}$ -COMBINED
Contract HQ 1/82 - General Assembly & North Parking

November 15, 1951
(page - 2 -)

Summary:

105 Compressor - 1 wk. @ \$75.00/wk.....	\$75.00
250' Air Hose - 40 hrs. @ \$.75/hr.....	38.00
1 $\frac{1}{2}$ " Pump - 236 hrs. @ \$.55/hr.....	129.80
2" Pump - 8 hrs. @ \$.64/hr.....	5.12

Pump Operator

135 1/3 hrs. @ \$2.75/hr.....	\$372.17
Insurance 13.333%.....	49.62
	<u>\$421.79</u>
15% O & P.....	63.27
4.5% - FOAB & UI.....	16.75
	<u>\$501.81</u>
	501.81

Premium Time

Pump Operator - 8 hrs. @ \$2.75/hr....	\$22.00
15% O & P.....	3.30
4.5% FOAB & UI.....	.99
	<u>\$26.29</u>
	26.29
Total Addition: (Slattery Contracting Company).....	\$776.02

TOTAL ADDITION - THIS ESTIMATE.....\$776.02

One (1) copy of each of Slattery Contracting Company's "Daily Report" covering the above work is already in your files.

We request your approval for issuing a Purchase Order in the amount of \$776.02 to Slattery Contracting Company to cover the cost of this work. The issuance of the Purchase Order will not increase or decrease our total guaranteed maximum cost price.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

WJG:CER:amc

Wagner Healy

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Mr. Healy
4

November 15, 1951

*General
Felt*

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

RE: HQ 1/82 Contract - General Assembly
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following miscellaneous iron shop drawings submitted by General Bronze Corp. and C. E. Halback & Co. -

<u>No.</u>	<u>Date</u>	<u>Title</u>
HGP 114-1	Rev. 11/13/51	Misc. Pipe Railings
HGP 114-2	Rev. 11/14/51	Misc. Pipe Wall Rails
HGP 114-3	Rev. 11/14/51	Scale Plans - Stair #27,29,30, 31, 32
HGP 101-1	Rev. 11/19/51	Developed Elevation of East and West Walls & Schedule of Brackets
HGP 101-2	Rev. 11/13/51	Layouts of Brackets & Outriggers in East & West Walls
HGP 101-3	Rev. 11/13/51	Angle Wall Supports Below Booths & Bent Plate Brackets From Booth to Cheeks

Will you kindly return two prints each of the above drawings marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer



CER/MH/lbr
Encls. - dwgs.



ISSUANCE OF DRAWINGS

OFFICE COPY

15 November 1951

30 November 1951

GA


Fuller-Turner-Walsh-Slaterry

hand

Submitted by General Bronze & Halback

2	HGP-14-1	26Aug'51	Misc. Pipe Railings (APPROVED AS NOTED 29 Nov 1951 JCB RESUBMIT)
2	14-2	28Sept'51	Misc. Pipe Wall Rails <i>app'd as noted</i>
2	14-3	23Oct'51	Scale Plans - Stair #27, 29, 30-22 32 (APPROVED 29 Nov 1951 JCB)

NOTE: Dwgs. HGP-101-1, 2 and 3 will follow



Lv Tyler

ISSUANCE OF DRAWINGS

OFFICE COPY

15 November 1951


5 December 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by General Bronze & Halback

2	HGP-101-1	18Oct'51	Developed Elev. of E & W Walls & Sch. of Brackets (APPROVED 5 Dec 1951 REN) (NOTE: CORRECTION IN WHITE CIRCLED WITH YELLOW CRAYON)
2	101-2	"	Layouts of Brackets & Outriggers in E & W Walls
2	101-3	26Oct'51	Angle Wall Supports Below Booths etc. (APPROVED 5 Dec 1951 REN)



J.V. Tyler

Fuller-Turner-Walsh-Slaterry, Inc.
UNITED NATIONS CONTRACT403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 15, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly
and North Half Parking Space
Special & Stock Light Fixtures

Dear Mr. Dawson:

We have your letter of November 8, 1951 in which you transmitted copies of the revised Standard and Special Light Fixtures schedules. You state in this letter that the issuance of these drawings should cause no change to the Contract Price up to November 5, 1951.

You, however, state that we are to proceed as per the information contained in these schedules and to notify you, if we disagree with your statement concerning change to the Contract Price.

As discussed at great length between Mr. Harris, of your office, Mr. Bartley, of Fuller-Turner-Walsh-Slaterry, Inc., and Mr. McNary, of Fischbach & Moore, Inc., it was agreed that the standard light fixture schedule would be re-estimated in our Change No. 328, and the previous estimate of cost of Standard Light Fixtures, contained in our Estimate for Change No. 69, would be deducted from the re-estimated cost of Change No. 328. The resulting addition or deduction would be included in our Estimate for Change No. 328.

Similarly, the Special Light Fixture schedule will be re-estimated in our Change No. 329, and the previous estimate of cost of Special Light Fixtures contained in our Estimate for Change No. 70, will be deducted from the re-estimated cost of Change No. 329. The resulting addition or deduction will be the cost of Change No. 329.

Our Estimates for Changes Nos. 328 and 329 will be submitted to you shortly on this basis.

Very truly yours,

FULLER-TURNER-WALSH-SLATERRY, INC.

C. E. Reese
C. E. Reese
Project Engineer



FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 15, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following
Miscellaneous Iron shop drawing submitted by General Bronze
Corp. and C. E. Halback & Company:

HGP-56-5 Rev. 11/13/51 Scale Details of Typical Bay
For Upper & Lower Booths.

Although approved by you on October 22, 1951, this drawing
has been revised to show four (4) $\frac{1}{4}$ " Plate Stiffeners welded
to the $\frac{1}{4}$ " Bent Plate (in head of Upper & Lower Booth Bays)
in each Bay of 7 degrees and 30 minutes.

This revision is in accordance with your Mr. Roy Nelson's
request and is being submitted for record purposes.

Will you please return two (2) prints of the above drawing
marked with your approval or necessary corrections?


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



ISSUANCE OF DRAWINGS

OFFICE COPY

15 November 1951


30 November 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by General Bronze & Halback

2 HGP-56-5 24Sept'51 Scale Details of Typical Bay for Upper & LowerBooths
(APPROVED 30 Nov 1951 REN)



*Shopper
Healy*

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 15, 1951

Mr. Healy
General Kike

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Cut Stone

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following
Cut Stone shop drawing, submitted by Monahan-McCann Stone Co.:

788-15 Rev. 11/3/51 Balcony & Ramp * West Elev.

Will you please return two (2) prints of the above drawing
marked with your approval or necessary corrections?

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



ISSUANCE OF DRAWINGS

OFFICE COPY

15 November 1951

21 November 1951


GA & North Parking
Fuller-Turner-Walsh-Slaterry

hand

Submitted by Monahan McCann

2 788-15 15Jan'51 Balcony & Ramp West Elev.

(APPROVED AS NOTED 21 Nov 1951 REN RESUBMIT)

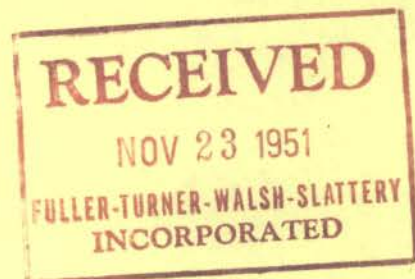

SV Tyler

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

Final Approved
Gen Files
11/16
LS

November 15, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (NHPS)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Miscellaneous Iron shop drawing, as
approved for field distribution:

HGP-102-1 Dated 10/17/51 3 Door Frames Type R-10
(1st Ave. Vent Duct).

(General Bronze Corp. & C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 15, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (NHPS)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Miscellaneous Iron shop drawing, as
approved for field distribution:

HGP-102-1 Dated 10/17/51 3 Door Frames Type R-10
(1st Ave. Vent Duct).

(General Bronze Corp. & C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 15, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (NHPS)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Miscellaneous Iron shop drawing, as
approved for field distribution:

HQP-102-1 Dated 10/17/51 3 Door Frames Type R-10
(1st Ave. Vent Duct).

(General Bronze Corp. & C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

-9-

UNITED NATIONS CONTRACT
NEW YORK

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (NHPS)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1) print of the following Miscellaneous Iron shop drawing, as approved for field distribution:

HQP-102-1 Dated 10/17/51 3 Door Frames Type R-10
(1st Ave. Vent Duct).

(General Bronze Corp. & C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CUR/MH/cm

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 15, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

*Final Approved
Gen Files
11/16/51*

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Ornamental Metal shop drawing, as ap-
proved for field distribution:

GBA-40 Rev. 10/31/51 Detail of Access Panel in Ceiling
Over Sliding Sash in East Wall.

(General Bronze Corp. and C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 15, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Ornamental Metal shop drawing, as ap-
proved for field distribution:

GBA-40 Rev. 10/31/51 Detail of Access Panel in Ceiling
Over Sliding Sash in East Wall.

(General Bronze Corp. and C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

-9-

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 15, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Ornamental Metal shop drawing, as ap-
proved for field distribution:

GBA-40 Rev. 10/31/51 Detail of Access Panel in Ceiling
Over Sliding Sash in East Wall.

(General Bronze Corp. and C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 15, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (CA)
Ornamental Metal

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Ornamental Metal shop drawing, as ap-
proved for field distribution:

GBA-40 Rev. 10/31/51 Detail of Access Panel in Ceiling
Over Sliding Sash in East Wall.

(General Bronze Corp. and C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CHH/MH/em

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

Final Approved
Gen files
11/16
LSJ

November 15, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Miscellaneous Iron shop drawings as
approved for field distribution:

HGP-46-4	Rev. 10/16/51	Railing in Corridor & Pipe Rails in Record Rooms
HGP-49-13	Rev. 10/16/51	St. & Glass Screens 347/GM to 354/GM incl.
HGP-49-15	Rev. 10/16/51	F.S. Details for Steel & Glass Screens.

(General Bronze Corp. and C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer



-9

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 15, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Miscellaneous Iron shop drawings as
approved for field distribution:

HGP-46-4	Rev. 10/16/51	Railing in Corridor & Pipe Rails in Record Rooms
HGP-49-13	Rev. 10/16/51	St. & Glass Screens 347/GM to 354/GM incl.
HGP-49-15	Rev. 10/16/51	F.S. Details for Steel & Glass Screens.

(General Bronze Corp. and C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

-9✓

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 15, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Miscellaneous Iron shop drawings as
approved for field distribution:

HGP-46-4	Rev. 10/16/51	Railing in Corridor & Pipe Rails in Record Rooms
HGP-49-13	Rev. 10/16/51	St. & Glass Screens 347/GM to 354/GM incl.
HGP-49-15	Rev. 10/16/51	F.S. Details for Steel & Glass Screens.

(General Bronze Corp. and C. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

91
COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 15, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/52 - General
Assembly and North Half
Parking Space (GA)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1)
print of the following Miscellaneous Iron shop drawings as
approved for field distribution:

HGP-46-4	Rev. 10/16/51	Railing in Corridor & Pipe Rails in Record Rooms
HGP-49-13	Rev. 10/16/51	St. & Glass Screens 347/GM to 354/GM incl.
HGP-49-15	Rev. 10/16/51	F.S. Details for Steel & Glass Screens.

(General Bronze Corp. and G. E. Halback & Company)
Subcontractor

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em

120-5-18-9
cc: Harrison
McLeod
Zunser
Van Name
Hopper
Healy

15 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, N.Y.

Re: Contract HQ 1/82 - General Assembly and
North Parking Garage - Notification of
Change No. 77 (R.P. #65) -
North Lobby Revisions

Gentlemen:

Attached hereto is one copy of Notification of Change No. 77 (R.P.#65)
approved by James A. Dawson for the United Nations.

This approval is given for you to proceed with the work required by the
modification with reference to North Lobby Revisions with the following work
to be omitted:

- (a) The finish cement work consisting of rubbing
the underside of the exposed roof slab and
beams with carborundum and cutting off the
toggle inserts;

The work required under the remainder of this Notification of Change
No. 77 shall be performed as described therein.

It is our understanding, however, that the amount of the omissions
and the amount of the additional work balance and that there will be no
additional cost for the remaining portion of the work described in
Notification of Change No. 77.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

Enclosure

JZ:ml:eh

120-5-18-9

cc: Harrison
McLeod
Zunser
Van Name
Hopper
Healy

15 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, N.Y.

Re: CONTRACT HQ 1/82 - General Assembly and
North Parking Garage - Notification of
Change No. 74 (R. P. #59) - Provide Masonry
Pylons at N.E. & N.W. Corners of Roof of Neck

Gentlemen:


Attached hereto is one copy of Notification of Change No. 74 (R.P. #59) approved by James A. Dawson for the United Nations.

This approval is given for you to proceed with the work required by the modification with reference to providing masonry pylons at northeast and northwest corners of roof of neck.

It is understood that this approval does not include the cost of this change as indicated in the Notification of Change No. 74, which is solely an approximation. It is understood, also, that the actual price adjustment will be made as required by the terms of the contract.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

Enclosure

JZ:eh

120-5-18-9
JJHE:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod
Seelman
Hannegan
S & H-2

15 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Electric - Change No. 316 and Miscellaneous
Changes

Gentlemen:

Please proceed with the following changes:

A. In the Press Lounge Area

1. Install two (2) floor outlets approximately on the K Line in lieu of the two (2) wall receptacles located between Columns K-21 and K-22.
2. Install two (2) floor outlets, approximately 2'-0" north of the metal railing, in lieu of two (2) wall receptacles located between Columns 21-J and 21-K.

Refer to Drawing GA-E-5L for these items.

B. At Podium, Elevation 453'-0"

1. Install one (1) convenience receptacle on wall under each of the two (2) Secretariat tables. For the exact locations please refer to Drawing DSK-449, one marked up copy of which was handed to Mr. A. Schumer of Fischbach & Moore, Inc. This receptacle shall be connected to the existing receptacle circuit serving the President's table. (See Drawing No. GA-E-4L.)

C. Maintenance Area - 2nd Basement

1. At Column T-29 move the 24" x 24" x 8" communication box on the north face of Column T-29 east to clear the new partition.
2. Provision must be made for access to the 20" x 10" x 3" telephone strip box located on the east face of Column T-28. This box was not installed in accordance with Mechanical Drawing GA-E-1C.

Submit for our consideration prices which will affect the Contract Price. Include the cost of C-1 in the same change as costs for Revision No. 45, i.e. Change No. 316.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

120-5-18-9
15 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Cement Fill and Finish
UNHPO Item GA-13


Gentlemen:

Proceed with the following change. In the area described below install cement fill screeded to the same height as the cement on top of beam at Column Line H but in no case higher than Elevation 40'-2 1/2".

From the west wall of the General Assembly Building west to Column Line H and from a line 10'-0" north of Column Line 18A north to a line 17'-0" north of Column Line 23.

Omit the installation of the two (2) six inch Type "Z" drains and place them in attic stock.

Submit for our consideration prices which affect the Contract Price.

 JHe:js

cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

120-5-18-92
15 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Ornamental and Miscellaneous Metal

Gentlemen:

Please refer to the enclosed Drawing No. HGP-56-4, Revision No. 1,
dated 15 October 1951.

You will note we have added 1-1/2" diameter holes in the 4" channels
which occur in the booth walls, running horizontally about four (4)
inches above the finish floor.

In Booths 313, 314, 315, 316 and 317 these holes shall be located
2'-8" each side of the center line of the sash. The center line
of the holes shall be located 2-1/2" from the Booth side face
(inside) of the channel.

The above should cause no change to the Contract Price and you shall
proceed accordingly.

JJHe:js/JS
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod
Ryer

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

120-5-18-9
15 November 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York


Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Heating, Ventilating, Air Conditioning

Gentlemen:

On 5 November 1951 we forwarded you twenty-one (21) copies of Drawing SK-GA-H7-3, the revision to the mushroom layout in the public seating area at Elevation 70'-0".

This revision should cause no change to the Contract Price. Proceed with the installation of this work if you agree with this statement, if not promptly notify us of your findings in order that we may inform you how to proceed.

JJHe:jz *JJH*
cc: Bohanon *JS*
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod
Ryer
Hannegan
Rumpelstin
S & H-2



Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

120-5-18-9
15 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Miscellaneous Changes - Revision No. 51


Gentlemen:

As of even date we are forwarding you twenty-five (25) copies
of the following drawings and Bulletin of Changes for Revision
No. 51: A-5, A-102, A-103, RA-106-B, A-111, RA-141, RA-145,
RA-158, RA-172.

You are to proceed with all of the work indicated on the
above drawings. There should be no change to the Contract
Price with the exception of the following two items indicated
on the Bulletin of Changes:

Item 1 of Drawing RA-106-B
Item 2 of Drawing RA-172.

Submit for our consideration prices which affect the Contract
Price.

 JJHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod
Ryer

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

120-5-18-9
15 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York


Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Structural Steel - Field Change

Gentlemen:

On 15 November 1951 we forwarded you twenty-five (25) copies
of Drawing GA-4-CS-34 dated 14 November 1951.

These prints are for your records. The work shown thereon is a steel
field change, the cutting of and reinforcing of two holes. There
should be no addition to any work by the construction trades.

Proceed with the work indicated thereon.

 JJHe:js

cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod
Ryer

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

120-5-18-7
15 November 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Plumbing

Gentlemen:

On 7 November 1951 we forwarded you twenty-one (21) copies of Drawing SK-GA-P4-2 dated 2 November 1951, the layout of the drains at Column 31 for the exterior balcony.

Proceed with the installation of this work and submit for our consideration prices which affect the Contract Price.

JJH:js

cc: Bohanon

Nelson

Healy-2

Harris

Hopper

Zunser

VanName

McLeod

Ryer

Hannegan

S & H-2

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

15 November 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Concrete

Gentlemen:

On 13 November 1951 we forwarded you twenty-five (25) copies
of Drawing GA-S-35, Revision No. 8, dated 12 November 1951.

Proceed with the work indicated thereon and submit for our
consideration prices which affect the Contract Price.

JJHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod
Ryer

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 11, 1951

Mr. James A. Dawson
Co Ordinator of Construction
Headquarters Planning Office
Room 2272, United Nations
New York 17, New York

Re: General Ass'y. & North Parking, Cont. HQ 1/82

Dear Sir:


We are attaching hereto three (3) signed copies each of
the following Change Orders:-

#8 - Addition - Atlantic Metal Prod., Inc. - \$46.00
#8 - Addition - Eugene Duklauer, Inc. - \$760.71

General Ass'y. & North Parking Contract.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



H. A. Hiener
Office Manager

HAH:vg
encls.



FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

November 14, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 331 - Copper Flashing in Lieu of Fabric on West Podium Wall

References: (a) U. N. Drawing SK-679, dated October 11, 1951
(b) FTWS, INC.'s Notification of Change No. 76, dated November 5, 1951
(c) Mr. James A. Dawson's letter of November 9, 1951

Dear Mr. Dawson:

On October 15, 1951 we received prints of Reference (a) which showed a modification of the previous drawing SK-665. This modification changes the original fabric flashing shown under the coping of the West Podium Wall to lead coated copper.

On November 5, 1951 we sent you our Notification of Change No. 76, Reference (b) which gave an approximation of the added cost involved in this modification.

On November 13, 1951 we received your approval letter, Reference (c), which reads in part as follows:

"This approval is given for you to proceed with the work required by the modification with reference to revision to Section-AA of Sketch #665."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the Contract Price and Contract Time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,
FULLER-TURNER-WALSH-SLATTERY, INC.

[Signature]
J. J. Grogan
Project Manager

MJG/PDV/em

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

November 14, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 325 - Revised Ventilation in Public Seating Area

References: (a) U. N. Drawing SK-GA-H7-3, dated October 25, 1951
(b) Mr. James A. Dawson's letter of November 8, 1951

Dear Mr. Dawson:

On November 5, 1951 we received prints of Reference (a).

On November 8, 1951 we received your transmittal letter, Reference (b), which reads in part as follows:

"On 5 November 1951 we forwarded you twenty-one (21) copies of Drawing SK-GA-H7-3 dated 25 October 1951, the revision to the Mushroom Type Ventilation for the Public Seating in the Assembly Hall.

"As per the advice of our mechanical engineers there should be no change in the Contract Price.

"Proceed with the work indicated thereon."

We have sent the above-referenced drawing to the interested subcontractors with the request that they advise us if this revision affects their sub-contract price.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/em

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

November 14, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Garage -
CHANGE NO. 323 - Architectural Revision #49 - dated 11/2/51

References: (a) List of Drawings included in Attachment
(b) Bulletin of Changes - Revision #49 - dated 11/2/51
(c) Mr. James A. Dawson's letter 9 November 1951

Dear Mr. Dawson:

On November 7, 1951 we received the Drawings and Bulletin listed in References (a) and (b) and on November 13, 1951 we received your transmittal letter, Reference (c), which reads **in part as follows:**

"Nothing indicated on the above documents should cause any change to the Contract Price with the exception of Item No. 6, Drawing RA-175, shown on Page 2, Bulletin of Changes.

Proceed with the work and submit for our consideration prices which affect the Contract Price."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/eas

LIST OF DRAWINGS - REFERENCE (a) - CHANGE NO. 323

RA-170)
RA-171)
RA-172)
RA-173)
RA-174)
RA-175)

Rev. No. 49 - dated 11/2/51

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y. November 14, 1951

file

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Garage -
CHANGE NO. 320 - Architectural Revision No. 47, dated 10/30/51

- References:
- (a) List of Drawings included in Attachment
 - (b) Bulletin of Changes - Rev. #47, dated 10/30/51
 - (c) Specifications, Picture Sheet, Hoist and Booms for U.N. General Assembly Building, dated 8/21/51
 - (d) Specifications for Shutter and Shutter Mechanism in Eye of Dome, dated 10/30/51
 - (e) Mr. James A. Dawson's letter 1 November 1951 to FTWS, Inc.

Dear Mr. Dawson:

On October 31, 1951 we received the Drawings, Bulletins and Specifications listed in the above references. On November 5, 1951 we received your transmittal letter, Reference (e), which reads as follows:

"Proceed with the work indicated on all of the above drawings. There should be no change to the Contract Price caused by any of the items except the following found on the Bulletin of Changes:

Drawing RA-105, Item 2
" RA-128, Item 3
" RA-149, Item 1
" RA-147, Items 1 and 2

As per instructions given to your Mr. P. DelVecchio by our Mr. J. J. Healy, please have Joseph Vasconcellos, Inc., 43-15 Dutchkille Street, Long Island City 1, N.Y., perform the subcontract work for the Picture Sheet Hoist and Boom and the Sliding Shutter and Shutter Mechanism for the Glass Eye of the Dome.

Submit for our consideration prices which will affect the Contract Price."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed Estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,
FULLER-TURNER-WALSH-SLATTERY, INC.
M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/eas

List of Drawings - Reference (a) - CHANGE NO. 320

A-16	RA-136A
RA-105	RA-136B
A-112	RA-136C
A-113	RA-147
A-114	RA-149
RA-126	RA-150A
RA-127A	RA-153
RA-128	RA-155
A-131	RA-164
RA-136	

Revision No. 47 - dated 10/30/51

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

November 14, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 308 - Replacement Lights of Photosensitive Glass for the
North Wall

References: (a) U. N. Drawing DSK-441, dated October 10, 1951
(b) Mr. James A. Dawson's letter, dated October 11, 1951
(c) U. N. Drawing DSK-441, revised October 16, 1951
(d) U. N. Drawing DSK-447, dated October 18, 1951
(e) FTWS, INC.'s letter (C. E. Reese) to Mr. James A. Dawson, dated October 22, 1951
(f) Mr. James A. Dawson's letter, dated November 8, 1951

Dear Mr. Dawson:

On October 11, 1951 we received prints of Reference (a) which show the scale detail of the arrangements of the photosensitive glass pattern on the North Wall of the General Assembly. This drawing also indicates that you require 86 spare lights of glass to be turned over to you for possible future breakage.

On October 15, 1951 we received your transmittal letter, Reference (b), which reads in part as follows:

"We assume that there is an over-run or an allowance for breakage, etc. of 10% included in the Contract Price."

Our letter, Reference (e), explains that we had made a monetary allowance of Four Hundred Dollars (\$400.00) to take care of possible breakage, during erection only, in our Estimate for Change No. 83. We were advised by Mr. Healy, however, that you require 86 spare lights to be turned over to you for replacement of breakage, after the building is completed.

On November 5, 1951 we received prints of References (c) and (d). These revised details show a new arrangement of the glass pattern on the North Wall and also increase the number of spares you require from 86 to 87.

continued.....

Mr. James A. Dawson

-2-

November 14, 1951
CHANGE NO. 308

Your transmittal letter of November 8, 1951, Reference (f) reads as follows:

"These drawings are a modification of the drawings for the manufacture and installation of the photosensitive glass. You are to proceed according to the information contained thereon.

"There should be no change to the Contract Price."

However, since the number of spare lights has been increased by these revised drawings, it is obvious that these later details will entail a change in price.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/em

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

November 14, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 267-B - Architectural Revisions, dated August 24, 1951

Reference: (a) Mr. M. M. Harris' Verbal Instructions of November 13, 1951

Dear Mr. Dawson:

This change is supplemental to our Change No. 267, dated September 21, 1951 and Change No. 267-A, dated October 4, 1951.

In our Change No. 267-A you advised us to proceed with a change in railing design for the Assembly Hall, based upon the wood material for the railing being furnished by the Union of South Africa.

On November 13, 1951, however, Mr. Harris advised us that the lumber for the railings was not to be furnished by this member Nation but was to be furnished by the Murray Hill Woodworking Corp., as part of this change.

The veneer to be used is ~~to be~~ Yellow Narra to match the wood being furnished by the Philippine Government for the batten wall of the Assembly Hall.

We will take these supplemental instructions into account in preparing our Estimate for Change No. 267.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/em

FULLER - TURNER - WALSH - SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 14, 1951

*copy to Mr. Dawson
Nelly C.O.
copy to Harris
Healy
Hypen*

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General
Assembly and North Parking
Garage -
Ornamental Metal

Dear Mr. Dawson:

We are enclosing herewith a copy of our Mr. DelVecchio's report on his inspection of the status of fabrication of the frames for the North Wall of the General Assembly.

As is apparent from the report, we may not expect complete delivery of this item until well into January, 1952 and completion of erection possibly three weeks later.

You will note that, if we authorize General Bronze Corp. to work overtime, we will have the sash delivered complete before Christmas and erection completed immediately after the first of the year. If we do not, however, the premium time costs will be more than overcome in temporary enclosure of the North Wall.

We are also enclosing herewith a chronological survey of the numerous changes which this facade has undergone. It is apparent from this chronology that the revisions to the North Wall were vigorously followed and prosecuted by both ourselves and General Bronze Corp.

We strongly recommend that we be allowed to instruct General Bronze Corp. to work overtime on this item, so that we may attempt to close in the General Assembly Building this winter, in enough time to complete the interior work on schedule.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
Project Manager



CHRONOLOGY OF CHANGES TO NORTH WALL DETAILS

GENERAL ASSEMBLY BUILDING

- 5/15/50 Contract Drawing A-109 - details North Wall Sash for Translucent Marble.
- 8/21/50 Revision No. 1, Drawing A-109, amplifies details of Sash for North Wall with Translucent Marble.
- 1/8/51 Revision No. 11, Drawing A-109, changed Translucent Marble to Photosensitive Glass. Removed column furring which changed detail of jamb trim on Sash.
- 3/7/51 Revision No. 15, Drawing A-109, changed detail of sill and size of rebate from 1/2" to 5/8". Changed spacing of joints in joint trim.
- 5/27/51 Revision No. 21, Drawing A-109, reinstated column furring and changed size of muntin at sill.
- 5/17/51 General Bronze shop details No. 24 and 25 approved by United Nations.
- 6/29/51 At request of United Nations, Fuller-Turner-Walsh-Slaterry, Inc. advised General Bronze to "HOLD" North Wall pending wholesale revision to entire facade.
- 7/16/51 U.N. Drawings DSK-415 and DSK-417 sent to General Bronze releasing "HOLD", but advising them not to proceed with revisions shown until price was accepted by United Nations (Fuller-Turner-Walsh-Slaterry, Inc. Request for Price No. 45). This revision showed omission of Canopy No. 1 and Vestibule No. 1 and addition of typical sash where Canopy was omitted.
- 7/23/51 Mr. M. M. Harris of United Nations advised Fuller-Turner-Walsh-Slaterry, Inc. that omission of Canopy and Vestibule No. 1 was accepted and to proceed with change (Fuller-Turner-Walsh-Slaterry, Inc. Change No. 243).
- 7/24/51 Fuller-Turner-Walsh-Slaterry, Inc. letter to all subs advising them to use DSK-415 and DSK-417 (Change No. 243).
- 8/9/51 United Nations issued SK-668 showing addition of Special Door No. 160 in North Wall where Canopy No. 1 was omitted. Changes sash requirements and details in this area.
- 9/5/51 United Nations issued SK-670, revised shape of North columns, removes column furring again, revises details of sash. (Fuller-Turner-Walsh-Slaterry, Inc. Request for Price No. 54).
- 9/24/51 United Nations issued SK-673, voiding SK-670, reverts to original concrete fireproofing details - omits plaster and furring on columns. Advised to proceed with Change (Fuller-Turner-Walsh-Slaterry, Inc. Change No. 290).
- 10/17/51 On verbal advise of Messrs. Healy and Nelson, Fuller-Turner-Walsh-Slaterry, Inc. advised General Bronze Corp. that details of Door No. 160 (SK-668) OK for construction.

CHRONOLOGY OF CHANGES TO NORTH WALL DETAILS - GENERAL ASSEMBLY BLDG. (cont'd)

- 10/19/51 General Bronze Corp. revised details of North Wall received.
- 10/26/51 General Bronze Corp. revised details of North Wall approved by United Nations.
- 10/30/51 United Nations verbally advised hardware requirements for Special Door.

INTER-BRANCH COMMUNICATION

November 13 19 51

Report of Inspection of

TO Mr. Grogan

REGARDING General Bronze Corp.'s Work
on North Wall Enframement of General Assembly

On November 12, 1951 Mr. Cantey and the undersigned discussed with the following people in General Bronze Corp. the status of fabrication of the frames of the North Wall of the General Assembly Building:

Mr. W. Wilson - Chief of Production
Mr. F. Groiss - Assistant Chief of Production
Mr. J. Leonard - Shop Superintendent
Mr. L. Horvath - In Charge of Materials and Bent Shapes
Mr. F. Seibert - In Charge of Assembly

Concerning the status of fabrications (see attached sketch) there are two major assemblies involved in this frame; the muntin (approximately 3900 lineal feet required) and jamb trim (approximately 3500 lineal feet required). The status of fabrication of the muntin is as follows:

1. The lower stainless steel angle has been completely cut and bent.
2. The upper stainless steel tee has been cut, but not bent. Bending operations on this member were starting on November 12, 1951.
3. The intermediate stainless steel bar has been approximately 30% cut to length and all the bars remain to be notched out for fitting to the jamb.
4. The 16-gauge plain steel glass stop has been completely cut and bent but has yet to be drilled for the attachment screws.

Concerning fabrication of the jamb trim, the stainless steel angle has been cut but not bent, as has the plain steel jamb trim. No other work has been done on this assembly to date.

At present General Bronze Corp.'s shop facilities have been devoted to cutting and bending material only which involved a force of four to six men. After bending operations are complete, approximately November 16, 1951, Mr. Wilson advises that a complete assembly area will be devoted to this job, using approximately ten to fifteen men.

At present General Bronze Corp. has not expended any premium time in completing the work. There are approximately 3700 man hours left to complete this item, which would indicate that we would get partial delivery on or about December 15, 1951, and complete delivery about January 22, 1952. However, if we can authorize General Bronze Corp. to expend 700 man hours of premium time, starting on the weekend of November 16, 1951, Mr. Wilson states that we can expect first delivery approximately December 6, 1951 and completion about December 22, 1951. Mr. Wilson feels that this time saving on the completed item can be affected by avoiding work through the Christmas and New Year holidays and further feels that the psychological impetus given to his men on account of the overtime would also expedite completion of the job.

Mr. Grogan

-2-


November 13, 1951

re: Inspection Report 1/82 - General Bronze Corp.


These 700 hours of premium time would include two hours daily and eight hours each Saturday and Sunday, Based on a cost of \$2.00 plus insurances, Mr. Wilson made a quick estimate of cost to be in the neighborhood of \$1,500.00 to \$2,000.00.

Mr. Wilson would like a quick decision on this authorization to expend premium time.

P. DelVecchio /s/

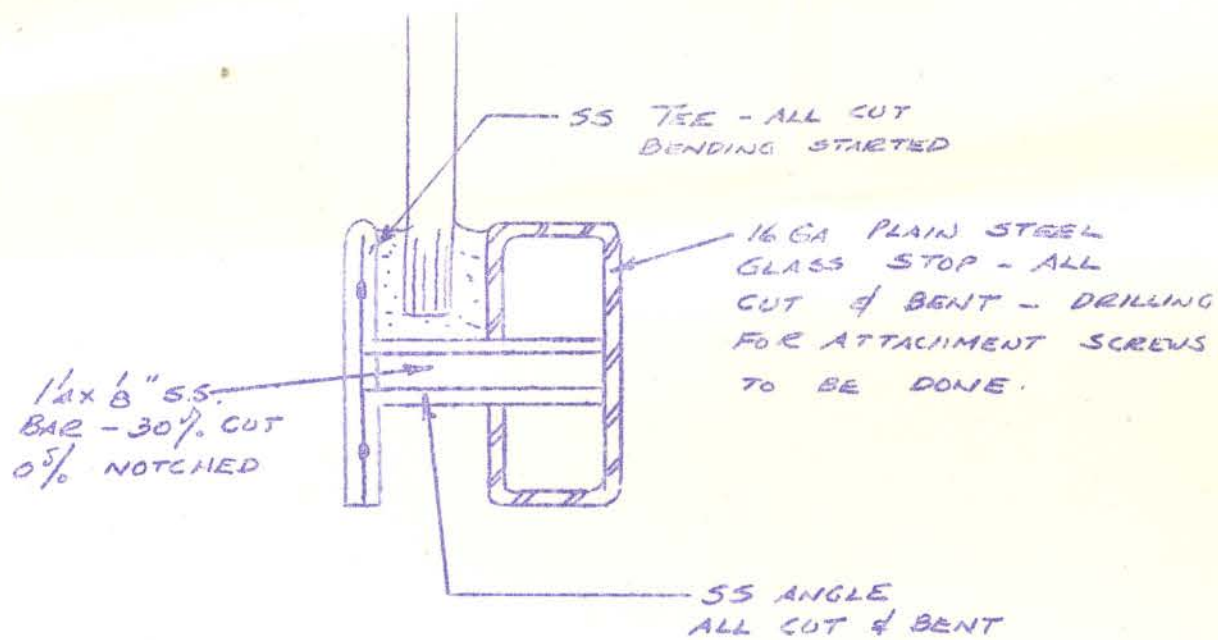

TYPICAL MUNTIN ASSEMBLY

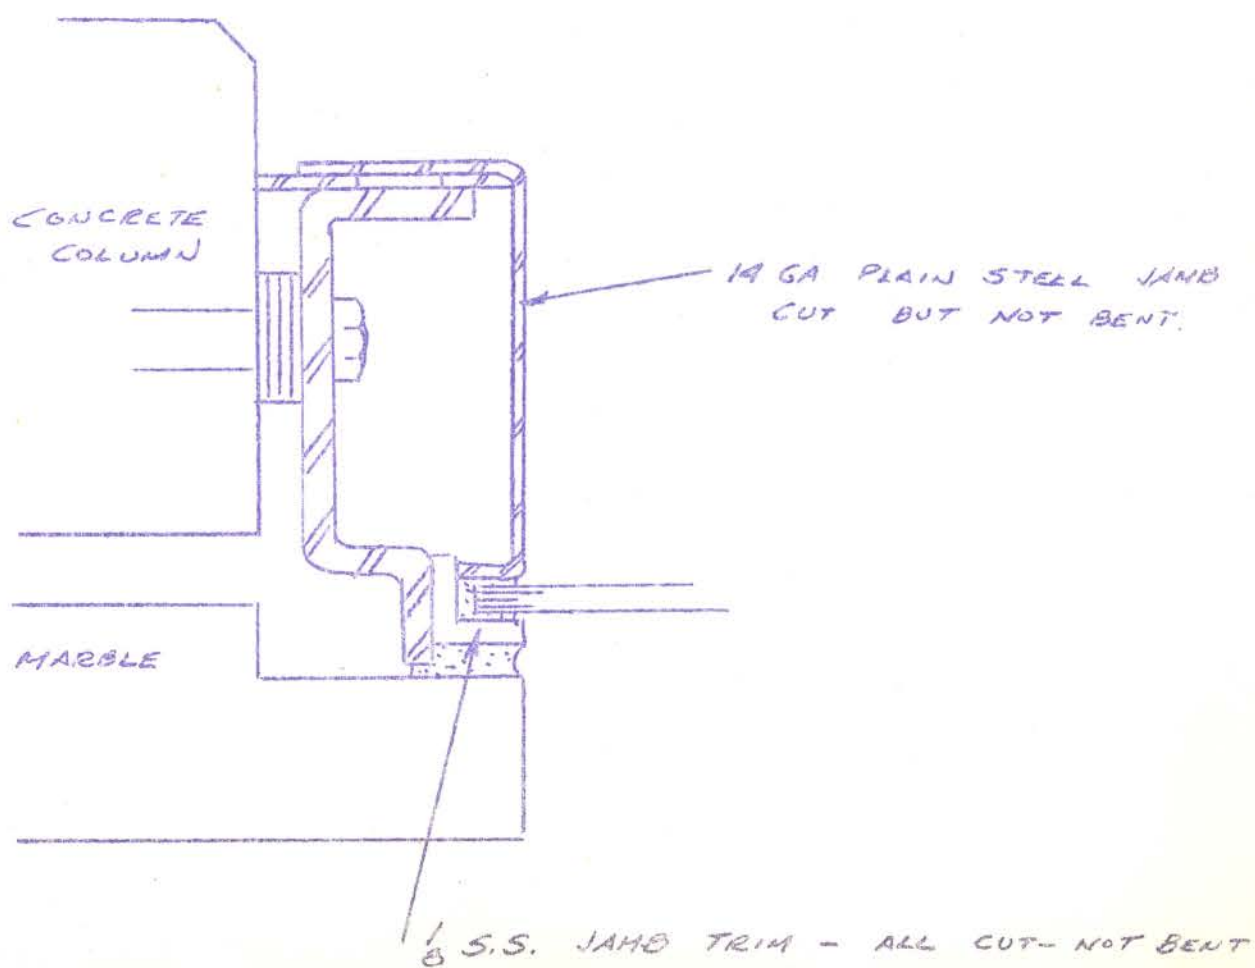

TYPICAL JAMB ASSEMBLY

120-5-18-9 ✓
cc: Harrison
McLeod
Zunser*
Van Name
Hopper
Healy

14 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, N.Y.

Re: Contract HQ 1/82 - General Assembly
and North Parking Garage - Notification
of Change No. 75 (Change No. 243) -
Omission of Canopy No. 1 and Vestibule
No. 1 complete with all Doors and Frames -
Add Special Door-North Public Lobby per
Dwg. SK-668 dated 8/9/51

Gentlemen:

Attached hereto is one copy of Notification of Change No. 75 (Change No. 243) approved by James A. Dawson for the United Nations.

This approval is given for you to proceed with the work required by the modification with reference to omission of canopy No. 1 and vestibule No. 1 complete with all doors and frames and the addition of special door-north public lobby per drawing SK-668 dated 8/9/51.

It is understood that this approval does not include the cost of this change as indicated in the Notification of Change No. 75, which is solely an approximation. It is understood, also, that the actual price adjustment will be made as required by the terms of the contract.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

Enclosure

JZ:eh

120-5-189
14 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Change No. 320
Motion Picture Boom and Light Shutter
in Dome

Gentlemen:

We have at hand your letter of 12 November 1951 with the various prices for the above subject items listed thereon and in the last paragraph of which you request our comments and/or approval of these quotations in order that you may proceed with the work.

We have contacted Mr. W. A. Baerenklau of Joseph Vasconcellos, Inc. reference this amount of \$6,574.92 and he has stated that Joseph Vasconcellos, Inc. will take the job at no more than \$6,000.00.

Our Mr. J. J. Healy has informed your Mr. P. DelVecchio reference this and we hereby approve Joseph Vasconcellos, Inc., 43-15 Dutchkills Street, Long Island City, N. Y., as sub-contractor for the Motion Picture Boom and Light Shutter in the Dome at the \$6,000.00 price.

JJHe:js

cc: Bohanon

Nelson

Healy-2

Harris

Hopper

Zunser

VanName

McLeod -

Hannegan

Seelman

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

14 November 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Heating, Ventilating, Air Conditioning


Gentlemen:

Please proceed with the omission of the following items:

Six (6) 56 square foot wall hung radiators at Landings
of Stairs Nos. 5, 7, 32, 3, 27, 29 and 8.

These radiators are shown on Drawing GA-H-3A. The pipes are to
be capped below the floor and the six radiators returned for
credit.

Submit for our consideration prices which will affect the Contract
Price.



JJHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
Van Name
McLeod
Hannegan
Rumpelstin
S & H-2

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

**opper
ready*

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Healy

November 13, 1951

General F.H.

Mr. James A. Dawson
Vo-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General
Assembly and North Parking
Garage -
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawing, submitted by General Bronze Corp. & C.E. Halback & Co.

HGP-49-14 rev. 11/12/51 Steel & Glass Screens
407, 408, 409, 412, 413, 414
G. M.

Will you please return two (2) prints each of the above drawings, with your approval and/or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C.E. Reese

C. E. Reese
Project Engineer

CER/MH/eas



Hopper
Healy

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Healy
General File

November 13, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General
Assembly and North Parking
Garage - (GENERAL ASSEMBLY)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawings submitted by Genral Bronze Corp. & C.E. Halback & Co.:

HGP-25-1 11/7/51 Iron Railing & Framing at Press
Lounge Balcony

HGP-97-1 rev. 11/12/51 Supports for Railings

Drawing HGP-97-1 was previously approved by you on 9/7/51. Since then several dimensional errors have become apparent and a copy of the approved drawing was marked-up by your Mr. Van Riper, with a request for resubmittal of the present corrected drawing.

Will you please return two (2) prints each of the above drawings, marked with your approval and/or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/eas



ISSUANCE OF DRAWINGS

OFFICE COPY

13 November 1951

21 November 1951

QA & North Parking

Fuller-Turner-Walsh-Slattery

hand


Submitted by General Bronze & Halback

2 HGP-97-1 2 Aug'51 Supports for Railings

(APPROVED WITH NOTES IN WHITE 19 Nov 1951 REN)

NOTE: Dwg. HGP-25-1 will follow

See Letter dated 13 Nov. 1951



SV Tyler

ISSUANCE OF DRAWINGS

OFFICE COPY

13 November 1951


4 December 1951

CA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by General Bronze & Halback

2 HGP-25-1 7 Nov '51 Iron Railing & Framing at Press Lounge Balcony
(APPROVED AS NOTED 3 Dec 1951 VR RESUBM.)



*See Hopper-Rumpfella
Hopper-Hammegau
11/14/51*

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Tyler

November 13, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

Gen Files

re: Contract HQ 1/82 @ General
Assembly and North Parking
Garage -
Shop Drawings for Approval
Kerby Saunders, Inc. (Nat'l. Sheet Met. Wks)

Dear Mr. Dawson:

We are submitting herewith, for your approval, six (6) copies of the following shop drawings prepared by the National Sheet Metal Works, Inc., Subcontractor to Kerby Saunders, Inc.

GA-RS-3	Ductwork Riser W/Wall Columns	28-30
GA-1-5	Ductwork - 1st floor Col. J-L	24-28
GA-1-4	" " " M to wall	24-28


We ask that you review these drawings and return three (3) each to this office, as soon as possible, with your approval and/or comments. Please note that insofar as it is possible trade clearances have been taken care of.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER/CWB/eas



ISSUANCE OF DRAWINGS

OFFICE COPY

13 November 1951

29 November 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Kerby Saunders (Nat'l Sheet Metal Dwgs.

3	GA-RJ-3	3 Oct '51	Ductwork Riser W/Wall Cols. 28-30
3	GA-1-5	5 Sept '51	" 1st Fl. Col. J-L-24-28
3	GA-1-4	9 Aug '51	" " " " H to wall 24-28

(ALL APPROVED 28 Nov 1951 REM)

NOTE: FROM SYSKA & HENNESSY

"These drawings are approved."

"All approvals are subject to strict compliance with the Contract Plans and Specifications and to all Authorities having Jurisdiction."

RECEIVED

NOV 29 1951

FULLER-TURNER-WALSH-SLATTERY
INCORPORATED

S. V. Tyler

FULLER-TURNER-WALSH-SLATTERY, INC.
 UNITED NATIONS CONTRACT
 403 EAST 42ND STREET
 NEW YORK 17, N. Y.

November 13, 1951

Mr. James A. Dawson
 Co-Ordinator of Construction
 Headquarters Planning Office
 Room 2272 - United Nations
 New York, N.Y.

re: Contract HQ 1/82 - General Assembly
 and North Parking Garage -
Reinforcing Steel Dwgs.

Dear Mr. Dawson:

We are sending you herewith six (6) prints of the following Reinforcing Steel shop drawings submitted by Brennan & Sloan, Inc.

605 11/2/51 Plan showing Special Reinforcing around Duct
 Holes - Part. 4th floor - El. 83'-0" & 86'-0"

Will you please return three (3) prints each of the above drawings, marked with your approval and/or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
 C. E. Reese
 Project Engineer

DER/BK/eas



ISSUANCE OF DRAWINGS

OFFICE COPY

13 November 1951

13 December 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Brennan & Sloan & Knickerbocker

2 605 2 Nov'51 Special Reinf. around Duct Holes etc.
(UNSATISFACTORY 11 Dec 1951 REW RESUBMIT)



L v Syle

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 13, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General
Assembly and North Parking
Garage -
Change No. 278-Ornamental Metal

Dear Mr. Dawson:

On September 7, 1951 Mr. J. Zunser authorized us to modify the aluminum sash on the south wall of the General Assembly to suit the existing conditions of the structural steel mullions.

At that time, it was agreed that any gap between the aluminum and steel mullion would be inspected by you to determine if you would require a mullion cover.

Please be advised that General Bronze's work in this location is substantially complete and we expect to start glazing during the week of November 19, 1951.

Will you please examine this work and advise us if you require the mullion covers. These should be installed, if required, before the sash is glazed.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/PDV/eas



*Any tags after check in
Hopper
Manville in comment quickly.*

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

General File.

November 13, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space
Acoustical Treatment

Dear Mr. Dawson:

We have not installed the metal pan ceilings in the Recording Rooms and Control Rooms adjacent to Studios Nos. 5 to 9 inclusive because of possible damage to the metal pans which may be caused by the moist conditions of these spaces.

of
Your Mr. W. Hopper, however, has advised us that because/your communications requirements, it will be necessary for us to install these ceilings as soon as possible.

Consequently, upon Mr. Hopper's instructions, we are instructing Johns-Manville Sales Corp. to install these pan ceilings, with the understanding that any damage sustained by the ceilings, due to moisture, will not be the responsibility of Johns-Manville Sales Corp.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/PDV/em

cy: Johns-Manville Sales Corp.



Can. File

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 19, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Space
ESTIMATE FOR CHANGE NO. 214 - April 4, 1951 Architectural Revisions

- References:
- (a) U.N. letter (Dawson) to FTWS, Inc. dated 4/6/51
 - (b) " " " " " " " 7/6/51
 - (c) FTWS, Inc. letter (Grogan) to U.N., dated 7/13/51
 - (d) U.N. Bulletin of Changes, Rev. No. 23, dated 4/4/51
 - (e) U.N. Dwg. CA-9 and RA-139A, dated 4/4/51, as compared with Contract Documents
 - (f) U.N. Dwg. RA-110, rev. 4/4/51, as compared with the same drawing dated 1/8/51
 - (g) U.N. Dwg. RA-160, rev. 4/4/51, as compared with the same drawing dated 3/14/51
 - (h) U.N. Dwg. RA-158, RA-160A, RA-161, RA-161A, RA-163 and RA-163A, all dated 4/4/51, as compared with Dwg. A-4, A-5, A-6, dated 3/7/51 and Dwg. A-16, dated 8/21/50.

Dear Mr. Dawson:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we hereby offer a DECREASE in our total guaranteed maximum cost price in the amount of TWO HUNDRED EIGHTY-TWO AND 61/100 DOLLARS (\$282.61), for work itemized in this Estimate as required by the above references.

This Estimate does not include the following:

- a) Electrical or Mechanical Changes.
- b) Any change in Catwalk requirements, Dwg. RA-9.
- c) General Bronze Corp. does not include grilles shown on Dwg. Nos. RA-160A, RA-161, RA-161A, RA-163 and RA-163A.
- d) 1/4" Tempered Glass Dwg. RA-110 (has always been 1/4" P.P. Change #1, Rev. #1, left as 1/4" P.B. this Estimate).

The above price is broken down as follows:

I Spec. PART IV, Section 19 - TERRAZZO	Add	Deduct
(DeiTurco Bros.)		
Omit 302 L.F. of Base @ \$1.17/L.F.		\$353.34
NET DEDUCTION		\$353.34

Continued

Mr. James . Dawson

-2-

November 19, 1951

re: Contract HQ 1/82 - ESTIMATE FOR CHANGE NO. 214

	<u>Add</u>	<u>Deduct</u>
NET DEDUCTION Brt. fwd.		\$353.34
II <u>Spec. PART IV - Section 20 - PLASTERING</u> (T.M.O'Rourke, Inc.)		
Screed for A.T. Base 750 L.F. @ .20/LF	\$150.00	
15% O.& P.	22.50	
NET ADDITION	\$172.50	
III <u>Spec. PART IV - Section 21 - FURRING & LATHING</u> (Jeremiah Burns, Inc.)		
Add F.&L. Heads of Telephone Booths		
17 L.F. @ \$2.00/LF	\$ 34.00	
Add Plaster Stop 402 LF @ 0.35/LF	140.70	
	174.70	
15% O.& P.	26.21	
NET ADDITION	\$200.91	
IV <u>Spec. PART IV - Section 23 - WOODWORK</u> (Murray Hill Woodworking Corp.)		
Add Dwg. Rm-158 Col. I 27-28 - 39 LF Mldg. G rds.		
" Q 27-28 39 " "		
78 " "		
@ 1.13/LF	88.14	
Omit Wood Base 563 LF @ .913/LF		514.02
	88.14	514.02
		88.14
NET DEDUCTION		425.88
V <u>Spec. PART IV - Section 26 - PAINTING</u> (The Shatz Painting Co., Inc.)		
Omit Painting Woodbase 563 LF @ .06/LF		33.78
NET DEDUCTION		33.78
VI <u>Spec. PART IV - Section 28 - RESELIANT FLOOR COVERING</u> (Newell, Orr & Walsh, Inc.)		
Add A.T. Base 750 LF @ .182/LF	136.50	
15% O. & P.	20.48	
NET ADDITION	\$156.98	
(Carried fwd.)	\$530.39	813.00

Continued

Mr. James A. Dawson

-3-

November 19, 1951


re: Contract HQ 1/82 - ESTIMATE FOR CHANGE NO. 214

<u>Add</u>	<u>Deduct</u>
\$530.39	\$813.00
	<u>530.39</u>
<u>TOTAL DEDUCTION</u>	282.61

Will you kindly issue a Change Order - DEDUCTION, in the amount of \$282.61 for the work itemized above.

Very truly yours,

FULLER-TURNER-WILSH-SLATTERY, INC.


M. J. Grogan
Project Manager

MJG/CER/eas

1

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 17, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General
Assembly and North Parking
Garage -
Change No. 215 - Acoustical
Treatment

Dear Mr. Dawson:

In Revision #27 (Change No. 215) you changed the finish schedule for the corridors and booth ceilings adjacent to the Committee Rooms so that the ceiling material was changed from Perforated Metal Pan (Sanacoustic) to Perforated Acoustical Tile (Fibre-tone).

In Revision #29 the details of drawings A-121 and 122 were changed to conform with this change in ceiling material.

When the detailed drawings were revised, however, an 18-gauge metal casing between the ceiling and the wall, which was originally required for the metal pan ceiling, was retained for use with the perforated acoustical tile ceiling.

Johns-Manville Sales Corporation has advised us that they do not believe that this type construction is good practice with a cemented-up tile whereas it is necessary with a metal pan ceiling.

Subsequently, we have been advised by you to change the perforated acoustical tile ceilings in this location to fissured acoustical tile and Johns-Manville feels that the 18-gauge metal casing is not required for this material either.

In our Change Estimate for Change No. 215 we will not include the cost of furnishing or installing the metal edge channels at the intersection of the acoustical tile on the walls.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/PDV/eas

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

September 17, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations,
New York

Re: Contract HQ 1/82-General Assembly
and North Parking Space
Cut Stone

Dear Mr. Dawson:

As discussed in Mr. Glenn E. Bennett's office on September 13, 1951, we are enclosing Monahan-McCann's stone order No. 19 covering the requirements for the East and West Podium wall copings, which have been added to the contract since the original orders were placed.

It was felt originally that the material for these two copings could be obtained from the extra blocks ordered for replacement of slab breakage. However, as you will note on the attached tabulation, the breakage, to date, has exceeded the extra blocks ordered.

The measurements indicated on the blocks listed in the attached order are net requirements upon which payment will be made, but Manor Limestone is to ship blocks 3" longer, 3" wider and 3" deeper to allow for saw cuts and spalls. Each block is to be identified in black paint with the mark number. Blocks are to be scabbled or sawed.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER:PDV:tw



1 to 5 to 6 to 11

Net Cube of Stone on Order
 Less Blocks Ordered for Breakage
 Less Blocks in McCann's Order

1158'-0"
 323'-9"
1481'-9"

22127'-9"

Contract Net Requirements
 E. Podium Wall Coping - Not Ordered
 W. Podium Wall Coping - Not Ordered
Revised Net Requirements

20648'-0"
 421'-0"
 235'-0"
21304'-0"

Slabs Shipped from England
 Purchased Locally
 Slabs Delivered

17834'-1"
 631'-0"
18465'-1"

Less Breakage 1575'-3"
 Less "Not to Size" 428'-8"
2003'-11"

Usable Slabs
 Blocks Shipped from England

16461'-2"
 5135'-3"
21596'-5"

Less Allow. for Saw Cuts (20%)

1016'-0"
20580'-5"

Less Flawed Blocks to date

200'-0"
20380'-5"

Plus Slabs on PARTHIA

69'-4"
20449'-9"

Total Cube Available

20449'-9"

Deficit

854 CF*

Hopper
Healy

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Healy
General File

November 13, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
405 East 42nd Street
New York, N.Y.

re: Contract HQ 1/82 - General
Assembly and North Parking
Garage -
Carpentry & Millwork

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following Carpentry
and Millwork shop drawings, submitted by ~~General Bronze Corp., & C.E.~~
~~Halback & Co.:~~ **MURRAY HILL WOODWORKING**

320	11/7/51	F.S. Detail of Dressing Counters	1B135 & 304
306	rev. 11/10/51	Plan & Elevations - Conf. Rm.	#4
307	"	F.S. Details	" #4
308	"	West Elev.	" #4
309	"	East "	" #4

Will you please return two (2) prints each of the above drawings marked
with your approval and/or necessary corrections.


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C.E. Reese

C. E. Reese
Project Engineer

CER/MH/eas

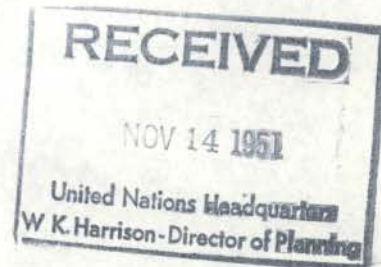

ISSUANCE OF DRAWINGS

OFFICE COPY

13 November 1951

21 November 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand


Submitted by Murray Hill Woodworking

2	306	12Mar'51	Plan & Elevs. - Conf. Rm. #4
2	307	"	F. S. Details " " "
2	308	"	West Elev. " " "
2	309	"	East " " " "

(ALL "APPROVED AS NOTED" 20 Nov 1951 JCB. RESUBMIT

NOTE: DWG. 320 will follow

See letter dated 13 Nov. 1951



SV Tyler

ISSUANCE OF DRAWINGS

OFFICE COPY

13 November 1951

11 December 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand


Submitted by Murray Hill Woodworking

2 320

7 Nov'51

F.S. Detail of Dressing Counters 1B135 & 304

(APPROVED AS NOTED 10 Dec 1951 A.D. RESUBMIT)



L V Tyler

120-5-18-9
13 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York


Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Heating, Ventilating, Air Conditioning
Ducts at North Columns in North Lobby
UNHPO Item GA-29

Gentlemen:

This will confirm verbal instructions by our Mr. M. Harris to your Mr. C. Bartley to proceed with the fabrication and installation of the ducts at the North Columns in No. 18 gauge steel. The slotted outlets shall also be 18 gauge.

This work shall be performed at the approximate addition in cost of \$2,400.00.

Submit for our consideration prices which affect the Contract Price.

 JJHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod
Hannegan
Rumpelstin
S & H-2

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

120-5-18-7
13 November 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York


Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Concrete

Gentlemen:

As of even date we are forwarding you twenty-five (25) copies of Drawing GA-3-CS-37 dated 12 November 1951, the structural detail of slabs below the windows in the east elevation between column lines 25 and 27.

You are to proceed with the work.

This slab has previously been shown on both Drawings RA-101 and GA-S-17-C. If there is a change to the Contract Price due to the different method of reinforcing and installing the slab, include this cost in Change No. 304.

 JJHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office



120-5-18-9
13 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Miscellaneous Iron and Concrete

Gentlemen:

As of even date we are forwarding you ten (10) copies of
Drawing SK-682 dated 13 November 1951.

This drawing is being issued that you may proceed with the fabri-
cation and installation of the anchorages for the metal railings
shown thereon. Information shown on this sketch and completed
details of the railings will be incorporated on Drawing RA-130B
to be issued.

This is an amplification drawing and you are to include the
cost of the items in the same Change Order as will be assigned
to N. C. No. 62 which was approved as per our letter to you dated
20 September 1951.

Very truly yours,

JHE:js

cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod
Ryer

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

120-5-18-7
13 November 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Concrete and Structural Steel

Gentlemen:

As of even date we are forwarding you twenty-five (25) copies
of Drawing GA-3-CS-36 dated 12 November 1951, the relocation
of brackets at the south cheek walls and cutting of beam flanges.

You are to proceed on a time and material basis and submit
for our consideration the prices which affect the Contract
Price.



JJHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod
Ryer

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

120-5-18-92
Then is too in our budget
Please what you can do to fix
the reduced and then reply to them
FULLER, TURNER - WALSH - SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

OREGON 9-3950

November 12, 1951

Mr. Dawson
Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly
and North Half Parking Space
CHANGE NO. 320
Motion Picture Boom and Light
Shutter in Dome

Dear Mr. Dawson:

In Revision No. 47 you sent us copies of drawings RA-147 and 149 plus specifications for the above-referenced items. In your letter of November 1, 1951 you requested that we take prices for these items from Joseph Vasconcellos, Inc. 43-15 Dutchkills Street, Long Island City, N. Y.

You also advised us to proceed with the work indicated in the drawings involved in Revision No. 47.

We have received the following quotations from Joseph Vasconcellos, Inc. for these items:

For the Motion Picture Boom

Material	\$4,178.00
Field Labor	726.00
Insurance	66.22
	<u>\$4,970.22</u>

For the Light Shutter:

Material	\$1,085.00
Field Labor	474.00
Insurance	45.70
	<u>\$1,604.70</u>

The total cost of these two items is, therefore \$6,574.92.

In order that we may initiate a contract with this firm it is requested that you give us your prior approval of these prices rather than wait for approval of the price after it is included in our estimate for Change No 320.

Mr. James A. Dawson

-2-

HQ 1/82-Nov. 12, 1951

Will you please let us have your comments and/or approval of these quotations so that we may know how to proceed with this work.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/PDV/em



Healy

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Mr. Healy
General File

November 12, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawing submitted by General Bronze Corp. and C. E. Halback & Company:

HGP-43-3 Rev. 11/9/51 Steel & Glass Rails -
West & East Elevations.

Will you please return two (2) prints of the above drawing marked with your approval or necessary corrections?

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/MH/em



ISSUANCE OF DRAWINGS

OFFICE COPY

12 November 1951

3 December 1951

GA & North Parking
Fuller-Turner-Walsh-Slattey

hand

Submitted by General Bronze & Halback

2 HGP-43-3 6 Aug '51

Steel & Glass Rails - West & East Elevs.

(APPROVED 30 Nov 1951 REN)



L. V. Tyler

Hopper
Healy

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Mr. Healy
General File

November 12, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawing submitted by General Bronze Corp. and C. E. Halback & Company:

HGP-46-2A Dtd. 11/8/51 Layout of Railing for Stair
36 - First Floor to Second
Floor.

Will you please return (2) prints of the above drawing marked with your approval or necessary corrections?

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C.E. Reese

C. E. Reese
Project Engineer

CER/MH/em



ISSUANCE OF DRAWINGS

OFFICE COPY

12 November 1951


3 December 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by General Bronze & Halback

2 HGP-46-2A 8 Nov '51 Layout of Railing for Stair 36 1st Fl. to 2nd Fl.
(APPROVED AS NOTED 28 Nov 1951 RWN RESUBMIT)



J V Tyler

*Let
Hopper-Rumpfeller
Henney
11/13
255*

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 12, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Gen file

Re: Contract HQ 1/82 - General Assembly
and North Half Parking Space
Grille & Diffuser Schedule - Heating,
Ventilating and Air Conditioning

Dear Mr. Dawson:

We are re-submitting for your approval six (6) copies of Grille & Diffuser Schedule, Part ~~II~~ for General Assembly. This revised schedule is dated October 31, 1951 and incorporates all Grilles and Diffusers on Syska & Hennessy's drawing GA-H2 and revised drawings SK-GA-H2-1, 2-3, 2-4, 2-5 and verbal changes made at Syska & Hennessy's field engineering office by Mr. E. Marshall.

It does not include items between Columns 29 to 24 & "Q" to one half way between "O" & "N". This ^{is} shown on Part I Schedule. It also includes Registers & Register Boxes for the North Half Parking Space.

We are especially anxious that you give a very quick approval of the special finishes on diffusers shown in the schedule so that plaster frames, etc. can be delivered to the job in time to keep up with the field progress. We, therefore, request that we be given a preliminary approval of the finishes, as shown in the special column of the schedule marked "finishes." We are confident that the sizes are correct, and when this approval is given we will immediately release them for fabrication. No fabricating (i. e., finishing) will be done until this approval is given.

Please return three (3) copies of this schedule to this office as soon as possible together with your approval and/or comments.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER/CWB/em



ISSUANCE OF DRAWINGS

OFFICE COPY

19 November 1951

20 November 1951

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Kerby Saunders (John B. Hewitt Schedule)

3

31 Oct '51


Grille & Diffuser Schedule Part II GA

(APPROVED AS NOTED 20 Nov 1951 REN RESUBMIT)

NOTE: FROM SYSKA & HENNESSY

"This drawing is approved, except as noted in red crayon."

"All approvals are subject to strict compliance with the Contract Plans and Specifications and to all Authorities having Jurisdiction."



SV Tyler

Hopper Healy

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Mr Healy

General Files

November 12, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General
Assembly and North Half
Parking Space (GA)
Cut Stone

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following Cut Stone shop drawing submitted by Monahan-McCann Stone Company:

788-5EZ Rev. 11/5/51 East Wall - Between Columns
25 - 27.

Will you please return two (2) prints of the above drawing marked with your approval or necessary corrections?

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

ECR/MH/em

NOV 12 1951

ISSUANCE OF DRAWINGS

OFFICE COPY

12 November 1951


21 November 1951

GA & North Parking
Fuller-Turner-Walsh-Slaterry

hand

Submitted by Monahan McGahey

2 788-5EZ 23Oct'51 East Wall- Between Cols. 25-27
(APPROVED 20 Nov 1951 JCB)



L v Gyle

ISSUANCE OF DRAWINGS

OFFICE COPY

13 November 1951

21 November 1951

GA & North Parking

Fuller-Turner-Walsh-Slaterry

hand

Submitted by General Bronze & Halback

2 HGP-49-14 17Aug'51 Steel & Glass Screens 407,408,409,412,413,414 /GM
(APPROVED 19 November 1951n REN)

RECEIVED

NOV 23 1951

FULLER-TURNER-WALSH-SLATTERY
INCORPORATED

See letter dated 13 Nov. 1951

JV Byler

12 November 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion of
Parking Garage - Contract HQ 1/82
Acoustical Treatment and Sound Conditioning
Change No. 227

Gentlemen:

Will you please have your sub-contractor install a white metal linoleum type binding strip in Conference Room No. 4 on the top sloped edge of the perforated transite board on the east and west walls from the light cove north of Column 27 to the sound lock doors. This edge molding shall be the width of each panel, i.e. 1'-11 7/8". This information has already been noted on Johns-Manville Shop Drawing No. 109 which was returned to you dated 1 November 1951.

Proceed with this work and include the cost in your breakdown of prices for Change No. 227.



JJHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

12 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Space - Contract HQ 1/82
Acoustical Treatment and Sound Conditioning

Gentlemen:

Since the United Kingdom is furnishing the wood panelling in Committee Room No. 7, the perforated transite and sound absorptive material behind the panelling will be deleted as per our letter to you dated 20 September 1951.

However, not all this sound absorptive material should be deleted. On Elevations "C" and "D" where the wood panelling will be perforated the sound absorptive material must be retained. See Johns-Manville Sales Corporation's Drawing No. 101 for location of Elevations "C" and "D". This drawing was returned to you marked "Approved as noted and resubmit" dated 29 October 1951.

In submitting your breakdown of prices for the above, take into consideration the installation of the sound absorptive material in Elevations "C" and "D".

JJHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

12 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Finished Hardware - Door No. 160

Gentlemen:

Install the following hardware on Door No. 160:

One (1) (Lockwood Hardware) #2243-1/2 x 2-3/4" BS x 97, 3 keys
MK x GM with square shank into turn knob. Lock to be placed
6" above floor.

One (1) Throw Bolt (Lockwood Hardware) #8111-1/2 x 8" x 97.

Two (2) Rixon Pivots #M-19 x 97.

One (1) "Doromatic" #R-253 (Right Hand) from Attic Stock.

Include the cost of these items in the same change as will be used
for N.C. No. 75 since this cost has already been included in N. C.
No. 75.



JJHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod



Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

120-5-18-9-
12 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Heating, Ventilating, Air Conditioning
Shop Drawings


Gentlemen:


Buffalo Forge Company Drawing No. 8C-16796-A, dated July 6, 1951, titled G-123 PCW Cabinets, and Drawing No. 8C-16792-A, no date, titled G-121 PCW Cabinets, were marked "Approved Except for Corrections" September 24, 1951 by Syska & Hennessy, Inc. and returned for resubmission.

We have been informed by Syska & Hennessy, Inc. that there was a misinterpretation of the drawings. The corrections noted thereon should be disregarded. The information shown on the drawings is herewith approved and the drawings need not be resubmitted.

Please inform all interested parties of this action.

Very truly yours,


JHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod
Ryer
Hannegan
Rumpelstin
S & H-2



James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

120-5-18-9
12 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Electric
Cole Electric Company Drawings, H-1170,
H-1174, H-1174-A, H-1175

Gentlemen:

We returned the following Cole Electric Company drawings to you,
marked "Disapproved and Resubmit", on the dates noted:

H-1170 Rev. No. 2 dated 28 August 1951
Disapproved and Resubmit 1 October 1951

H-1174 Dated 11 June 1951
Disapproved and Resubmit 9 October 1951


H-1174A Dated 12 June 1951
Disapproved and Resubmit 9 October 1951

H-1175 Dated 31 July 1951
Disapproved and Resubmit 24 October 1951.

In order to expedite the fabrication of work shown thereon we here-
with change the "Disapproved" to "Approved as Noted and Resubmit".

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office



JJHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod
Ryer

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 10, 1951

Copy to Mr. Dawson

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

Not being handled by Mr. Bennett

re: Contract HQ 1/82 - General
Assembly and North Parking Garage -
Dinner Equipment - General Assembly

Dear Mr. Dawson:

For your information, we are attaching a copy of a letter dated November 7, 1951 from Fischbach & Moore, Inc.

This letter indicates that the Dinner Equipment in the General Assembly Hall cannot be put into operation before December 1952.

We are endeavoring to expedite these motors through the N.P.A. and will do everything we possibly can to improve the delivery date,

These are special motors and as far as we can find out, there is no other manufacturer which makes this type of motor. We have talked with Mr. Conley, Production Manager of the Electric Specialty Co., and he advises that they have a back-log of rated orders for the next twelve months and there is nothing that can be done without an official directive, which would have to be issued by the Nations Production Authority in Washington, D.C.

Up to the present time it has not been necessary to obtain any official directives, but it may be necessary if it is desired to operate the Dinner Equipment in the General Assembly Hall by September 1952.

Drawings on this Dinner Equipment were first submitted on November 4, 1950 and returned without action on January 19, 1951. When further details were furnished to the Ward Leonard Electric Co., they resubmitted their drawings on August 29, 1951 and they were returned "Approved" and "Approved as Noted" on September 18, 1951.

We shall keep you informed of any change of the delivery date for this equipment.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER/WWS/eas

cc/ Mr. Glenn E. Bennett (2)



November 7, 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd St.
New York 17, N.Y.

Attention: Mr. Charles Bartley

re: Dimmer Equipment
General Assembly

Gentlemen:

We will require help on delivery of equipment for our subcontractor Ward Leonard Electric Co., if the dimmer equipment is to be installed and in operation for opening of General Assembly.

Ward Leonard Electric Co. will need six (6) motors for the two dimmer banks in the General Assembly Hall, three (3) of which they have in stock. The remaining three have been ordered from the Electric Specialty Co., Stamford Conn., on Ward Leonard's order #A84310 and delivery promised in November 5, 1952.

The following is a description of the motors ordered:

- 2 - #90403540101 Special Type J Synchronous Wound Motors, 208 Volt, 60 Cycle, 3 phase, 1800 RPM, with gear reduction of 192 to 1.
- 1 - #90403540201 Type B 542.5, 3 phase, 1/4 HP. 60 Cycle, 208 Volt, 1800 RPM Synchronous Wound Motor with 900 to 1 gear reduction similar to serial #143155.

Ward Leonard will require these motors not later than January 31, 1952, in order to assemble the dimmer banks and delivery by March 1st.

Regarding the dimmer bank for Conference Room 4, all equipment is on hand and Ward Leonard require no help on this bank.

We would appreciate your taking necessary steps to expedite motors from Electric Specialty Co.

Very truly yours,

FISCHBACH & MOORE, INC.

-9✓

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 10, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General
Assembly and North Parking Garage -
Dimmer Equipment - General Assembly

Dear Mr. Dawson:

For your information, we are attaching a copy of a letter dated November 7, 1951 from Fischbach & Moore, Inc.

This letter indicates that the Dimmer Equipment in the General Assembly Hall cannot be put into operation before December 1952.

We are endeavoring to expedite these motors through the N.P.A. and will do everything we possibly can to improve the delivery date.

These are special motors and as far as we can find out, there is no other manufacturer which makes this type of motor. We have talked with Mr. Conley, Production Manager of the Electric Specialty Co. and he advises that they have a back-log of rated orders for the next twelve months and there is nothing that can be done without an official directive, which would have to be issued by the Nations Production Authority in Washington, D.C.

Up to the present time it has not been necessary to obtain any official directives, but it may be necessary if it is desired to operate the Dimmer Equipment in the General Assembly Hall by September 1952.

Drawings on this Dimmer Equipment were first submitted on November 4, 1950 and returned without action on January 19, 1951. When further details were furnished to the Ward Leonard Electric Co., they resubmitted their drawings on August 29, 1951 and they were returned "Approved" and "Approved as Noted" on September 18, 1951.

We shall keep you informed of any change of the delivery date for this equipment.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CEN/WWS/eas

cc/ Mr. Glenn E. Bennett (2) ✓

November 7, 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd St.
New York 17, N.Y.

Attention: Mr. Charles Bartley

re: Dimmer Equipment
General Assembly

Gentlemen:

We will require help on delivery of equipment for our subcontractor Ward Leonard Electric Co., if the dimmer equipment is to be installed and in operation for opening of General Assembly.

Ward Leonard Electric Co. will need six (6) motors for the two dimmer banks in the General Assembly Hall, three (3) of which they have in stock. The remaining three have been ordered from the Electric Specialty Co., Stamford Conn., on Ward Leonard's order #A84310 and delivery promised in November 5, 1952.

The following is a description of the motors ordered:

- 2 - #90403540101 Special Type J Synchronous Wound Motors, 208 Volt, 60 Cycle, 3 phase, 1800 RPM, with gear reduction of 192 to 1.
- 1 - #90403540201 Type B 542.5, 3 phase, 1/4 HP./ 60 Cycle, 208 Volt, 1800 RPM Synchronous Wound Motor with 900 to 1 gear reduction similar to serial #143155.

Ward Leonard will require these motors not later than January 31, 1952, in order to assemble the dimmer banks and delivery by March 1st.

Regarding the dimmer bank for Conference Room 4, all equipment is on hand and Ward Leonard require no help on this bank.

We would appreciate your taking necessary steps to expedite motors from Electric Specialty Co.

Very truly yours,

FISCHBACH & MOORE, INC.

120-5-18-9
COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 10, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General
Assembly and North Parking Garage -
Dimmer Equipment - General Assembly

Dear Mr. Dawson:

For your information, we are attaching a copy of a letter dated November 7, 1951 from Fischbach & Moore, Inc.

This letter indicates that the Dimmer Equipment in the General Assembly Hall cannot be put into operation before December 1952.

We are endeavoring to expedite these motors through the E.P.A. and will do everything we possibly can to improve the delivery date.

These are special motors and as far as we can find out, there is no other manufacturer which makes this type of motor. We have talked with Mr. Conley, Production Manager of the Electric Specialty Co. and he advises that they have a back-log of rated orders for the next twelve months and there is nothing that can be done without an official directive, which would have to be issued by the Nations Production Authority in Washington, D.C.

Up to the present time it has not been necessary to obtain any official directives, but it may be necessary if it is desired to operate the Dimmer Equipment in the General Assembly Hall by September 1952.

Drawings on this Dimmer Equipment were first submitted on November 4, 1950 and returned without action on January 19, 1951. When further details were furnished to the Ward Leonard Electric Co., they resubmitted their drawings on August 29, 1951 and they were returned "Approved" and "Approved as Noted" on September 18, 1951.

We shall keep you informed of any change of the delivery date for this equipment.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

G. R. Neese
G. R. Neese
Project Engineer

GMH/WAB/ean

cc/ Mr. Glenn E. Bennett (2) ✓ 9/1951

November 7, 1951

ler-Turner-Walsh-Slattey, Inc.
3 East 42nd St.
New York 17, N.Y.

Attention: Mr. Charles Bartley

re: Dinner Equipment
General Assembly

Gentlemen:

We will require help on delivery of equipment for our subcontractor Ward Leonard Electric Co., if the dinner equipment is to be installed and in operation for opening of General Assembly.

Ward Leonard Electric Co. will need six (6) motors for the two dinner banks in the General Assembly Hall, three (3) of which they have in stock. The remaining three have been ordered from the Electric Specialty Co., Stamford Conn., on Ward Leonard's order #A84310 and delivery promised in November 5, 1952.

The following is a description of the motors ordered:

- 2 - #90403540101 Special Type J Synchronous Wound Motors, 208 Volt, 60 Cycle, 3 phase, 1800 RPM, with gear reduction of 192 to 1.
- 1 - #90403540201 Type B 542.5, 3 phase, 1/4 HP./ 60 Cycle, 208 Volt, 1800 RPM Synchronous Wound Motor with 900 to 1 gear reduction similar to serial #143155.

Ward Leonard will require these motors not later than January 31, 1952, in order to assemble the dinner banks and delivery by March 1st.

Regarding the dinner bank for Conference Room 4, all equipment is on hand and Ward Leonard require no help on this bank.

We would appreciate your taking necessary steps to expedite motors from Electric Specialty Co.

Very truly yours,

FISCHBACH & MOORE, INC.

120-5-18-9
COPY

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
NEW YORK

November 10, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General
Assembly and North Parking Garage -
Dimmer Equipment - General Assembly

Dear Mr. Dawson:

For your information, we are attaching a copy of a letter dated November 7, 1951 from Fischbach & Moore, Inc.

This letter indicates that the Dimmer Equipment in the General Assembly Hall cannot be put into operation before December 1952.

We are endeavoring to expedite these motors through the N.P.A. and will do everything we possibly can to improve the delivery date.

These are special motors and as far as we can find out, there is no other manufacturer which makes this type of motor. We have talked with Mr. Conley, Production Manager of the Electric Specialty Co. and he advises that they have a back-log of rated orders for the next twelve months and there is nothing that can be done without an official directive, which would have to be issued by the National Production Authority in Washington, D.C.

Up to the present time it has not been necessary to obtain any official directives, but it may be necessary if it is desired to operate the Dimmer Equipment in the General Assembly Hall by September 1952.

Drawings on this Dimmer Equipment were first submitted on November 4, 1950 and returned without action on January 19, 1951. When further details were furnished to the Ward Leonard Electric Co., they resubmitted their drawings on August 29, 1951 and they were returned "Approved" and "Approved as Noted" on September 18, 1951.

We shall keep you informed of any change of the delivery date for this equipment.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER/WWS/eas

cc/ Mr. Glenn E. Bennett (2)

November 7, 1951

Fuller-Turner-Walsh-Battery, Inc.
403 East 42nd St.
New York 17, N.Y.

Attention: Mr. Charles Bartley

re: Dinner Equipment
General Assembly

Gentlemen:

We will require help on delivery of equipment for our subcontractor Ward Leonard Electric Co., if the dinner equipment is to be installed and in operation for opening of General Assembly.

Ward Leonard Electric Co. will need six (6) motors for the two dinner banks in the General Assembly Hall, three (3) of which they have in stock. The remaining three have been ordered from the Electric Specialty Co., Stamford Conn., on Ward Leonard's order #A84310 and delivery promised in November 5, 1952.

The following is a description of the motors ordered:

- 2 - #90403540101 Special Type J Synchronous Wound Motors, 208 Volt, 60 Cycle, 3 phase, 1800 RPM, with gear reduction of 192 to 1.
- 1 - #90403540201 Type B 542.5, 3 phase, 1/4 HP./ 60 Cycle, 208 Volt, 1800 RPM Synchronous Wound Motor with 900 to 1 gear reduction similar to serial #143155.

Ward Leonard will require these motors not later than January 31, 1952, in order to assemble the dinner banks and delivery by March 1st.

Regarding the dinner bank for Conference Room 4, all equipment is on hand and Ward Leonard require no help on this bank.

We would appreciate your taking necessary steps to expedite motors from Electric Specialty Co.

Very truly yours,

FISCHBACH & MOORE, INC.

Fuller-Turner-Walsh-Slaterry, Inc.
General Contractors
United Nations Permanent Headquarters

R.P. #63

NOTIFICATION OF CHANGE

Date: November 9, 1951

TO: Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272, United Nations
New York 17, New York

N. C. # 78

Building: GENERAL ASSEMBLY & NORTH PARKING SPACE - CONTRACT HQ 1/82

Reference Information: U. N. Interiors Drawing No. 7 - "Press Food Bar" - Dated 9/28/51.

Description of Changes: Food Bar Details

The above contemplated change effects the changes of the work indicated by X marks. There is shown below a quick estimate of the approximate cost of the change merely to indicate its magnitude and to assist the Owner in determining whether or not the change should be made.

(X) F-T-W-S Inc. Work	() Construction Insulation	(X) Painting & Finish
() Structural Steel	(X) Metal, Doors, Frames & Trim	() Venetian Type Blinds
() Concrete Construction Work	() Roll-up Seal Doors	(X) Resilient Floor
() Concrete Slabs & Fireproofing	() Metal Toilet Enclosures	Covering
() Floor & Roof Fill	() Hollow Metal Partitions	() Miscellaneous
(X) Finish Cement Work	() Marble Work	Accessories
(X) Masonry-Mortars	() Ceramic Tile	() Heating, Ventilating
(X) Waterproofing (Membrane Spondrel)	() Terrazzo Work	& Air Conditioning
() Dampproofing (Mastic)	(X) Furring & Lathing	() Plumbing
() Caulking	(X) Plastering	() Sprinklers
() Cut Stonework	() Acoustical Treatment	() Electrical
() Lining (built-up)	() Sound Conditioning	() Sheet Metal Work
(X) Carpentry & Millwork	(X) Miscellaneous Iron	(X) Glass & Glazing
() Ornamental Metal Work	(X) Finish Hardware	

The Approximate Total Cost of this Change is \$ 1700. * ADDITION
(SEVENTEEN HUNDRED DOLLARS-ADDITION)

and the Owner's immediate decision is required, avoiding a "Stop Order" of Field Operations and permitting the work to continue without interruption.

Fuller-Turner-Walsh-Slaterry, Inc.

By M. J. Hogan
Project Manager

Date: 11/9/52

The Above change will not be made and the work is to proceed in accordance with the existing Contract Requirements.

You are hereby instructed to proceed with the work in accordance with this N.C. and issue P.W.O.'s as required. Price adjustments to be made under the Contract Terms. ***

UNITED NATIONS HEADQUARTERS

UNITED NATIONS HEADQUARTERS

By: _____ Date: _____

By: Chulan Date: 11/9/51

* This price includes only the changes in the work of Architectural Trades shown on the left hand (Work by Gen'l Contractor) side of the drawing. Finishing of the wood rolling shutters are included. The cost of changes in work by Mechanical Trades is not included.

***Waterproofing and cement finish around drains are deemed by the United Nations to be included in the base contract and are not, therefore, extra work.

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 9, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General
Assembly and North Parking
Garage - Electrical Control
Centers - Fan Rooms #1 and #2

Dear Mr. Dawson:

We have been advised by the National Production Authority (New York Regional Office) that they received the following communication from their Cincinnati, Ohio offices. It reads essentially as follows:

"Reference: Trumbull Dept. of the General Electric Co. Shop Order L-2046. This manufacturer has received 11 Directives and 2 DX Orders which sets back this order to December 15, 1951 and, if no more Directives are received, this date will be met."

The above order includes the sheet metal fronts and cubicles for Control Centers #2B-1 and #1B-4 for Fan Rooms #1 and #2, respectively. Inasmuch as it has been expressed that it is desired to put these Fan Rooms into operation for heating the Studios, Master Control Room, etc., it will not be possible to do so at this time without using temporary electric starters.

For your information, drawings on the above control centers were first submitted for approval in December 1950. They were returned "Approved as Noted" in January 1951, however, certain items were marked "HOLD". This, therefore, prevented fabrication of the cubicles.

When further details were obtained by Trumbull they resubmitted these drawings in July 1951. They were returned "Approved as Noted" in August 1951. These drawings were corrected and the third and final submission was made in September 1951. These were returned "Approved" stamped September 24, 1951.

We believe that you can see and understand the difficulty which the Trumbull Co. faced in trying to have these cubicles placed in their plant for fabrication, prior to receiving final "Approved" drawing.

If the Norwood, Ohio plant can ship these cubicles on December 15th, without being displaced by further Directives, the Trumbull Co. in Long Island will require three to four weeks to assemble these cubicles with starters, circuit breakers, etc. This would make the earliest possible delivery date about the middle of January 1952. Fischbach & Moore, Inc. the Electrical subcontractor, would then require about two weeks to wire up these control centers on the job.

Mr. James A. Dawson

-2-

November 9, 1951

re: Contract HQ 1/82 - Electrical Control Centers - Fan Rooms #1 and #2

The above indicates that it will be February 1952 before these control centers will be ready for operation.

We ask that you review our letter to you, dated August 10, 1951, in which we advise the cost of setting up temporary electric work for certain Fan Systems in Fan Room3 #1 and #2. The approximate cost was \$450.00, plus or minus 10%. If it is desired, the electrical work can be done on a time and material basis with an approximate guaranteed upset price of \$500.00.

Please advise on the above.

Very truly yours,

FULLER-TURNER-WALSH-SLATTEY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER/WWS/eas

cc/ Mr. Glenn E. Bennett (2)



120-5-18-9
COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 9, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General
Assembly and North Parking
Garage - Electrical Control
Centers - Fan Rooms #1 and #2

Dear Mr. Dawson:

We have been advised by the National Production Authority (New York Regional Office) that they received the following communication from their Cincinnati, Ohio offices. It reads essentially as follows:

"Reference: Trumbull Dept. of the General Electric Co. Shop Order L-2046.
This manufacturer has received 11 Directives and 2 DX Orders which sets back this order to December 15, 1951 and, if no more Directives are received, this date will be met."

The above order includes the sheet metal fronts and cubicles for Control Centers #2B-1 and #1B-4 for Fan Rooms #1 and #2, respectively. Inasmuch as it has been expressed that it is desired to put these Fan Rooms into operation for heating the Studios, Master Control Room, etc., it will not be possible to do so at this time without using temporary electric starters.

For your information, drawings on the above control centers were first submitted for approval in December 1950. They were returned "Approved as Noted" in January 1951, however, certain items were marked "HOLD". This, therefore, prevented fabrication of the cubicles.

When further details were obtained by Trumbull they resubmitted these drawings in July 1951. They were returned "Approved as Noted" in August 1951. These drawings were corrected and the third and final submission was made in September 1951. These were returned "Approved" stamped September 24, 1951.

We believe that you can see and understand the difficulty which the Trumbull Co. faced in trying to have these cubicles placed in their plant for fabrication, prior to receiving final "Approved" drawing.

If the Norwood, Ohio plant can ship these cubicles on December 15th, without being displaced by further Directives, the Trumbull Co. in Long Island will require three to four weeks to assemble these cubicles with starters, circuit breakers, etc. This would make the earliest possible delivery date about the middle of January 1952. Fischbach & Moore, Inc. the Electrical subcontractor, would then require about two weeks to wire up these control centers on the job.

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

Mr. James A. Dawson

-2-

November 9, 1951

re: Contract HQ 1/82 - Electrical Control Centers - Fan Rooms #1 and #2

The above indicates that it will be February 1952 before these control centers will be ready for operation.

We ask that you review our letter to you, dated August 10, 1951, in which we advise the cost of setting up temporary electric work for certain Fan Systems in Fan Room3 #1 and #2. The approximate cost was \$450.00, plus or minus 10%. If it is desired, the electrical work can be done on a time and material basis with an approximate guaranteed upset price of \$500.00.

Please advise on the above.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER/WWS/eas

cc/ Mr. Glenn E. Bennett (2) ✓

NOV 9 1951

120-5-18-9 ✓
COPY

FULLER - TURNER - WALSH - SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 9, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract No 1/52 - General
Assembly and North Parking
Garage - Electrical Control
Centers - Fan Rooms #1 and #2

Dear Mr. Dawson:

We have been advised by the National Production Authority (New York Regional Office) that they received the following communication from their Cincinnati, Ohio offices. It reads essentially as follows:

"Reference: Trumbull Dept. of the General Electric Co. Shop Order L-2046.
This manufacturer has received 11 Directives and 2 DX Orders which sets back this order to December 15, 1951 and, if no more Directives are received, this date will be met."

The above order includes the sheet metal fronts and cubicles for Control Centers #2B-1 and #1B-4 for Fan Rooms #1 and #2, respectively. Inasmuch as it has been expressed that it is desired to put these Fan Rooms into operation for heating the Studios, Master Control Room, etc., it will not be possible to do so at this time without using temporary electric starters.

For your information, drawings on the above control centers were first submitted for approval in December 1950. They were returned "Approved as Noted" in January 1951, however, certain items were marked "HOLD". This, therefore, prevented fabrication of the cubicles.

When further details were obtained by Trumbull they resubmitted these drawings in July 1951. They were returned "Approved as Noted" in August 1951. These drawings were corrected and the third and final submission was made in September 1951. These were returned "Approved" stamped September 24, 1951.

We believe that you can see and understand the difficulty which the Trumbull Co. faced in trying to have these cubicles placed in their plant for fabrication, prior to receiving final "Approved" drawing.

If the Norwood, Ohio plant can ship these cubicles on December 15th, without being displaced by further Directives, the Trumbull Co. in Long Island will require three to four weeks to assemble these cubicles with starters, circuit breakers, etc. This would make the earliest possible delivery date about the middle of January 1952. Fischbach & Moore, Inc. the Electrical subcontractor, would then require about two weeks to wire up these control centers on the job.

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

Mr. James A. Dawson

-2-

Nov

Re: Contract No. 1/82 - Electrical Control Centers - Fan #

The above indicates that it will be February 1952 before these will be ready for operation.

We ask that you review our letter to you, dated August 10, 1951, in which we advise the cost of setting up temporary electric work for certain Fan System. Fan Room #1 and #2. The approximate cost was \$450.00, plus or minus 10%. If it is desired, the electrical work can be done on a time and material basis with an approximate guaranteed upset price of \$500.00.

Please advise on the above.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CHW/WMS/eas

cc/ Mr. Glenn A. Bennett (2) ✓

120-5-18-9
cc: Harrison
McLeod
Zunser
Van Name
Hopper
Healy

9 November 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, N.Y.

Re: Contract HQ 1/82 - General Assembly and
North Parking Garage - Notification of
Change No. 76 (R.P. 64) - Revisions to
Section AA-of Sketch 665

Gentlemen:

Attached hereto is one copy of Notification of Change No. 76 (R. P. 64) approved by James A. Dawson for the United Nations.

This approval is given for you to proceed with the work required by the modification with reference to revisions to section AA-of Sketch 665.

It is understood that this approval does not include the cost of this change as indicated in the Notification of Change No. 76, which is solely an approximation. It is understood, also, that the actual price adjustment will be made as required by the terms of the contract.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

Enclosure

JZ:eh

120-5-18-92
9 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Carpentry and Millwork - Samples - Plastic Laminate

Gentlemen:

Reference is made to your letter of the 24th of August 1951, wherewith you transmitted for our consideration and/or approval samples in triplicate of the Parkwood Corporation's No. 3070 Rift Oak "Genu-wood" which you propose to provide for facings of the north balcony railings of the General Assembly.

As you know, these samples were found to be unacceptable both in color and graining and we verbally asked for a new submission more closely approximating the characteristics of the manufacturer's sample on file in this office. The samples brought over by hand yesterday in quintuple, in response to our earlier oral request, have been reviewed and although not precisely matching the noted manufacturer's specimen are found to be acceptable for the use noted in the initial paragraph.

It is understood that our acceptance of this Rift Oak "Genu-wood" in lieu of Formica or Micarta sheets will not entail any change to the Contract Price.

Our approval of the use of this material in no way relieves the contractor of his responsibility for the satisfactory performance of the work in accord with the Specifications of the Contract Documents.

Returned herewith, marked "Approved", are four of the five samples received yesterday. Also returned, unmarked, are the three samples originally submitted.

HBW:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
Ryer
Scilipoti

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

9 November 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Glass and Glazing - Photosensitive Glass

Gentlemen:

The design of the photosensitive glass as developed by Mr. Thomas O'Leary of the Corning Glass Works with our Design Department is acceptable and has been incorporated in our Drawings DSK-441 and DSK-447 and on the samples of photosensitive glass sent in for our approval on 30 October 1951. Although several samples were submitted for our approval only one was satisfactory in both design and finish. We are therefore retaining this sample in our office.

In addition to the design indicated on the drawings, the Corning Glass Works through Mr. O'Leary has been advised to deliver this glass with a photo-etched finish similar to the sample which they submitted to this office for our approval. They are proceeding with the manufacture of this glass on this basis and have forwarded to you through your subcontractor, Morris Levin, a schedule for the delivery of this glass.

We are sending you this letter as a confirmation of our approval of the design and ask that you forward this information to both Morris Levin and the Corning Glass Works for their records.

There will be no change in price caused by the approval and you have already been advised to proceed with the work as per our letter to you of 8 November 1951.

Very truly yours,

JJHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

130-5-18-9
9 November 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, N. Y.

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Painting

Gentlemen:

In confirmation of verbal instructions given your Mr. Russell McKee by our Mr. Frank Egan recently in the field, we hereby advise that the finish paint color, to be applied on these plastered and/or masonry vertical surfaces which are to be painted in the Second Basement areas as outlined in our letter to you of the 29th ultimo concerning Revision No. 45, is Meeting Halls Blue No. 30.

The ceiling surfaces in these areas to be painted shall be finished in Meeting Halls White No. 10.

The paint types to be used in this work are to be those suitable for application on the various surfaces as set forth in our letter to you of the 29th of June of this year concerning approval of painting and finishing materials.

HBW:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

(4)

9 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York


Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Electrical - Special Lighting

Gentlemen:

On 8 November 1951 we forwarded you twenty-one (21) copies of
Schedule GA-94S, 4th Revision, dated 8 November 1951. You will
note the number of fixtures in the Assembly Hall have been
revised.

At the request of Mr. McNary of Fischbach & Moore, Inc, made at
a meeting held at the UNHPO on 8 November 1951, we are forwarding
you this latest schedule in preparation for a probable change to
the dome of the Assembly Hall.

This change has not yet been issued to you but will be in the near
future.

 JJHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod
Ryer
Hannegan
Seelman
S & H-2

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

120-5189

9 November 1951

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Re: General Assembly and Northerly Portion
of Parking Garage - Contract HQ 1/82
Architectural Revision No. 49 dated
2 November 1951 - Miscellaneous Change

Gentlemen:


On 5 November 1951 we forwarded you twenty-five (25) copies of the following drawings and Bulletin of Changes to Revision No. 49.

Drawing RA-170	Drawing RA-173
" RA-171	" RA-174
" RA-172	" RA-175.

Bulletin of Changes sent under separate cover.

Nothing indicated on the above documents should cause any change to the Contract Price with the exception of Item No. 6, Drawing RA-175, shown on Page 2, Bulletin of Changes.

Proceed with the work and submit for our consideration prices which affect the Contract Price.

 JJHe:js
cc: Bohanon
Nelson
Healy-2
Harris
Hopper
Zunser
VanName
McLeod
Ryer

Very truly yours,

James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

FULLER - TURNER - WALSH - SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 8, 1951
file

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

RE: Contract HQ 1/82 - General Assembly & North Parking Space
ESTIMATE FOR CHANGE NO. 298 - Deletion of
G.M. Screen at South Balcony, 3rd Floor
and Substitution of Railings

References:

- (a) U.N. Dwg. DSK-431 - "Press Balcony Rail - Elev. 68'-4" - Voiding Screen", dated 9/4/51
- (b) FTWS, Inc. Notification of Change No. 67, dated 9/26/51
- (c) Mr. James A. Dawson's letter dated 10/4/51 to FTWS, Inc.
- (d) FTWS, Inc. letter (Grogan) to U.N. dated 10/10/51 (C.O.298)

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we offer a decrease in our total guaranteed maximum cost price in the amount of SIX THOUSAND FOUR HUNDRED NINETY-EIGHT DOLLARS and SEVENTY-ONE CENTS (\$6498.71) for the changes in the work itemized herein, which are required by the above references.

This estimate is broken down as follows:

PART IV-SECTIONS 11 & 12 - MISCELLANEOUS IRON & ORNAMENTAL METAL WORK
(General Bronze Corp.)

		<u>DEDUCT</u>	<u>ADD</u>
Omit G.M. Screens #382, 383 and 310, and substitute two (2) sections of railing:			
DEDUCT - material, trucking, paint, etc.	\$886.00		
Shop Labor	4256.00		
Field Labor	871.00		
Engring (Dwgs. complete)	---		
	<u>\$6013.00</u>		
TOTAL - THIS SECTION		\$6,013.00	--

PART IV - SECTION 14 - METAL DOORS, FRAMES & TRIM
(Atlantic Metal Products, Inc.)

Deduct - 1 pair doors in opening of screen #310

TOTAL - THIS SECTION	115.00	---
----------------------	--------	-----

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

-2-

November 8, 1951

RE: Contract HQ 1/82 - Estimate for Change No.298

Brought forward from P. 1

DEDUCT
\$6,128.00

ADD
--

PART IV - SECTION 23 - CARPENTRY & MILLWORK
(Murray Hill Woodworking Corp.)

Add - Wood railing in lieu of GM Screens at
382, 383:

382 - 25'-0" teakwood rail

383 - 36'-0" " "

61'-0" @ \$5.00/L.F. = \$305.00

TOTAL - THIS SECTION

--

\$305.00

PART IV - SECTION 24 - GLASS & GLAZING
(Morris Levin & Sons, Inc.)

Deduct: 3 pcs P.P.G. 74 x 118 - 181.92 sq.ft.

5 pcs 66 x 118 - 270.41

5 pcs 66 x 28 - 64.16

1 pc 74 x 30 - 15.41

1 pc 74 x 36 - 18.50

1 pc 74 x 40 - 20.55

2 pcs. 32 x 75 - 33.76

2 pcs 32 x 24 - 10.66

2 pcs 14 x 76 - 14.78

2 pcs 14 x 24 - 4.66

1 pc. 74 x 76 - 39.05

1 pc 74 x 24 - 12.33

2 pcs. 40 x 108 - 60.00

2 pcs. 28 x 108 - 42.00

788.19 sq.ft.

Material - 788.19 sq.ft. @ .60/sq.ft. - 472.91

Labor - 30 hrs. @ \$3.00/hr. 90.00

Welfare & Pension @ 6% 5.40

568.31

FOAB & U.I. @ 4.5%

4.05

572.36

TOTAL - THIS SECTION

572.36

--

PART IV - SECTION 26 - PAINTING & FINISHING
(Shatz Painting Co.)

1. Omit painting of metal & glass partition - 143.00

2. Add metal railing - 61 l.f. @ .30 - 18.30

Add wood handrail - 61 l.f. @ .35 - 21.35

39.65 143.00

- 39.65

103.35

TOTAL - THIS SECTION

103.35

6803.71

305.00

- 305.00

\$6498.71

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

- Page 3 -

November 8, 1951

RE: HQ 1/82 - Estimate for Change No.298

Will you kindly issue a Change Order-DEDUCTION in the amount
of \$6498.71 to cover the costs itemized above.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan
Project Manager

MJG/CER/lbr

FULLER - TURNER - WALSH - SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 8, 1951
file

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

RE: Contract HQ 1/82 - General Assembly & North Parking Space
ESTIMATE FOR CHANGE NO. 280
CHANGE IN HARDWARE FOR DOORS 104, 115 and 121

References:

- (a) Mr. James A. Dawson's letter dated 9/11/51 to FTWS, INC.
- (b) FTWS, Inc. Letter (Grogan) to U.N. dated 9/17/51 (C.O.280)

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we claim an increase in our total guaranteed maximum cost price in the amount of TWO HUNDRED TWELVE DOLLARS AND FORTY-TWO CENTS (\$212.42) for the changes in the work itemized herein, which are required by the above references.

This estimate is broken down as follows:

PART IV - SECTION 14 - METAL DOORS, FRAMES & TRIM
(Atlantic Metal Products, Inc.)

A D D

1. To alter two (2) doors and three (3) bucks to take door closer brackets:

Material, reinforcing plates, welding -

Material and paint	\$18.00
Shop labor & supervision	90.00
	<u>108.00</u>

15% O & P	16.20
-----------	-------

TOTAL THIS SECTION	<u>124.20</u>
--------------------	---------------

✓ \$124.20

PART IV - SECTION 25 - FINISHED HARDWARE
(Lockwood Hardware Mfg. Co.)

1. Delete and put in attic stock:

- (a) Hardware Schedule, Item No. 269- 1 Dor-O-Matic Floor Hinge R251
- (b) Hardware Schedule Item No. 270 - 2 Dor-O-Matic Floor Hinges L251.

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

- 2 -

November 8, 1951

RE: HQ 1/82 - ESTIMATE FOR CHANGE NO. 280

Brought Forward from P.1 - A D D
\$124.20

PART IV - SECTION 25 - FINISHED HARDWARE (continued)

2. Add in lieu of above:

(a) 3 sets Rixon Door Pivots 117-US26D, 1/RH and 2/LH
all MS to templet @ \$16.70 ea. \$50.10

(b) 3 Door Closers C30PC, 2/RH, 1/LH
all MS ~~LX~~ 10337 @ \$10.30 ea. 30.90

(c) 3 Corner Brackets C914 all MS
IK 1512 @ \$1.55 ea. 4.65

Sales Tax

85.65
2.57
88.22

TOTAL THIS SECTION - - - \$ 88.22

TOTAL - THIS ESTIMATE..... \$212.42

Will you kindly issue a Change Order-ADDITION in the amount
of \$212.42 to cover the costs itemized above.

Very truly yours,

RULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan

M. J. Grogan
Project Manager

MJG/CER/lbr

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

November 8, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, N.Y.

re: Contract HQ 1/82 - General Assembly and North Parking Garage -
CHANGE NO. 322 - Addition of Light Fixtures over Exterior Doors at the
East and West Podium (Openings 129, 130, 131, 134, 135, 136)

References: (a) U.N.Dwg. DSK-425, dated 8/8/51
(b) E.F. Caldwell's Lighting Diagram K-12320, dated 7/17/51 -
"Lights Over Door Banks - East and West Exit Doors"

Dear Mr. Dawson:

On November 5, 1951 Mr. Paul Bohannon handed us copies of References (a) and (b) which show the requirements for six (6) light fixtures on the east and west podium exit doors.

These fixtures will require that the transom panels of these doors be drilled for a knockout and four (4) attachment screws for each fixture. It will probably also be necessary to put aluminum stiffener plates at each attachment so that the screws may be drawn up tight to make a weather-tight condition between the fixture and the transom panel.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/eas

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

November 8, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations

re: Contract HQ 1/82 - General Assembly and North Parking Garage -
CHANGE NO. 315 - October 23, 1951 Structural Revisions

References: (a) U.N.Dwg. GA-3-CS-32, issued 10/22/51
(b) U.N.Dwg. GA-3-CS-35, issued 10/22/51
(c) U.N.Dwg. GA-3-CS-35, rev. #1, issued 11/1/51
(d) Mr. James A. Dawson's letter 26 October 1951 to FTWS, Inc.

Dear Mr. Dawson:

On October 23, 1951 we received copies of References (a) and (b) and on November 2, 1951 we received Reference (c). Your transmittal letter, Reference (d), which we received on October 29, 1951, reads as follows:

"There are no cost changes involved, these changes being only field steel changes. These drawings are for your records.

Proceed with the work shown on the above drawings and submit for our consideration process which affect the Contract Price."

We have sent copies of the above referenced drawings to the interested subcontractors and have asked them to advise us if these structural steel revisions will entail any change to their contract price.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This Change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this Change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/eas

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

file

November 8, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272 - United Nations
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Half Parking Space
CHANGE NO. 312 - Adjustment of Catwalk Requirements

References: (a) U. N. Addendum No. 1 to Section 11 of the Contract Specifications, dated 11/3/49.
(b) U. N. Memorandum of June 7, 1950.
(c) U. N. Drawing SK-680 - "Location of Inserts For Catwalk in Dome," dated 10/16/51.
(d) Mr. James A. Dawson's letter dated October 22, 1951.

Dear Mr. Dawson:

Addendum No. 1 of the Specifications, Reference (a), specifies the construction of the catwalk required in the attic space of the General Assembly.

In Reference (b) we requested information from you concerning the extent of the catwalk system and you replied as follows:

"Architect's estimate of linear footage is 650 lineal feet.
Details to conform to specifications of Section 11."

You have recently issued us Drawing RA-9 which shows the catwalk plan for the North Half of the General Assembly. Since this plan is incomplete, we have been unable to determine the complete scope of your current requirements for the catwalk system. Since the full extent of your catwalk requirements, compared with the Contract requirements shown in References (a) and (b), is not readily determinable at this time, we will make the adjustment between the two in our Estimate for Change No. 312.

On October 17, 1951 we received prints of Drawing SK-680, Reference (c), which show inserts to be placed in the concrete slab of the Dome to provide for the future installation of a catwalk in this area.

Your letter of transmittal, Reference (d), reads as follows:

"Proceed with the purchasing and installing of the inserts as shown on this drawing and furnish for our consideration the prices which affect the Contract Price."

continued...

Mr. James A. Dawson

-2-

HQ 1/82 - CHANGE NO. 312


We will take into consideration in our Estimate for Change No. 312 the furnishing and installing of these inserts for the Dome catwalk.

We were verbally advised by your Messrs. Healy, Cole and Walther on October 17, 1951 that the Richmond Screw Anchor, No. US-406, loop type, malleable, adjustable insert would be satisfactory for the insert indicated on Drawing SK-680.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan
Project Manager

MJG/PDV/em

FULLER - TURNER - WALSH - SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

November 8, 1951

NEW YORK 17, N. Y.

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, New York

VOID

file

RE: HQ 1/82 Contract - General Assembly & North Parking Space
ESTIMATE FOR CHANGE NO. 300
Omission of Stainless Steel Glazing Channels

References:

- (a) U.N. Dwg. No. RA-105, Rev. No.7, dated 11/30/50
- (b) U.N. Dwg. No. A-107, Rev. No.1, dated 8/21/50
- (c) General Bronze Corp. shop dwgs. Nos. GB-A-9,10,19,20,21
- (d) FTWS, Inc. letter (Grogan) to U.N., dated 10/10/51 (C.O.300)

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we offer a decrease in our total guaranteed maximum cost price in the amount of ONE HUNDRED NINETY-ONE DOLLARS AND FIFTY-FOUR CENTS (\$191.54) for the changes in the work itemized herein, which are required by the above references.

This estimate is broken down as follows:

DEDUCTADD

PART IV-SECTION 12 - ORNAMENTAL ALLOY METAL WORK
(General Bronze Corp.)

1. Omit stainless steel glazing channels from
the East, West and South Sash,
5700 L.F. @ .10/L.F.

TOTAL - THIS SECTION

\$570.00

--

PART IV - SECTION 24 - GLASS AND GLAZING
(Morris Levin & Sons, Inc.)

1. Furnish labor and material to use putty
in lieu of glazing channels:

Material - 1500# Putty @ \$8.75/100# - 131.25
Labor - 60 hrs. @ \$3.00/hr 180.00
Welfare & Pension 6% 10.80

322.05

O & P 15%

48.31

FOAB & U.I. - 4.5%

8.10

378.46

TOTAL - THIS SECTION

570.00

378.46

378.46

- 378.46

TOTAL - THIS ESTIMATE

\$191.54

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office

-2-


November 8, 1951

RE: HQ 1/82 - Estimate for Change No. 300

Will you kindly issue a Change Order-DEDUCTION in the amount of \$191.54 to cover the changes itemized above.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan
Project Manager

MJG/CER/lbr

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 8, 1951

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, N. Y.

RE: Contract HQ 1/82 - General Assembly & North Parking Space
ESTIMATE FOR CHANGE NO. 255 and 255A
Changes to Sprinkler Layout in Assembly Hall

References:

- (a) U.N.Dwg. SK-GA-P6-1, Rev. No.1, dated 8/2/51
- (b) Mr. James A. Dawson's Letter dated 8/6/51 to FTWS, Inc.
- (c) U.N.Dwg. SK-GA-P6-1, Rev. No.2, dated 9/4/51
- (d) Mr. James A. Dawson's letter dated 9/5/51 to FTWS, Inc.
- (e) FTWS, Inc. letter (Grogan) to U.N. dated 8/15/51 (C.O. 255)
- (f) FTWS, Inc. letter (Grogan) to U.N. dated 9/10/51 (C.O. 255A)

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we claim an increase in our total guaranteed maximum cost price in the amount of THREE HUNDRED EIGHTY DOLLARS AND FORTY-FIVE CENTS (\$380.45) for the changes in the work itemized herein which are required by the above references.

Attached are three (3) copies of Automatic Sprinkler Corp. of America's Estimate (2 pages) dated 9/27/51, giving itemized breakdown of this change.

No charge is included in this estimate for patching by architectural trades.

Will you kindly issue a Change Order-ADDITION in the amount of \$380.45 covering the changes itemized herein.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan

M. J. Grogan
Project Manager

MJG/CER/lbr
Attachments

"AUTOMATIC" SPRINKLER CORPORATION OF AMERICA

MANUFACTURERS AND INSTALLERS OF APPROVED FIRE PROTECTION EQUIPMENT

GENERAL OFFICES
YOUNGSTOWN 1, OHIO

ADDRESS REPLY TO:

17 John Street
New York 38, New York

Telephone - Cortland 7-5730

RECEIVED
OCT 1 1951
FULLER - TURNER - WALSH - SLATTERY
INCORPORATED

September 27, 1951

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York

Attention: Mr. C. W. Bartley
Mechanical Supervisor

Subject: Contract HQ 1/82 - General Assembly
and North Parking Space
Change #255A
Sprinkler Layout for Battens in
General Assembly Hall

Gentlemen:

In accordance with your letter of September 7, 1951, we are pleased to submit, herewith, the following breakdown of additional cost for Change #255A as indicated on SK-GA/P6-1, revision #2 dated September 4, 1951. This amount is in addition to Change #174 and supersedes our estimate of August 22, 1951.

MATERIALS

8--4 in. C.I. Ells @ 3.23	\$ 25.84
30'--4 in. Steel Pipe @ 120.49	36.15
4--3 in. C.I. Ells @ 1.80	7.20
	<u>69.19</u>

SALES TAX

3%	2.08
----	------

TRANSPORTATION

8.00

LABOR

Fitter	48 hours @ 3.10	148.80
Foreman	7 hours @ 3.25	22.75



FOR INVESTMENT PROTECTION

RECEIVED

WELFARE & PENSION FUND

6%

OCT 1 1951

10.29

ENGINEERING

18 hours @ 3.50

FULLER - TURNER - WALSH - SLATTERY
INCORPORATED

63.00

324.11

Plus 15%

48.62

372.73

Federal O.A.B.
Unemployment Ins.
4.50 per C

7.72

\$380.45

We trust you will find this satisfactory.

Very truly yours,

"AUTOMATIC" SPRINKLER CORPORATION OF AMERICA

R V Benson c 2

R. V. Benson
Department Manager

RVB:CJF

FULLER - TURNER - WALSH - SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 8, 1951 *file*

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
Room 2272
United Nations, N. Y.

RE: Contract HQ 1/82 - General Assembly & North Parking Space
Estimate for Change No. 251
Revised Lighting Layout in Master
Control Room

References:

- (a) U.N. Dwg. SK-GA-E-1L-2 dated 7/27/51
- (b) Mr. James A. Dawson's letter dated 7/30/51 to FTWS, Inc.
- (c) FTWS, Inc. letter (Grogan) to U.N. dated 3/8/51 (CO 251)

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we claim an increase in our total guaranteed maximum cost price in the amount of NINETY-THREE DOLLARS (\$93.00) for the changes in the work itemized herein which are required by the above references.

Attached are three (3) copies of Fischbach & Moore's Pricing Sheet dated 8/23/51 giving itemized breakdown of this change.

No charge is included in this estimate for any patching by architectural trades.

Will you kindly issue a Change Order-ADDITION in the amount of \$93.00 covering the work itemized herein.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/GER/lbr
Attachment

PRICING SHEET

JOB U. N. GENERAL ASSEMBLY

LOCATION _____

Job
Estimate No. 9130OWNER C.O. 251

ARCHITECT _____

SHEET No. _____

BID TO _____

OF _____ SHEETS

ESTIMATED BY C.A.

PRICED BY _____

EXTENDED BY _____

CHECKED BY _____

DATE 8/23/51

MATERIAL

QUANTITY

MATERIAL
LIST PRICE

PER

DISC.

EXTENSION

LABOR
UNIT PRICE

PER

EXTENSION

Per Letter F.T.W.B. August 1st, 1951ADD

Relocate & Reconnect Type C

Fixtures

3

1/4 Oct. Box

3

13 70 C

1 -

Collar Box & Blank Cover

3

25 00 C

1 -

3/4 Black Cond Exp

10'

13 35 C

1 -

#12 R. C. Wire

25'

12 43 H

Incidentals

Allow

2 -

5 -

Labor & Supervision

60 -

2% Sales Tax

-

13.75% Insurance

8 -

Job Expense

4 -

77 -

O.H. & Profit 15%

12 -

6% F.B.A.B. & U.I.

4 -

\$93 -
