

CENTRAL REGISTRY (120-5-18-9) SG Building Construction - Working Project - General Assembly & North parking $\frac{1}{8}$ 2
Fuller-Turner-Wash-Slattey Inc. 1 NOV 1950

CLEAR

S.E. 7/04

S-0472

Box-24

File-6

(BAG-1)

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 30, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Re: Contract HQ 1/82 - General Assembly & North Parking Garage
CHANGE NO. 1 $\frac{1}{2}$ - Adjustment of Ornamental Metal and Hollow
Metal Subcontracts Concerning Glass and
Metal Screens

- References:
- (a) United Nations Comments on Contractor's Addenda,
dated April 20, 1950.
 - (b) Analysis of Bids and Recommendation for Award
of Subcontract for Hollow Metal Doors, Frames
and Trim, dated July 28, 1950, Approved August
9, 1950.
 - (c) Analysis of Bids and Recommendation for Award
of Subcontract for Ornamental and Miscellaneous
Metal, dated August 3, 1950, Approved August 23, 1950

Dear Mr. Dawson:

On November 28, 1950, at a meeting held in your office and at-
tended by the following:

Messrs. J. Zunser, U.N.H.P.O.
E. A. Van Name, "
J. J. Healy, "
M. M. Harris, "
P. Bohanon, "
W. Hopper, "
C. E. Reese, F-T-W-S, Inc.
P. Del Vecchio, "
J. Brock, Atlantic Metal Products, Inc.,

it was determined that both Atlantic Metal Products, Inc. and
General Bronze Corporation had proposed furnishing the interior
glass and metal screens for the General Assembly. This was brought
about by the following circumstances:

- (a) Reference (a), "Black Book", changed the construction
of the GM Screens from Aluminum to Hollow Metal as
follows:

Continued.....

November 30, 1950

Re: General Assembly Change No. 1 $\frac{1}{2}$

1. Item 15, Sections 11 and 12 - "Change all metal and glass screens from Aluminum to Steel".
2. Item 4, Section 14 - "Provide H.M. Doors where metal and glass screens are changed from Aluminum to Steel".

It is evident from the above that the intent was to have General Bronze Corporation furnish the screens, less the doors, and to have Atlantic Metal Products, Inc. furnish the doors only. This is borne out by paragraph 1a, Item "U" in Reference (c).

- (b) However, in Atlantic's subcontract, paragraph 1a reads as follows:

"Included in the scope of this contract is all the hollow metal work specified or implied in the Comments on Contractors Addenda of February 15, 1950 under Sections 14 and Sections 11 and 12".

Obviously Atlantic Metal Products, Inc. had included in their bid the price of the screens and doors.

Since no details were available in the contract documents, the subcontractors figured as follows:


- (a) General Bronze - in accordance with drawings A-127 and A-136, dated October 3, 1949, which were included in a previous bid set.
- (b) Atlantic Metal Products - in accordance with a detail prepared by them for a similar screen in the Meeting Halls.

The current details, shown on your drawing RA-128, Revision No. 3, dated September 28, 1950, conform with your previous requirements shown on A-136, dated October 3, 1949. This detail involves a Tee shaped mullion, faced with hollow metal. Since Atlantic Metal Products can not make these screens in this manner, we have requested that Atlantic delete the screens only from their contract and submit their credit for the deletion.

For purposes of accounting, we are hereby identifying this adjustment as our Change No. 1 $\frac{1}{2}$, which does not change our total guaranteed maximum cost price.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.


M. J. Grogan
Project Manager

MJG:PDV*cab

Fuller Dawson
This is expected to be modified new schedule
when we get B.B. Underwood That this schedule
therefore please return to me please
FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 30, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
405 East 42nd Street
New York 17, N. Y.

RECEIVED

DEC 1 1950

United Nations Headquarters
JAMES A. DAWSON
(Co-Ordinator of Construction)

RE: HQ 1/82 Contract - General Assembly & North Parking Space

Dear Mr. Dawson:

We are enclosing herewith a copy of Progress Schedule which was prepared at the time the contract was let for the General Assembly and North Parking Space. This is the schedule on which our subcontractors have based their bids.

We were very greatly disappointed with the delay experienced by the American Bridge Company with their structural steel for the North Parking Space which caused corresponding general delays in the progress of the North Parking Garage, as indicated on the chart. We were more than ever concerned yesterday in a meeting in Mr. Zunser's office with the American Bridge Company where it developed that American Bridge Company is not yet prepared to say when they will erect the steel for the superstructure for the General Assembly Building, nor will they commit themselves as to their procedure for the time required after the start of erection of the superstructure until areas are released by them for the installation of concrete and other work.

It is our opinion that the American Bridge Company will not start the erection of the superstructure above the main floor of the General Assembly before February 1, 1951. That would result in a delay of nearly three months in this progress schedule.

I hope you will be able to use this information in dealing with the American Bridge Company for betterment of their deliveries and improvement of the system of erection so as to allow the early installation of concrete work.

Very truly yours,


FULLER-TURNER-WALSH-SLATTERY, INC.

MJG/lbr
Encl. - Progress Schedule

M. J. Grogan
M. J. Grogan
Project Manager

UNITED NATIONS PERMANENT H
NEW YORK, N.Y., U.S.A

LEGEND



SHOP DETAILING PERIOD
MATERIAL ORDER OR SHOP FABRICATION
ERECTION PERIOD

	AUG.	SE
STRUCTURAL STEEL		
CONCRETE		
MISCELLANEOUS METAL		
PLUMBING WORK		
SPRINKLER WORK		
ELECTRICAL WORK		
HEATING, VENT., & A.C. WORK		
SHEET METAL		
ACOUSTICAL TREATMENT		
MASONRY		
METAL DOORS & FRAMES		
FURRING & LATHING		
PLASTERING		
CERAMIC TILE		
FINISH HARDWARE		

GENERAL ASSEMBLY & CONTRACT

PERIOD

[illegible]

FULLER-T
G

NORTH PARKING SPACE
HQ 1/82

1951


[illegible]


TURNER-WALSH-SLATTERY, INC.
GENERAL CONTRACTORS
NEW YORK, N.Y.

1952

[illegible]

FINISH HARDWARE		
CONCRETE FILL & FINISH		
FLOOR COVERINGS		
ORNAMENTAL METAL		
EXTERIOR MARBLE & STONE		
TOILET ENCLOSURES - METAL		
CARPENTRY & MILLWORK		
GLASS & GLAZING		
WATERPROOFING & DAMPPROOFING		
CAULKING		
ROLL-UP DOORS & GRILLES		
PAINTING & FINISHING		
TELEPHONE BOOTHS		
INTERIOR MARBLE		
ELEVATORS & ESCALATORS		
TERRAZZO		
INSULATION		
BUILT-UP ROOFING		
LIGHT SHUTTERS & SCREENS		
MISC. ACCESSORIES		

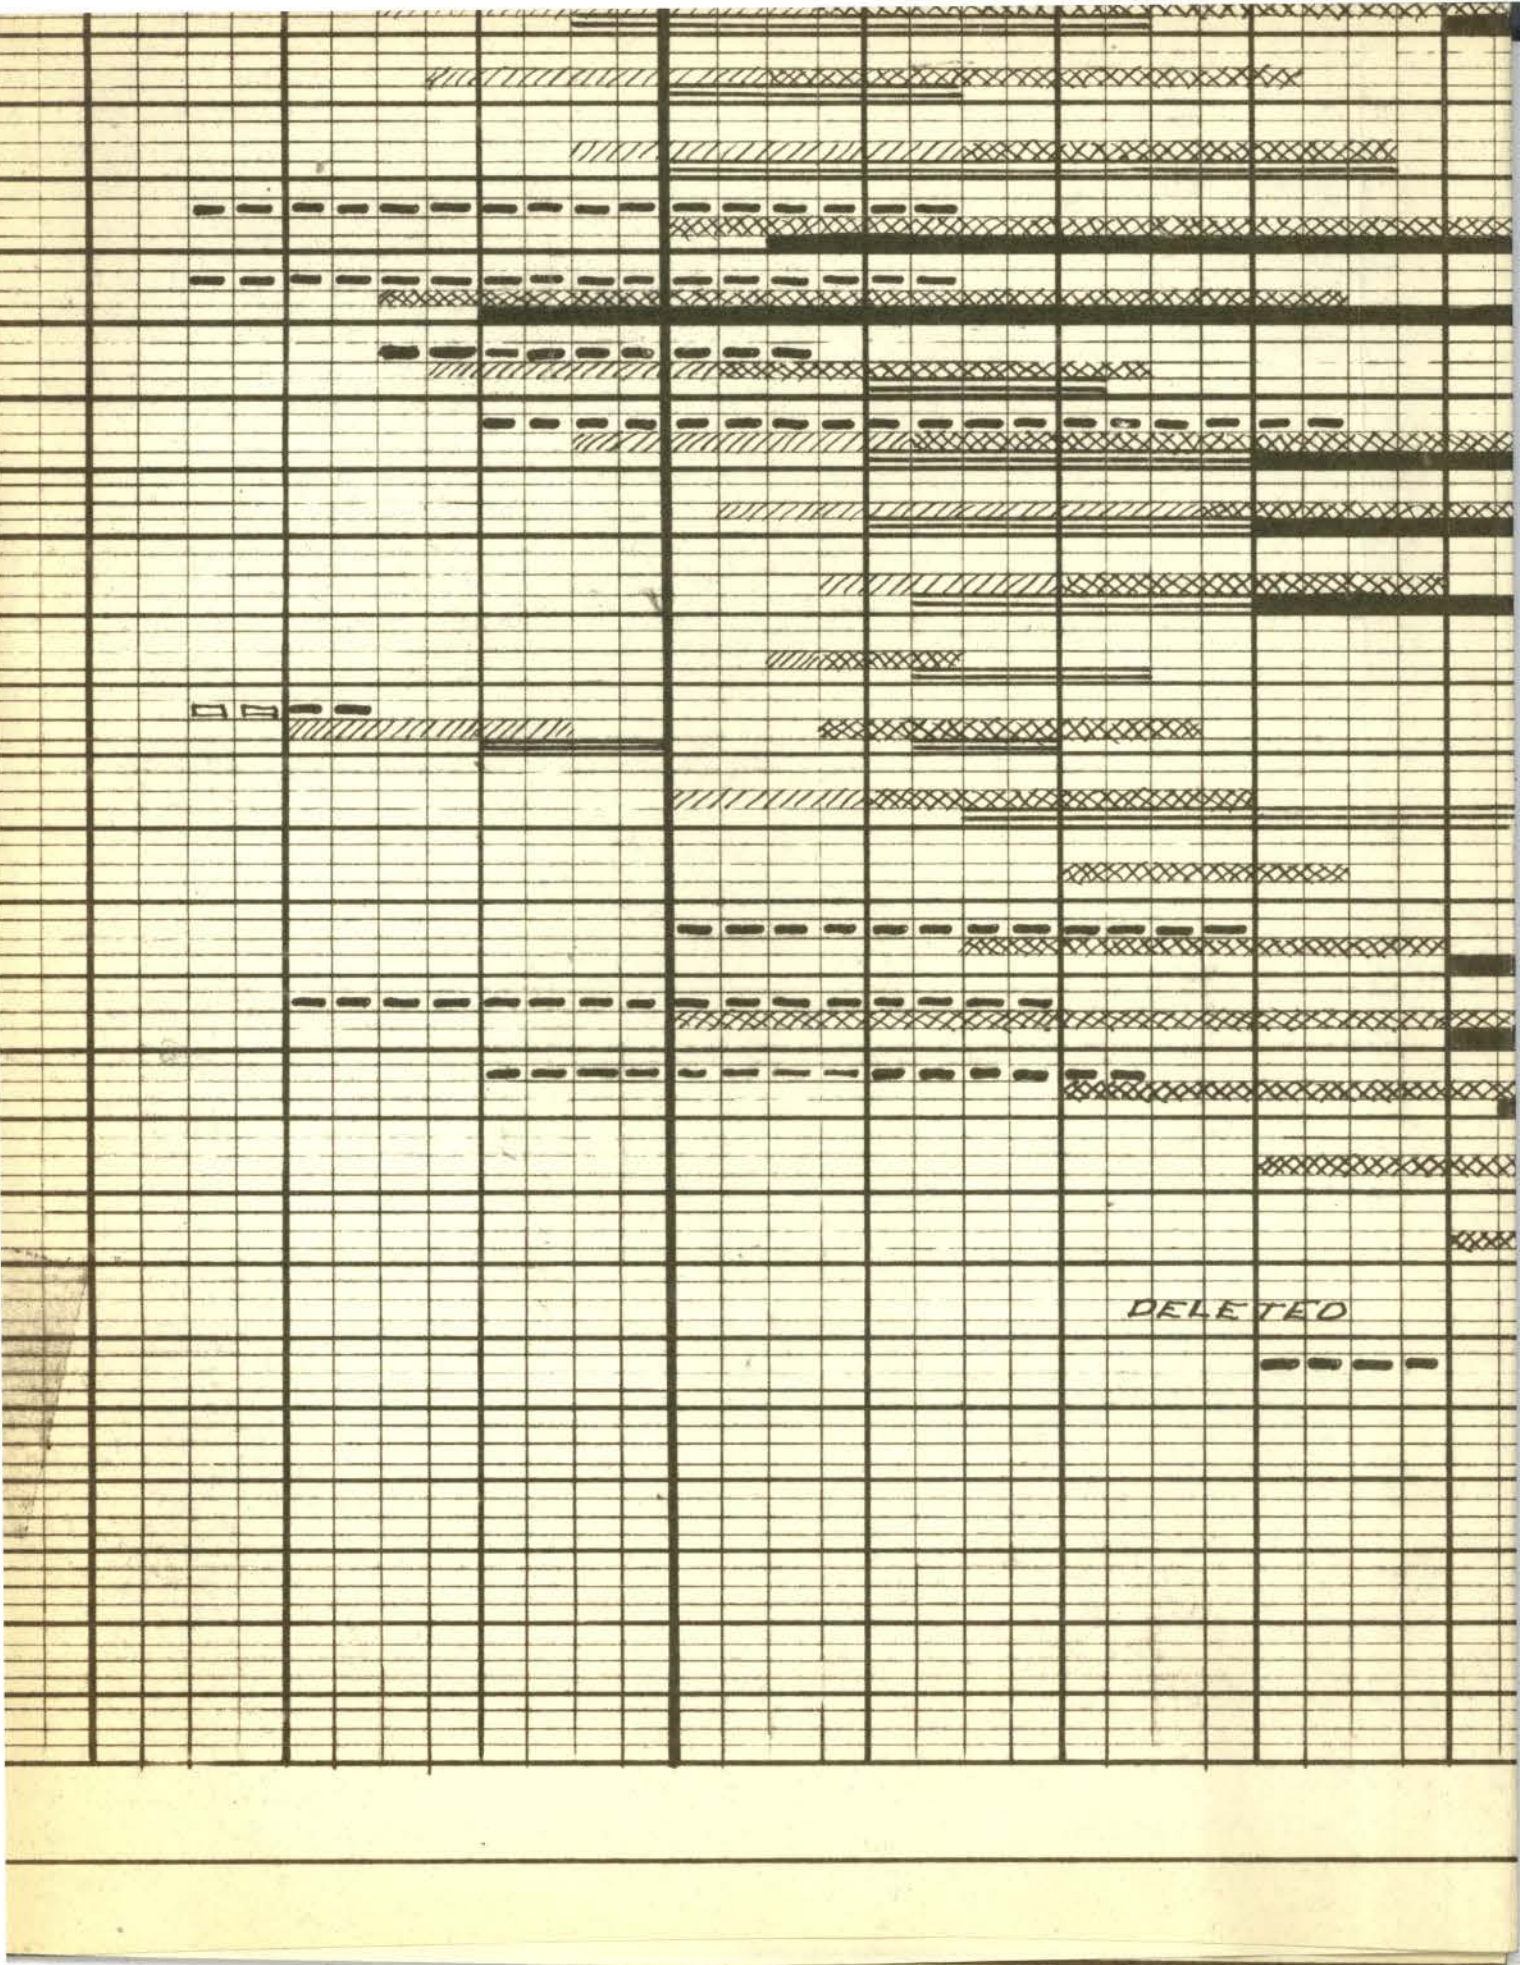

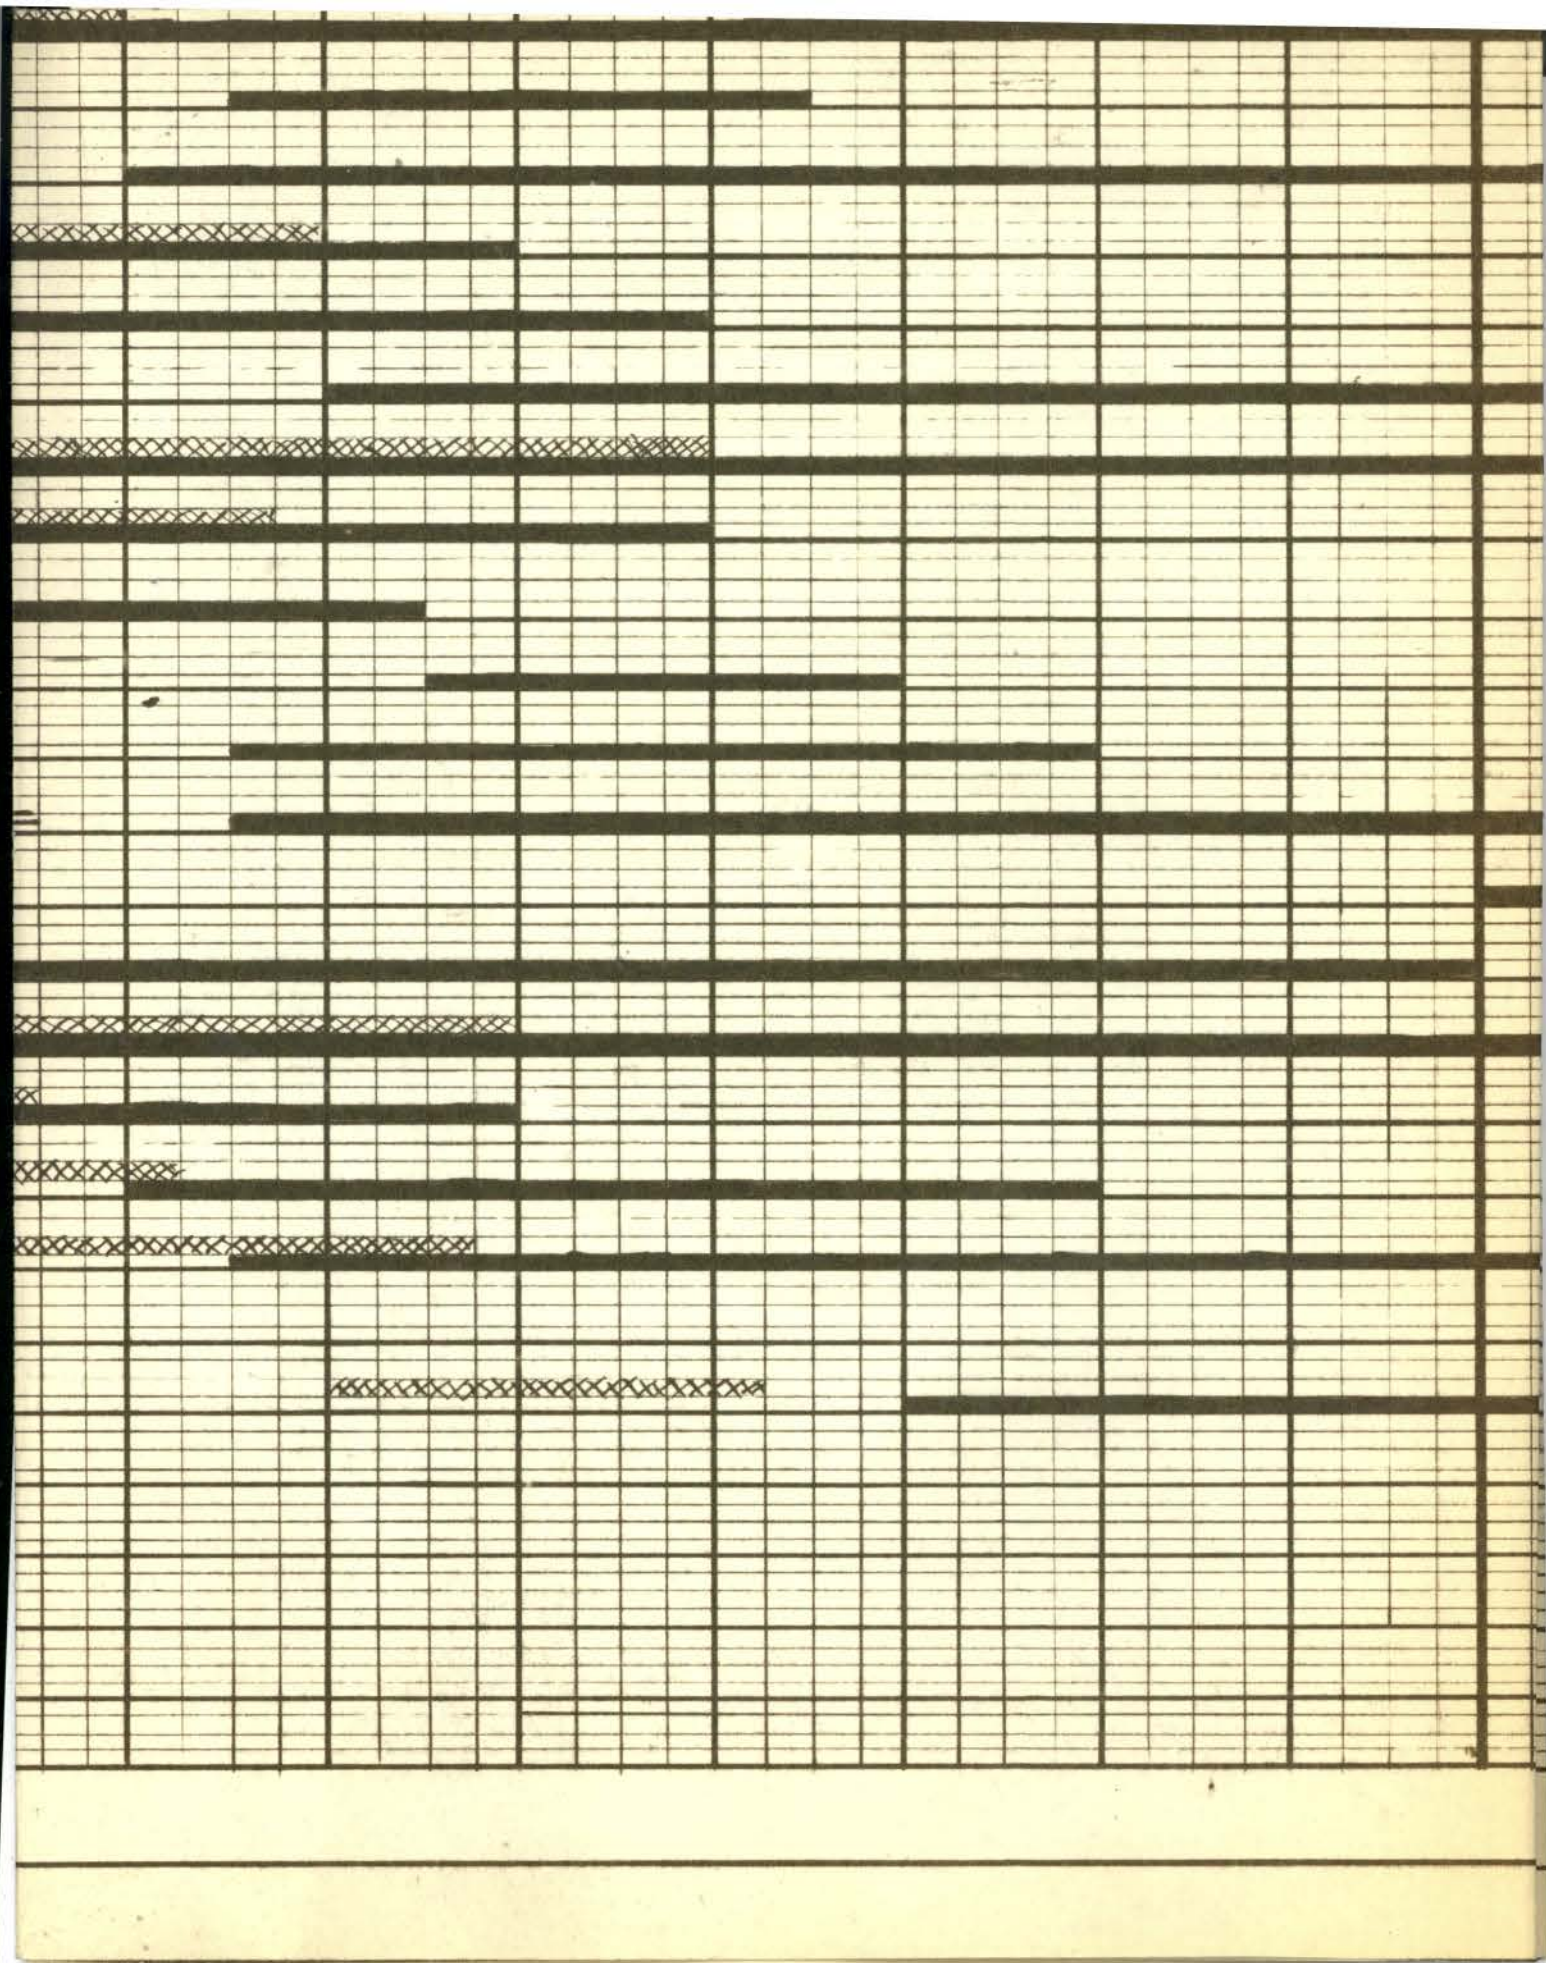

DATE: 8/29/50
REV.:

UN

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
NEW YORK

November 30, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
405 East 42nd Street
New York 17, N. Y.

RE: HQ 1/82 Contract - General Assembly & North Parking Space

Dear Mr. Dawson:

We are enclosing herewith a copy of Progress Schedule which was prepared at the time the contract was let for the General Assembly and North Parking Space. This is the schedule on which our subcontractors have based their bids.

We were very greatly disappointed with the delay experienced by the American Bridge Company with their structural steel for the North Parking Space which caused corresponding general delays in the progress of the North Parking Garage, as indicated on the chart. We were more than ever concerned yesterday in a meeting in Mr. Zunser's office with the American Bridge Company where it developed that American Bridge Company is not yet prepared to say when they will erect the steel for the superstructure for the General Assembly Building, nor will they commit themselves as to their procedure for the time required after the start of erection of the superstructure until areas are released by them for the installation of concrete and other work.

It is our opinion that the American Bridge Company will not start the erection of the superstructure above the main floor of the General Assembly before February 1, 1951. That would result in a delay of nearly three months in this progress schedule.

I hope you will be able to use this information in dealing with the American Bridge Company for betterment of their deliveries and improvement of the system of erection so as to allow the early installation of concrete work.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

A handwritten signature in blue ink that reads "M. J. Grogan".

M. J. Grogan
Project Manager

MJG/lbr
Encl. - Progress Schedule


FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 30, 1950



To HAW. FILE

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Finish Hardware

We are sending you herewith four copies of the Finish Hardware Schedule for the North Parking Space, revised November 17, 1950, submitted by the Lockwood Hardware Mfg. Co.

Will you please return two copies of the above Schedule, marked with your approval or necessary corrections.

This Schedule incorporates the following revisions, as verbally instructed by your Mr. W. Hopper on November 13, 1950:

- (a) Door Closers and brackets are shown on the Public toilets only (3B6 and 2B6). None are scheduled for the Private toilets Nos. 3B27, 20, 33 and 1B15.
- (b) The same master key for the South Parking Space has been listed for use in the North Parking Space.

May we please have your immediate comments on this revised Schedule. The fabrication of the door bucks for the North Parking Space has been delayed pending the receipt of an approved hardware schedule.


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C.E. Reese
Project Engineer

PDV*eah



R 12/1

ISSUANCE OF DRAWINGS

OFFICE COPY

30 November 1950

4 December 1950

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Lockwood

2

None

Rev.
17Nov'50

Finish Hardware Schedule for North Parking

(APPROVED 1 Dec 1950 REM.)



SV Dyker

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 30, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

John Fick

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Misc. Iron

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawing submitted by General Bronze Corporation and C. E. Halback & Company:

H.G.P. 13-6, revised 11/29/50 - Layout of Stair #35

Will you please return two (2) prints of the above drawing marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH*eab



[Signature]

ISSUANCE OF DRAWINGS

OFFICE COPY

30 November 1950

15 December 1950

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by General Bronze & Halback

2 H-GP-13-6 13Nov'50 Layout of Stair #35

(APPROVED 5 Dec 1950 P.B.)




L. V. Tyler

*Must
Stopper
Hannegan*

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 30, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
405 East 42nd Street
New York 17, N. Y.

RE: CONTRACT HQ 1/82 - GENERAL ASSEMBLY & NORTH PARKING SPACE
Reinforcing Steel Details

Dear Mr. Dawson:

We are sending you herewith for approval six (6) copies each of the following reinforcing steel details submitted by Brennan & Sloan, Inc. and Knickerbocker Construction Corporation:

- 1301, corrected 11/13/50 - "Bottom Bar Layout, Div. #1,
1st Floor"
- 1302, corrected 11/27/50 - "Top Slab Bars, Div. #1, 1st Floor"
- 2202, corrected 11/27/50 - "Top Slab Bar Layout, Div. #2,
1st Base."
- 2301, corrected 11/27/50 - "Top & Bottom Slab Bars, Div. #2,
1st Floor"
- 4101, corrected 11/27/50 - "Top & Bottom Slab Bars, Div. #4,
2nd Base."
- 6101, corrected 11/27/50 - "Top & Bottom Slab Bars, Div. #6,
2nd Base."
- C4101, corrected 11/27/50 - "Bar Layout for Curbs, Div. #4 & #5,
2nd Base."
- C2203, corrected 11/27/50 - "Curbs on H and G Lines, Div. #1 & #4,
1st Base."

Will you please return three (3) copies each of the above drawings marked with your approval or necessary correction.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese BK
C. E. Reese
Project Engineer

[Signature]
12/11



ISSUANCE OF DRAWINGS

OFFICE COPY

30 November 1950

13 December 1950

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Brennan & Sloan & Knickerbocker


3	1302	2 Oct'50	Top Slab Bars Div. #1, 1st fl.
3	2202	16Sept'50	Top Slab Bar Layout, Div. #2, 1st Bmt.
		4 Oct'50	
3	4101		Top & Bottom Slab Bars, Div. #4, 2nd Bmt.
3	GA101	20Nov'50	Bar Layout for Curbs Div. 4 & 5, 2nd Bmt.

(ALL "APPROVED" 8 Dec R.E.N.)

3	2301	3 Oct'50	Top & Bottom Slab Bars, Div. #2, 1st fl.
3	6101	28Oct'50	" " " " " " #6, 2nd Base.
3	02203	31Oct'50	Curbs on H & G Lines. Div. 1 & 4, 1st base.

(APPROVED AS NOTED 8 Dec 1950 R.E.N. RESUBMIT)

NOTE: Dwg. 1301 will follow



SV Zifer

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 30, 1950



*Asst
Hoffen-Rumpel
Saunegau
12/5
SWS*

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York, New York

Gen Files

Re: Contract HQ 1/82 - General Assembly and North Parking Space
Heating, Ventilating and Air Conditioning
Vibration Eliminators for Fan Systems

Dear Sir:

We are submitting herewith six copies of the Vibration Eliminator Co. Drawings No. 25260-1 to 25260-57 inclusive and Drawing No. 25260-59 to 25260-68 inclusive for the Vibration Eliminators being furnished by the Vibration Eliminator Co. for Kerby Saunders, Inc., the heating, ventilating and air conditioning subcontractor.

We request the return of three copies of each of the above drawings together with your approval and/or comments at your earliest convenience.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
Project Engineer

CER:WWS:bc

WWS Ret'd 19 Dec 1950



FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 30, 1950

RECEIVED

DEC 1 1950

United Nations Headquarters

JAMES A. DAWSON

(Co-ordinator of Construction)

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York, New York

Re: Contract HQ1/82 - General Assembly and North Parking Space
Heating, Ventilating and Air Conditioning
Buffalo Forge Co. Shop Drawings

Dear Sir:

We are submitting herewith six (6) copies of each of the following Buffalo Forge Co. drawings for fans for the General Assembly being furnished under the Heating, Ventilating and Air Conditioning sub-contract of Kerby Saunders, Inc.

Buffalo Forge Co. Drawing No.	7W-19797, Fan Drawing for System 404-8
" " " " "	5W-19767, Fan Drawing for System 403-6,-7
" " " " "	7W-19785, Fan Drawing for System 401-1,-2

Buffalo Forge Co. Fan Schedule for all Systems.

Please review the above and return three (3) copies together with your approval and/or comments.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER:WWS:bc



Handwritten signature
12/4

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 30, 1950

DEC 1 1950

United Nations Headquarters
JAMES A. DAWSON
(Coordinator of Construction)

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Orn. Metal

We are sending you herewith four (4) prints each of the following Ornamental Metal shop drawings submitted by General Bronze Corporation and C. E. Halback & Co:

GB-A-2, dated 11/27/50 - Louvers at East Podium Wall

GB-A-3, " " - " " " " " " F.S.D.

Will you please return two (2) prints each of the above drawings marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH*ab

RECEIVED

DEC 4 1950

United Nations Headquarters
W.K. Harrison, Director of Planning

12/11

ISSUANCE OF DRAWINGS

OFFICE COPY

30 November 1950

7 December 1950

GA & North Parking

Fuller-Turner-Walsh-Slaterry

hand

Submitted by General Bronze & Halback

2	GB-A-2	27Nov'50	Louvers at East Podium Wall
2	GB-A-3	"	" " " " " F.S.D.

(APPROVED 6 Dec 1950 P.B.)



Handwritten signature or initials in the bottom right corner.

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 30, 1950



to Gen. Fick

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd St.
New York 17, N. Y.

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Misc. Iron

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawing submitted by General Bronze Corporation and C. E. Halback & Company:

H.G.P. 35-2, revised 11/28/50 - Expansion Joint at
Fire Tower Court
between Garage &
General Assembly
(N.P.)

Will you please return two (2) prints of the above drawing marked with your approval or necessary corrections.


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH*ead



J. H. H.



ISSUANCE OF DRAWINGS

OFFICE COPY

30 November 1950

5 December 1950

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by General Bronze & Halback

2 H-GP-35-2 26Oct'50 Exp. Joint at Fire Tower Court bet. Garage & GA (NP)
(APPROVED 5 Dec 1950 R.E.N.)



LV [signature]

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 30, 1950

RECEIVED

DEC 1 1950

United Nations Headquarters

JAMES A. DAWSON

(Co-ordinator of Construction)

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Misc. Iron

We are sending you herewith one (1) print each of the following Miscellaneous Iron shop drawings as approved for field distribution:

H.G.P. 13-2, revised 11/13/50 - Layout of Stair No. 1

H.G.P. 13-3, " " - " " " " 9

H.G.P. 13-4, " " - " " " " 8

H.G.P. 44-1, dated " - Transformer Vault Gratings & Frames

(General Bronze Corporation & C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH*ead



[Handwritten signature]
11/24

- 9 ✓

November 30, 1950

Dear Mr. Dawson:

We are sending you herewith one (1) print each of the following Miscellaneous Iron shop drawings as approved for field distribution:

H.G.P. 44-1, dated " - Transformer Vault Gratings & Frames

Very truly yours,

C. E. Reese

MH**eab*

-9✓

November 30, 1950

Dear Mr. Dawson:

We are sending you herewith one (1) print each of the following Miscellaneous Iron shop drawings as approved for field distribution:

H.G.P. 13-3, " " - " " " " 9

H.G.P. 13-4, " " - " " " " 8

(General Bronze Corporation & C. E. Halback & Co.)

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
Project Engineer

MH*cab

-9-

UNITED NATIONS CONTRACT

NEW YORK

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/62 - General Assembly
& North Parking Garage - Misc. Iron

We are sending you herewith one (1) print each of the following Miscellaneous Iron shop drawings as approved for field distribution:

H.G.P. 13-3, " " - " " " " 9

H.G.P. 13-4, " " - " " " " 8

H.G.P. 44-1, dated " - Transformer Vault Gratings & Frames

(General Bronze Corporation & C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

SH#eab

170-5-18-9 ✓
cc: Harrison
Zunser
McLeod
Van Name
Healy
Hopper
Dawson

30 November 1950

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, N.Y.

Re: Contract HQ 1/82 - General Assembly
and North Parking Garage
Notification of Change No. 3 (Change No. 23)
Structural Changes

Gentlemen:

Attached hereto is one copy of Notification of Change
No. 3 (Change No. 23) approved by Joseph Zunser for the United
Nations.

This approval is given for you to proceed with the work
required by the modification with reference to the structural changes.

It is understood that this approval does not include the
cost of this change as indicated in the Notification of Change No. 3,
which is solely an approximation. It is understood, also, that the
actual price adjustment will be made as required by the terms of the
contract.

Very truly yours,

Enclosure
JZ:ml

Joseph Zunser
Assistant Co-Ordinator of Construction

100-5-18-9 ✓

cc: Harrison
McLeod
Zunser
Van Name
Hopper
Healy
Dawson

30 November 1950

Fuller-Turner-Walsh-Slaterry, Inc.
403 East 42nd Street
New York 17, N.Y.

Re: Contract HQ 1/82 - General Assembly
and North Parking Garage
Notification of Change No. 2 (Estimate Requested)
Revisions to Roof Gutter Expansion Joint Details

Gentlemen:

Returned herewith is one copy of Notification of Change
No. 2 (Estimate Requested).

We believe that the work included in this Notification of
Change is required by the contract and that additional authorization
to proceed with this work is not necessary.

Very truly yours,

Enclosure

JZ:ml

Joseph Zunser
Assistant Co-Ordinator of Construction

30 November 1950

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Northerly
Portion of the Parking Garage
Contract HQ 1/82
Glass and Glazing

Gentlemen:

Please refer to our Drawing No. RA-110, Revision No. 1,
dated 21 August 1950.

On the details for the glass screen in vestibules Nos.
1 and 2, we have noted Tempered Glass. Be advised that this
note will be changed to read 1/4" clear Polished Plate Glass.

Please proceed accordingly.

Very truly yours,



Joseph Zunser
Assistant Co-Ordinator of Construction

JJHe:eam
cc: Bohanon
Nelson
Weigel
Healy
Harris
Hopper
~~Zunser~~
Dawson
VanName

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 29, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
405 East 42nd Street
New York 17, N. Y.

RE: Contract HQ 1/82 - General Assembly and North Parking Space
Change No. 56
November 21, 1950 Structural Revisions

References:

- (a) U.N. Drawing GA-WS-133A, dated Oct. 25, 1950, Issued 11/20/50
- (b) " " GA-WS-149, dated 9/13/50 " "
- (c) " " GA-5-CS-3, dated 8/28/50 " "
- (d) " " GA-1-CS-B1, Sheet 1, dated 11/9/50, Issued 11/20/50
- (e) " " " Sheet 2, " " " "
- (f) Mr. James A. Dawson's letter of November 20, 1950

Dear Mr. Dawson:

On November 21, 1950, we received prints of References (a) thru (e) inclusive. On November 27, 1950, we received your transmittal letter, Reference (f), which reads, in part, as follows:

"All of these drawings are amplification drawings causing no change to the Contract Price. Proceed with the work shown thereon if you agree with this statement. If not, promptly notify us of your investigation."

We have sent these drawings to the subcontractors involved and have requested that they notify us promptly of any changes to their contract price.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/lbr

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 29, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
405 East 42nd Street
New York, N. Y.

RE: HQ 1/82 Contract - General Assembly and
North Parking Space
Metal Furring and Lath

Dear Mr. Dawson:

We are listing below, in lieu of the sample requirements contained in Paragraph 20-06 General Assembly Specifications, materials which Jeremiah Burns, Inc. have proposed for use in the above project:

- (a) 2" x $\frac{1}{2}$ " x $\frac{1}{8}$ " - 1.37# Hot Rolled Channel (see attached sample)
- (b) $\frac{3}{4}$ " - 0.30# Hot Rolled Channel (see attached sample)
- (c) 1" x $\frac{1}{8}$ " Flat Iron, Painted
- (d) Milcor No. 8 Bullnose Exp. Corner Bead, $1\frac{1}{2}$ " Radius
- (e) 2" Fibreglas, 2 $\frac{1}{2}$ # Density

Items (a) and (b) are proposed for use in both the Meeting Halls and General Assembly.

Jeremiah Burns also proposes to use in the General Assembly the following items previously approved by you for use in either the Secretariat and/or Meeting Halls:

- MH (f) 3.4 Black Painted Diamond Mesh Lath
- MH (g) $1\frac{1}{2}$ " Hot Rolled Channel
- MH (h) 1" Hot Rolled Channel
- MH (i) 1" x $\frac{3}{16}$ " Flat Iron, Painted
- MH (j) 2 $\frac{1}{2}$ " Hairpin, #8 ga., galvanized
- MH (k) Milcor No. 1 Exposed Corner Bead
- MH (l) Milcor No. 3 Exposed Base Screed
- MH (m) Milcor No. 66 Plaster stop
- (n) 12 ga. White Metal Terrazzo Strip

May we have your approval or comments on the above mentioned materials?

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER/PDV/lbr

Copy to Dawson for info -
on Change No. 1 GA.

120-5-18-7
OREGON 9-3950

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 29, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
405 East 42nd Street
New York 17, N. Y.

RE: HQ 1/82 Contract - General Assembly and
North Parking Space
Ceramic Tile - Change No. 1

Dear Mr. Dawson:

Contract drawings No. A-2 and A-16, both dated
May 15, 1950, show a requirement for a ceramic tile wainscot
in locker room 2B4.

At the time of bidding, we instructed the
bidders to figure on a 4'-3" \pm high wainscot on the east
and south walls only, since the north and west walls were
hidden by lockers.

In Change No. 1, the wainscot for this space
has been omitted and our estimate for this change will be
based on the deletion of wainscot on the east and south walls
only.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER/PDV/lbr



11/30

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 29, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
and North Parking Space - Change No. 33
Change Sheet GA-PS-2B CS #12

On November 17, 1950, Mr. Walter Hopper gave me verbal instructions by 'phone that we were to have Brennan & Sloan, Inc. and Knickerbocker Construction Corporation proceed immediately on a Time and Material basis with the work required by United Nations drawing GA-PS-2B-CS-#12, dated October 19, 1950.

We have so instructed the subcontractor.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER*ead



R 11/29

-9✓

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
NEW YORK

November 29, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
and North Parking Space - Change No. 33
Change Sheet GA-PS-2B CS #12

On November 17, 1950, Mr. Walter Hopper gave me verbal instructions by 'phone that we were to have Brennan & Sloan, Inc. and Knickerbocker Construction Corporation proceed immediately on a Time and Material basis with the work required by United Nations drawing GA-PS-2B-CS-#12, dated October 19, 1950.

We have so instructed the subcontractor.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

CER:eab

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 29, 1950



Col. Fick

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Misc. Iron

We are sending you herewith four (4) prints each of the following Miscellaneous Iron shop drawings submitted by General Bronze Corporation and C. E. Halback & Co:

- H.G.P. 1-1, dated 11/22/50 - Pipe Railings - Stairs
4, 5, 6 & Ramp Nos. 2 & 3
- H.G.P. 1-2, " " - Pipe Railings - Stair #7
and #8
- H.G.P. 1-3, " " - Pipe Railings - Stair #9
and #10.


(N.P.S.)

Will you please return two (2) prints each of the above drawings marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer



ISSUANCE OF DRAWINGS

OFFICE COPY

26 Dec. 1950

Pk. Space NH

Fuller-Turner-Walsh-Slaterry, Inc.

Mr. Blumquist

UN

2 copies each of H-GP-1-1 22Nov1950 Pipe Railing

H-GP-1-3 " Pipe Railing Stair No. 9 and 10

H-GP-1-2 " Pipe Railing Stair No. 7 and 8

all approved as noted 22Dec.1950 resubmit R.Nelson

Gen. Bronze dwgs.

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 29, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
405 East 42nd Street
New York 17, N. Y.

Re: HQ 1/82 Contract - General Assembly & North Parking Space
Built-Up Roofing and Waterproofing

Dear Mr. Dawson:

We are submitting herewith for your approval the following list of materials which the New York Roofing Company proposes to use for the above project:

WATERPROOFING:

Barrett's Black Diamond Felt
Barrett's Black Diamond Fitch

ROOFING:

Barrett's Specification Felt
Barrett's Specification Pitch
White Marble Chips, manufactured by the Universal Marble Products Corp., Thornwood, N.Y. (Identical to sample submitted this date for use in the Meeting Halls). This item is specified by - Item 6, Section 10, of the U.N. Comments on the Contractor's Addenda, April 20, 1950.

In regard to the 1-1/2" Fibreglas now specified by Item 1, Section 10 of the "Black Book," New York Roofing Company suggests that other insulating materials be used which would withstand traffic better. Before submitting samples of the Fibreglas, will you please advise us whether you contemplate changing the 1-1/2" Fibreglas to 3" Permalite insulation, as was done on the Meeting Halls.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER/PDV/lbr


FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 29, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Metal Toilet
Enclosures, Screens & Doors

We are sending you herewith four (4) prints of the following shop drawings submitted by Scherbak Specialties Company:

~~451~~, no date - Weis Steel Toilet Partitions &
S. S. Doors
(G.A. & N.P.)

Will you please return two (2) prints of the above drawing marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH*ab

P.S. We are enclosing one color chart. Will you please advise us as to the color you wish for the partitions.




FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 29, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Approved
Shop Drawings

We are sending you herewith, for your information, one
(1) print of the following Miscellaneous Iron shop drawing as ap-
proved for field distribution:

H.G.P. 3-1, revised 11/14/50 - Steel Elevator Pit Ladders
(N. Parking Sp.)

(General Bronze Corp. & C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH*ead



[Handwritten signature]
11/30

-9-

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
NEW YORK

November 29, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
 & North Parking Garage - Approved
 Shop Drawings

We are sending you herewith, for your information, one
(1) print of the following Miscellaneous Iron shop drawing as ap-
proved for field distribution:

H.G.P. 3-1, revised 11/14/50 - Steel Elevator Pit Ladders
(N. Parking Sp.)

(General Bronze Corp. & C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH*ead

-9-

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
NEW YORK

November 29, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
 & North Parking Garage - Approved
 Shop Drawings

We are sending you herewith, for your information, one
(1) print of the following Miscellaneous Iron shop drawing as ap-
proved for field distribution:

H.O.P. 3-1, revised 11/14/50 - Steel Elevator Pit Ladders
 (N. Parking Sp.)

(General Bronze Corp. & C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH:eab

-9-

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
NEW YORK

November 29, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
 & North Parking Garage - Approved
 Shop Drawings

We are sending you herewith, for your information, one
(1) print of the following Miscellaneous Iron shop drawing as ap-
proved for field distribution:

H.G.P. 3-1, revised 11/14/50 - Steel Elevator Pit Ladders
(N. Parking Sp.)

(General Bronze Corp. & C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH*esb

1-70-5-18-9 ✓
29 November 1950

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42 Street
New York 17, New York


Re: General Assembly and Northerly
Portion of the Parking Garage
Contract HQ 1/82 - Electrical

Gentlemen:

Under separate cover, as of even date, we are forwarding you
the following items:

1. Ten copies of a Memorandum Specification covering
the Special Lighting Fixtures.
2. Ten copies of a letter from Syska & Hennessy to
us reference the Special Lighting Fixtures.
3. Twenty-one copies of Addendum No. 1 to Part V,
Section D, Electrical Work and Fixtures of the
Contract Documents.
4. Ten copies of a letter from Syska & Hennessy to
us dated 22 November 1950 reference the above
noted Addendum.

Very truly yours,



JJHe:eam

Joseph Zunser
Assistant Co-Ordinator of Construction

cc: Bohanon
Nelson
Weigel
Healy
Harris
Hopper
Dawson
VanName
Ryer Hannegan Seelman S & H (2)

140-5-18-9
29 November 1950

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Northerly
Portion of the Parking Garage
Contract HQ 1/82 - Glass and Glazing

Gentlemen:

Please refer to our letter to you of 23 October 1950 and in particular to the last paragraph. In this last paragraph we notify you that we accepted Alternate No. 2 which was to the effect that Tempered glass was to be used in the railing of exterior Stair No. 37 at an additional cost of \$90.00.

We now have decided to eliminate this Tempered glass from this railing and request that you furnish for our consideration the deductions from the Contract Price due to its deletion.

This means that we do not desire glass of any kind in this railing.

Very truly yours,

J. He

JJHe:eam

cc: Bohanon
Nelson (2)
Weigel
Healy
Harris
Hopper
~~Zunser~~
VanName
McLeod
Dawson

Joseph Zunser
Assistant Co-Ordinator of Construction

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 28, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York, New York

Re: Contract HQ 1/75 - Meeting Halls and Cover Over East
River Drive
Motor Controls in Fan Room # 1 to # 22

Dear Sir:

We understand that some of the control centers in the above mentioned fan rooms are to be or are being eliminated which should result in a credit under the established method of handling Meeting Hall Change orders for Fischbach & Moores, Inc.

We have further checked into the heating, ventilating and air conditioning specifications and there is apparently nothing there to indicate that Kerby Saunders, Inc. would be required to furnish controls, other than lock-stop buttons for motors in the above fan rooms.

Reviewing the Black Book and information available at hand, we have been unable to determine at the present time who is to furnish these controls due to the omission of certain of the control centers.

Please advise this office if the electrical sub-contractor is to furnish these under the method for handling changes for Meeting Halls, or have the heating, ventilating and air conditioning sub-contractor furnish them under an extra to his sub-contract. The usual method for furnishing individual controls for H.V. & A.C. equipment would be for the H.V. & A.C. sub-contractor to furnish same.

As the above items are critical material, please let us hear from you as soon as possible.

Very truly yours,
FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER:WWS:bc

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 28, 1950

*File
11/28/50*

File

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
 & North Parking Garage - Approved
 Shop Drawings

We are sending you herewith two (2) copies each of the
following reinforcing steel details as approved for field distri-
bution:

Nos. 2201, 3201 and 3301

(Brennan & Sloan, Inc. & Knickerbocker Construction Corp.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
Project Engineer

BK**eab*



*P
11/28*

-9✓

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
NEW YORK

November 28, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
 & North Parking Garage - Approved
 Shop Drawings

We are sending you herewith two (2) copies each of the
following reinforcing steel details as approved for field distri-
bution:

Nos. 2201, 3201 and 3301

(Brennan & Sloan, Inc. & Knickerbocker Construction Corp.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

BK*ead

-9-

UNITED NATIONS CONTRACT
NEW YORK

November 28, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
 & North Parking Garage - Approved
 Shop Drawings

We are sending you herewith two (2) copies each of the following reinforcing steel details as approved for field distribution:

Nos. 2201, 3201 and 3301

(Brennan & Sloan, Inc. & Knickerbocker Construction Corp.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

L. E. Reese

C. E. Reese
Project Engineer

BK#eab

-9-

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
NEW YORK

November 28, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
 & North Parking Garage - Approved
 Shop Drawings


We are sending you herewith two (2) copies each of the
following reinforcing steel details as approved for field distri-
bution:

Nos. 2201, 3201 and 3301

(Brennan & Sloan, Inc. & Knickerbocker Construction Corp.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.


C. E. Reese
Project Engineer

BK*ead


FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 28, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

*File
11/28/50*

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Approved
Shop Drawings

We are sending you herewith one (1) print of the following steel sash shop drawing as approved for field distribution:

NY7321 C-1, dated 10/25/50 - Commercial Steel Windows
by Detroit Steel Products
(N.P.S.)

(General Bronze Corporation & C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH:eab



*File
11/28/50*

-9-

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

NEW YORK

November 28, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
 & North Parking Garage - Approved
 Shop Drawings

We are sending you herewith one (1) print of the following steel sash shop drawing as approved for field distribution:

NY7321 C-1, dated 10/25/50 - Commercial Steel Windows
 by Detroit Steel Products
 (N.P.S.)

(General Bronze Corporation & C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH*ead

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
NEW YORK

November 28, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
 & North Parking Garage - Approved
 Shop Drawings

We are sending you herewith one (1) print of the following steel sash shop drawing as approved for field distribution:

NY7321 C-1, dated 10/25/50 - Commercial Steel Windows
 by Detroit Steel Products
 (N.P.S.)

(General Bronze Corporation & C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MI*ead

-9-

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
NEW YORK

November 28, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
 & North Parking Garage - Approved
 Shop Drawings

We are sending you herewith one (1) print of the following steel sash shop drawing as approved for field distribution:

NY7321 C-1, dated 10/25/50 - Commercial Steel Windows
by Detroit Steel Products
(N.P.S.)

(General Bronze Corporation & C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MI#eab

cc: Zunser
Hopper
Hannegan
Van Name

28 November, 1950

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York

Attention: Mr. C. E. Reese, Project Engineer
Re: Parking Space - North Half - Contract HQ 1/82
Parking Space - South Half - Contract HQ 1/74
Meeting Halls - Contract HQ 1/75
Frostproofing of Water Lines

Gentlemen:

In answer to your letter dated 6 November, 1950, in which you make the following suggestions in order to avoid freezing of water lines in the following locations:

1. - North Parking: Acceptance of Alternate #1 in Eugene Duklauer, Inc. Contract for frost proofing of temporary water main in the 3rd basement of the Parking Space North Half.
2. - Meeting Halls: Acceptance of Alternate #1 in Eugene Duklauer, Inc. Contract for complete winter protection, including insulation of exposed pipe lines, and other pipe lines not included in heated areas.
3. - Meeting Halls: Frost proofing of temporary fire stand pipe.
4. - Meeting Halls: Frost proofing of temporary water lines other than fire standpipe and that covered by item 2 above.
5. - South Parking: Frost proofing of Sprinkler Lines or shutoff valves and water lines in exposed areas north of temporary metal partitions.
6. - South Parking: Ramp #8 Panel Heating Coils. Frostproofing piping through Fresh Air Plenum to Fan Room #2. However, Kerby Saunders, Inc. advise the ethylene glycol solution used in this system would stand a 0° fahrenheit temperature.

- 2 -

Fuller-Turner-Walsh-Slattery, Inc.

28 November, 1950

Please be advised, the above suggested items of work of frostproofing are not accepted.

We refer you to your letter of 22 November, 1950, covering protection of water lines in open areas in the Parking Space - South Half and your letter of the 13 November, 1950, covering frostproofing of temporary water and fire lines in the Meeting Halls and Parking Space - North Half, both letters have been answered by this office under date of 27 November, 1950.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction

JJHa:mj

120-5-18-9
28 November 1950

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Northerly
Portion of the Parking Garage
Contract HQ 1/82
Concrete and Structural


Gentlemen:

As of even date we are forwarding you twenty-five (25) copies of drawing No. GA-1-CS-40, revised 24 November 1950. You will note the angle brackets are being removed from the columns. Proceed with the work shown thereon. In our opinion there should be no change to the Contract Price.

Please refer to our letter of 9 November 1950. You will note in this letter that we previously issued this drawing to you. This letter voids the previous issue of this drawing.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction


JJHe:eam

cc: Bohanon
Nelson
Weigel
Healy
Harris
Hopper
Zunser
VanName
Hannegan
Ryer

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 27, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Re: Contract HQ 1/82 - General Assembly & North Parking Space
CHANGE NO. 58 and Estimate for Change No. 58 Combined -
Acceptance of James Cullo & Son Marble Company's Alternate No. 1

Reference: Mr. James A. Dawson's letter of 22 November 1950
approving the award of subcontract for Cut Stone
Work and Exterior Marble (Section 9) and Interior
Marble Work (Section 17) to James Cullo & Sons
Marble Co., Inc.

Dear Mr. Dawson:


On November 24, 1950 we received the above "Reference"
letter which advised us that you are thereby accepting Alternate
No. 1 which reads as follows:

"Alternate 1. If the Vermont Marble Company's
"Lumar-Luminous" Translucent Marble Work in
the North Wall of the General Assembly Build-
ing is omitted - DEDUCT from the Subcontract
price the sum of Forty-Two Thousand Seven
Hundred Ninety-Seven Dollars and 00/100.....
(\$42,797.00). "

Your acceptance of this Alternate reduces our maximum
guaranteed cost price by the lump sum amount of \$42,797.00. For
accounting purposes we are identifying this reduction in cost
as our Change No. 58.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.


M. J. Grogan
Project Manager

MJG:CER*ead

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 27, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Parking Space
Heating, Ventilating and Air Conditioning
Shop Drawings

Dear Sir:

We are submitting herewith six (6) copies of each of the following shop drawings for materials and equipment being furnished under the heating, ventilating and air conditioning subcontract of Kerby Saunders, Inc.

Buffalo Forge Co.	Drawing No.	5W-15874, Fan Dimension Sheet
"	"	5W-15873, Fan Dimension Sheet
"	"	4W-10705, Fan Dimension Sheet
"	"	5W-10709, Fan Dimension Sheet
"	"	4W-10706, Fan Dimension Sheet
"	"	5W-10703, Fan Dimension Sheet
"	"	5W-10702, Fan Dimension Sheet
"	"	3V-6210A, Revision D, Fan Dimension Sheet
Kerby Saunders, Inc.	"	50-52-SK-1, Pipe, Fitters, Valve & Hanger Schedule
Nash Engineering Co.	"	SWD-4577, Wiring Diagram for vacuum pump in 2nd basement North Parking
"	"	NDE-17B, Dimension print for vacuum pump in 2nd basement North Parking
"	"	SWD-3750, Operating instructions for vacuum pump in 2nd basement North Parking
"	"	MTE-34, Installing detail for vacuum pump in 2nd basement North Parking
"	"	SWD-4526, Wiring diagram for condenser pump in Fan Room No. 8 North Parking
"	"	NGO-35A, Dimension plant for condenser pump in Fan Room No. 8 North Parking
"	"	NGD-30A, Dimension plant for condenser pump in Fan Room No. 8 North Parking
"	"	SWD-4506, Wiring diagram for vacuum pump for General Assembly

Supp. Let'd 19 Dec. 1950

P 11/27

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York, New York

- 2 -

November 27, 1950

Re: Contract HQ 1/82 - General Assembly and North Parking Space
Heating, Ventilating and Air Conditioning
Shop Drawings

Nash Engineering Co.	Drawing No.	K-4316,	Dimension Sheet for vacuum
"	"	"	pump in General Assembly
"	"	"	NIE-30, Installation detail for vacuum
"	"	"	pump in General Assembly
"	"	"	SWD-3750, Operating instructions for
"	"	"	vacuum pump in General Assembly

Please review the above drawings and return three (3) copies together with your approval and/or comments. Prompt attention being given to the above will be appreciated as these are critical materials.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER:WWS:bc



Hopper
Nealy
11/28
LW
FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 27, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

to J. A. Dawson
File

Dear Mr. Dawson: Re: Contract HQ 1/82 - General Assembly
and North Parking Garage - Misc. Iron

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawing submitted by General Bronze Corporation and C. E. Halback & Company:

H.G.P. 6-2, revised 11/21/50 - Door Frames for
Type R10, S1 & S2
(N.P.)

Will you please return two (2) prints of the above drawings marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

PDV*ead



ISSUANCE OF DRAWINGS

OFFICE COPY

27 November 1950

5 December 1950

GA & North Parking

Fuller-Turner-Walsh-Slaterry

hand

Submitted by General Bronze & Halback

2 H-GP-6-2 6 Nov '50 Door Frames for Type R10, S1 & S2 (NP)
(APPROVED 30 Nov 1950 R.E.N.)



J. V. Tyler

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 27, 1950

RECEIVED

NOV 28 1950

United Nations Headquarters

JAMES A. DAWSON

Co-Ordinator of Construction

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Cut Stone

We are sending you herewith four (4) prints of the following Cut Stone shop drawing submitted by Monahan-McCann Stone Co:

788-3B, dated 11/20/50 - Layout of East & West Walls
General Assembly

This drawing is supplemental to drawings Nos. 788-3 and 3A and shows both coordinate and arc dimensions in relation to the column centerlines, as discussed with your Mr. P. Bohanon.

Will you please return two (2) prints of the above drawing marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

PDV:eab



ISSUANCE OF DRAWINGS

OFFICE COPY

27 November 1950

5 December 1950

GA & North Parking

Fuller-Turner-Walsh-Slattery

hand

Submitted by Monahan-McCann

2

788-3B

20Nov'50

Layout of East & West Walls - GA

(APPROVED AS NOTED 4 Dec 1950 P.B. RESUBMIT)



120.5-18-9

cc: Zunser
Hopper
Hannegan
Seelman
Van Name
McLeod

27 November, 1950

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York


Attention: Mr. C. E. Reese, Project Engineer
Re: General Assembly and Parking Space - North Half
Contract HQ 1/82 - (Additional Telephones)

Gentlemen:

We acknowledge receipt of your letter dated 9 November, 1950, requesting approval and authorization to proceed with the installation of temporary telephones in the following locations in the Parking Space - North Half and General Assembly:

N. P. - 2nd Basement	- South side of Col. I-24
" " " "	West side of Col. O-36.
G. A. - 1st Basement	- Near Col. L-22 (on South Side of Elev. Shaft #6).
" " " "	South Side of Col. O-24.
" " " "	East Side of Col. N-29
	near Col. J-31 (Outside of Stair #27).
G. A. - 2nd Basement	- Near K-31 (Outside Stair #30)
" " " "	Near L-22 (South Side of Elev. Shaft #6.
" " " "	Near O-31 (Outside of Stair #31)
G. A. - 4th Floor	- Near K-31 (Outside of Stair #30)

Please be advised, you are hereby authorized to proceed with the work. The cost shall be a direct charge applicable to the General Assembly and Parking Space - North Half Contract.

 In submitting your request for payment kindly furnish an itemized breakdown of cost.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction

JJHa:mj

120-5-18-9

cc: Zunser
Hopper
Hannegan
Van Name
McLeod

27 November, 1950

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42nd Street
New York 17, New York

Attention: Mr. C. E. Reese, Project Engineer
Re: Contract HQ 1/82 - General Assembly and
Parking Space - North Half, Plumbing Work,
Frostproofing of Temporary Water Lines

Gentlemen:

This will confirm our verbal authorization to your Mr. W. Simmons to notify your Plumbing Sub-Contractor, Eugene Duklauer, Inc., to proceed with the installation of 3/4" bleeder lines at the high point of each exposed temporary water risers in the Parking Space - North Half to avoid freezing of these lines. Also, to instruct your Plumbing Sub-Contractor to work one (1) plumber 1/2 hour overtime after 3:30 P.M. each day, five (5) days a week, to check and make sure that these bleeder lines are operating satisfactorily before leaving the Job-site.

Kindly submit for our consideration and/or approval a breakdown estimate of labor and materials necessary and required for the complete installation. The overtime involved shall be kept separately and the daily time sheets will be signed by our Plumbing Inspector.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction

JJHa:mj

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 24, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York 17, N. Y.

Re: General Assembly and North Parking Garage
Contract HQ 1/82 - CHANGE No. 53 -
November 16, 1950 Structural Revisions

References: (a) Dwg. GA-1-CS-35, Rev. No. 1, Issued 11/15/50
(b) " GA-WS-124, " " 1, " 11/15/50
(c) " GA-PS-CS-10, Issued 11/16/50
(d) " GA-WS-174C, dated 10/13/50
(e) " GA-WS-175, " 10/13/50
(f) Mr. James A. Dawson's letter of Nov. 15, 1950
(g) Mr. James A. Dawson's letter of Nov. 15, 1950

Dear Mr. Dawson:

On November 16, 1950, we received prints of References (a) through (e) inclusive.

On November 20, 1950, we received your transmittal letter, Reference (f), which reads as follows:

"On 15 November 1950 we forwarded you twenty-five
(25) copies of the following drawings:
GA-WS-124, Revised 10 November 1950
GA-1-CS-35, Revision No. 1, dated 15 November 1950

Drawing No. GA-WS-124 has been revised to show
corrections which do not affect the Contract Price.
Drawing No. GA-1-CS-35 has been revised to show a
change to lintel L3 which should cause no change
to the Contract Price.

Proceed with the work shown on these drawings."

On November 20, 1950, we also received your second transmittal letter
(Reference g) which reads as follows:

continued on page 2

Mr. James A. Dawson
Re: Contract HQ 1/82
Change No. 53 (cont)

-2-

November 24, 1950

"On November 15, 1950, we forwarded you drawings GA-WS-174C and WS-175C, both dated October 13, 1950. Before proceeding with any work indicated on these drawings, notify us of any cost changes to the Contract Price, if there are no changes in cost, proceed with the installation of the work."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan

M. J. Grogan
Project Manager

MJG:CER:ar
PDV

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 24, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Hollow Metal
Doors, Frames and Trim

In order to expedite the fabrication of the Hollow Metal Frames for the second and first Basements of the General Assembly, so as to allow early occupancy of certain portions of the building, may we request that you release Atlantic Metal Products, Inc.'s Schedule Sheets, numbers one to nine, inclusive, and Detail Sheets numbers D-1 to D-8 inclusive, prior to the balance of the Schedule Sheets.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH:eab

Returned As per Notes
5 Dec 1950.



[Signature]
11/27

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 24, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Masonry

Please refer to our letter of October 23, 1950 and your letter of November 9, 1950, in regard to a proposed substitution of Hanley Co. brick, Shade S-42, in lieu of the specified Darlington face brick, Shade 50.

In your letter you have disapproved the use of the Hanley brick based upon the difference in color as compared with the Darlington. You state that the Darlington No. 50 has been established as a standard on the earlier buildings of the project and its use is required for the General Assembly and North Parking Space.

May we ask that you reconsider the use of the Hanley brick in view of the following ramifying considerations:

- (a) The hard-burned Darlington brick has a lesser rate of absorption than the Hanley brick. This causes the denser brick to slip on its mortar bed unless great care is exercised in laying it. In any case, a leaky joint or a badly jointed panel may result.
- (b) The hardness of the Darlington brick may be disadvantageous since it has a greater tendency to chip, with a probability that it may shale off in the future.
- (c) At the time of the use of the Darlington brick in the Secretariat building, there was considerable difficulty experienced with the masons because of the fact that the brick was not union-made.

November 24, 1950

- (d) Since face brick is required on the Fire Tower Court walls, in both the North Parking Space and General Assembly, both interior locations, there would be no direct color comparison between the previous use of the Darlington brick on the Penthouse of the Secretariat and the proposed Hanley brick on the interior fire tower court walls of the General Assembly and North Parking Space.

In view of the difficulty experienced by John B. Kelly, Inc. in using the Darlington brick in the Secretariat, they strongly recommend that this brick not be used in the General Assembly and North Parking Space. Because of the difficulty in obtaining a well laid-up panel and because of the slow rate of production which results in using Darlington brick, may we request that you reconsider your previous disapproval of the Hanley Co. brick.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese.

C. E. Reese
Project Engineer

PDV:eab




FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 24, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

TOBRAW. FILE

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Cut Stone

We are sending you herewith four (4) prints of the follow-
ing Cut Stone shop drawing submitted by Monahan-McCann Stone Co:

788-3A, dated 11/17/50 - Details of Stone adjacent
to S. W. Entrance

This drawing modifies drawing 788-3, which has been approved,
with corrections, by you. The detail, shown hereon, makes the stone
joints centered over the Sculpture Block and Entrance, as requested by
you. Will you please indicate where the expansion joint is to be lo-
cated to suit the revised jointing.

If this drawing is approved by you, it will be incorporated
on drawing No. 788-3, when resubmitted.

Will you please return two (2) prints of the above drawing
marked with your approval or necessary corrections.


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese

Project Engineer



PDV*ead

*11/27*

ISSUANCE OF DRAWINGS

OFFICE COPY

24 November 1950

5 December 1950

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Monahan-McCann

2 788-3A 17Nov'50 Details of Stone adjacent to S.W. Entrance
(APPROVED AS NOTED 4 Dec 1950 P.B. RESUBMIT)



SV Tyler

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 24, 1950



To Gen. Flick

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Misc. Iron

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawing submitted by General Bronze Corporation and C. E. Halback & Company:

H.G.P. 8-1, revised 11/21/50 - Loose Lintels
(N.P.)

Will you please return two (2) prints of the above drawing marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*C. E. Reese
Project Engineer

MH:ab

cc - General Bronze Corporation



[Signature]
11/27

ISSUANCE OF DRAWINGS

OFFICE COPY

24 November 1950

8 December 1950

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by General Bronze & Halback

2 H-GP-8-1 31Oct'50 Loose Lintels (NP)

(APPROVED AS NOTED 7 Dec. 1950 P.B. RESUBMIT)

NOTE: See ~~XXXXXXXX~~ letter attached to dwgs.



J V Zifer

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 24, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Parking Space
Plumbing - Type 1 Roof Drains

Dear Sir:

We are resubmitting herewith six (6) copies of the Zurn Mfg. Co. Drawing No. 3812 for the Type No. 1 Roof Drains which Eugene Duklauer, Inc., the plumbing subcontractor, proposed to furnish in lieu of the Josam Mfg. Co. Drawing No. A-3329-K as they do not meet the specifications only as to size.

Please review the above drawing and return three (3) copies together with your approval and/or comments.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER:WWS:bc



[Signature]
11/27

ISSUANCE OF DRAWINGS

OFFICE COPY

24 November 1950

4 December 1950

GA & North Parking

Fuller-Turner-Walsh-Slattery

hand

Submitted by Duklauer (Zurn Mfg. Co. Dwg.)

3 3812 30Jan'48 Type No. 1 Roof Drains

(APPROVED AS NOTED 1 Dec 1950) (P.B. RESUBMIT)

NOTE: FROM SYSKA & HENNESSY

"This drawing is approved as noted in red crayon."

"All approvals are subject to strict compliance with the Contract Plans and Specifications and to all Authorities having Jurisdiction."



J. V. Sykes


FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 24, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Parking Space
W. D. Allen Fire Standpipe Equipment

Dear Sir:

We are submitting herewith six (6) copies each of the W. D. Allen booklet for the Fire Standpipe Equipment which they propose to furnish under the plumbing subcontract of Eugene Duklauer, Inc., for the North Parking Space and for the General Assembly Building.

Eugene Duklauer, Inc. requests that on the General Assembly booklet that they would/you to make notation on the copies of the following information:
like

- 1 - The hand of hinges in ~~valve~~ opening of the fire hose cabinets.
- 2 - The hand of hinges of the fire extinguisher cabinets.

Please review the above booklets and return three (3) copies of each together with your approval and/or comments.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER:WWS:bc



[Signature]
11/27

10/24
Hopper
Hannequin

-9-

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

November 24, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York, New York

Re: Contract No. 1/52 - General Assembly and North Parking Space
W. D. Allen Fire Standpipe Equipment

Dear Sir:

We are submitting herewith six (6) copies each of the W. D. Allen booklet for the Fire Standpipe Equipment which they propose to furnish under the plumbing subcontract of Eugene Buklauer, Inc., for the North Parking Space and for the General Assembly Building.

Eugene Buklauer, Inc. requests that on the General Assembly booklet that they would/you to make notation on the copies of the following information:

- Like*
- 1 - The hand of hinges in ~~the~~ opening of the fire hose cabinets.
 - 2 - The hand of hinges of the fire extinguisher cabinets.

Please review the above booklets and return three (3) copies of each together with your approval and/or comments.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CHM:Gbc



RECEIVED
NOV 22 1950
U.S. DEPARTMENT OF COMMERCE
BUREAU OF STANDARDS

SECRET

3112/39

UNITED STATES DEPARTMENT OF COMMERCE

BUREAU OF STANDARDS

SECRET
The following information is being furnished to you for your information only. It is not to be distributed outside your organization.

1 - The name of person or firm to whom the information is being furnished.

2 - The name of person or firm to whom the information is being furnished.

3 - The name of person or firm to whom the information is being furnished.

4 - The name of person or firm to whom the information is being furnished.

5 - The name of person or firm to whom the information is being furnished.

6 - The name of person or firm to whom the information is being furnished.

7 - The name of person or firm to whom the information is being furnished.

8 - The name of person or firm to whom the information is being furnished.

NEW YORK

UNITED NATIONS CONTRACT

ENGINEERING-MAGNET-GATTERY, INC.

COBY

Handwritten notes and signatures at the bottom left corner.

ISSUANCE OF DRAWINGS

OFFICE COPY

24 November 1950

14 December 1950

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by Duklauer (W.D. Allen Booklets)

3	Booklet	None	Fire Standpipe Equipment (GA) (APPROVED AS NOTED 12 Dec 1950 P.B. RESUBMIT)
3	"	"	Fire Standpipe Equipment (North Parking) (APPROVED 8 Dec 1950 R.E.N.)

NOTE: FROM SYSKA & HENNESSY

"The booklet for the North Parking is approved."

"The booklet for the General Assembly is approved as noted in red crayon, showing fire hose cabinets to read 13 with "144 sq. inch glass door panel" as requested by the Architect."

"All approvals are subject to strict compliance with the Contract Plans and Specifications and to all Authorities having Jurisdiction."



FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 24, 1950

RECEIVED

NOV 24 1950

United Nations Headquarters

JAMES A. DAWSON

(Co-ordinator of Construction)

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Reinforcing
Steel Details

We are sending you herewith, for approval, six (6) copies each of the following reinforcing steel details prepared by Brennan & Sloan, Inc. and Knickerbocker Construction Corporation:

3202, corrected 11/18/50 - Top Bar Layout Div. #3, 1st Bsmt.
5101, " 11/17/50 - Bottom Slab Bars, Div. #5, 2nd Bsmt.
5102, " " - Top Slab Bars, Div. #5, 2nd Bsmt.
C2204, " 11/16/50 - Raised Areas, 1st Bsmt. Divs. 1 & 2
ST101, " 11/17/50 - Detail of Stair No. 26 from Elev.
26'-7" to Elev. 40'-0-5/16"

Kindly return three (3) prints each of the above drawings marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



C. E. Reese
Project Engineer



ISSUANCE OF DRAWINGS

OFFICE COPY

24 November 1950

1 December 1950

GA & North Parking
Fuller-Turner-Walsh-Slaterry

hand

Submitted by Brennan & Sloan & Knickerbocker

2	5101	28Oct'50	Bottom Slab Bars, Div #5, 2nd Bmnt.
2	5102	"	Top " " " " " "

(APPROVED AS NOTED 1 Dec 1950 R.E.N. RESUBMIT)

One (1) copy of each of these dwgs. given to Brennan & Sloan & Knickerbocker

NOTE: Dwgs. 3202, C2204 and ST101 will follow



J. V. Tyler

Fuller-Turner-Walsh-Slaterry, Inc.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 24, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Parking Space
Trumbull Electric Mfg. Co.
Panel Details

Dear Sir:

We are submitting herewith six (6) copies of the Trumbull Electric Mfg. Co. drawing No. ENY-150-9 for panels No. LC1B1, LC1B2, PC1B1. These are being furnished under the electrical subcontract of Fischbach & Moore, Inc.

Please review the above drawings and return three (3) copies together with your approval and/or comments.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER:WWS:bc



ISSUANCE OF DRAWINGS

OFFICE COPY

24 November 1950

7 December 1950

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand


Submitted by Fischbach & Moore (Trumbull Elec. Dwg.)

3 ENY-150-9 18Oct'50 Panels No. LC1B1, LC1B2, PC1B1
(APPROVED AS NOTED 5 Dec 1950 P.B. RESUBMIT)

NOTE: FROM SYSKA & HENNESSY

"This drawing is approved as noted in red crayon."

"All approvals are subject to strict compliance with the Contract Plans and Specifications and to all Authorities having Jurisdiction."




FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 24, 1950



James

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Misc. Iron

We are sending you herewith one (1) print each of the following Miscellaneous Iron shop drawings as approved for field distribution:

H.G.P. 9-1, revised 11/3/50 - Expansion Joint at 1st
Basement, col. line 18AG
to 18 O. (N.P.)

H.G.P. 13-1, " 11/2/50 - Layout - Stair No. 15
(G.A.)

(General Bronze Corporation and C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*C. E. Reese
Project Engineer

MH*ead



A handwritten signature, possibly "C. E. Reese", with the date "11/27" written below it.

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

NEW YORK

November 24, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Misc. Iron

We are sending you herewith one (1) print each of the following Miscellaneous Iron shop drawings as approved for field distribution:

H.G.P. 9-1, revised 11/3/50 - Expansion Joint at 1st
Basement, col. line 18AG
to 18 O. (N.P.)

H.G.P. 13-1, " 11/2/50 - Layout - Stair No. 15
(G.A.)

(General Bronze Corporation and C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH*ead

-9-

UNITED NATIONS CONTRACT

NEW YORK

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Misc. Iron

We are sending you herewith one (1) print each of the following Miscellaneous Iron shop drawings as approved for field distribution:

H.G.P. 9-1, revised 11/3/50 - Expansion Joint at 1st
Basement, col. line 18AG
to 18 O. (N.P.)

H.Q.P.13-1, " 11/2/50 - Layout - Stair No. 15
(G.A.)

(General Bronze Corporation and C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH#eab

-9-

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
NEW YORK

November 24, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Misc. Iron

We are sending you herewith one (1) print each of the following Miscellaneous Iron shop drawings as approved for field distribution:

H.C.P. 9-1, revised 11/3/50 - Expansion Joint at 1st
Basement, col. line 18AG
to 18 O. (N.P.)

H.C.P. 13-1, " 11/2/50 - Layout - Stair No. 15
(G.A.)

(General Bronze Corporation and C. E. Halback & Co.)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH:eab

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 22, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York 17, N. Y.

Re: Contract HQ 1/82 - General Assembly and
North Parking Space - CHANGE NO. 52
Nov. 14 and Nov. 15, 1950 Structural Revisions

References: (a) U. N. Dwg. GA-S-29, dated 10/20/50, Issued 11/14/50
(b) " GA-WS-169, dated 10/23/50 " " " "
(c) " GA-WS-159, dated 9/22/50 " " " "
(d) " GA-WS-168, dated 10/16/50 " " " "
(e) Mr. James A. Dawson's letter of Nov. 15, 1950

Dear Mr. Dawson:

On November 14, 1950, we received prints of References (a), (b) and (d).
On November 15, 1950 we received prints of Reference (c).

On November 20, 1950, we received your transmittal letter, Reference (e),
which reads, in part, as follows:

"On 14 November 1950 we forwarded you twenty-five (25)
copies of the following drawings:

GA-WS-159, dated 22 September 1950
GA-WS-168, " 16 October 1950
GA-WS-169, " 23 October 1950

The above three drawings are amplification drawings
including necessary information for locating structural
steel. There should be no change to the Contract Price
due to the work shown thereon, but if you disagree with
this statement, please promptly notify us of your findings.
On the same date we forwarded you twenty-five (25) copies
of drawing GA-S-29, dated 20 October 1950. This drawing
is a collection of work sheets and voids previous work sheets,
the numbers of which have been indicated on this drawing.
Since the revisions shown on this drawing are either reference
changes or dimensional changes, there should be no Contract
Price change. "

continued on page 2

Mr. James A. Dawson
Re: Contract HQ 1/82
Change No. 52 (continued)


-2-

November 22, 1950

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-BATTERY, INC.



M. J. Grogan
Project Manager

MJG:CER:ah
PDV

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 22, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
405 East 42nd Street
New York 17, N. Y.

RE: HQ 1/82 Contract - General Assembly & North Parking Space
Change No. 48A
November 13, 1950 Structural Revisions

Reference (a) Mr. James A. Dawson's letter of Nov. 14, 1950

Dear Mr. Dawson:

This change is supplemental to our Change No. 48 dated November 14, 1950.

On November 15, 1950 we received your transmittal letter which reads, in part, as follows:

"Drawings GA-WS-74, GA-WS-74A, GA-WS-78 and GA-WS-78A are amplification drawings including necessary radii and dimensional locations of the steel framing. Drawing No. GA-LCS-7 has dimensional corrections. Therefore, there should be no cost change involved. Proceed with the work if you agree with this statement. If not, promptly notify us of the results of your investigation."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/lbr

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 22, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
405 East 42nd Street
New York 17, N. Y.

RE: HQ 1/82 Contract - GENERAL ASSEMBLY & NORTH PARKING SPACE
CHANGE NO. 47A
NOVEMBER 10, 1950 STRUCTURAL REVISIONS

References: (a) Mr. James A. Dawson's letter of November 14, 1950

Dear Mr. Dawson:

This change is supplemental to our Change No. 47, dated Nov. 13, 1950.

In regard to References (a) to (j) inclusive in Change No. 47, your transmittal letter reads as follows:

"We assume there will be no change to the Contract Price caused by the work indicated on the above drawings. If you are not in agreement, promptly notify us of your findings. If you agree that the Contract Price is not affected, proceed with the installation of the work."

In regard to Reference (k) in Change No. 47, your letter states that this drawing is merely amplification and:

"Therefore, there should be no cost change involved. Proceed with the work if you agree with this statement. If not, promptly notify us of the results of your investigation."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/lbr

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 22, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
405 East 42nd Street
New York 17, N. Y.

RE: HQ 1/82 Contract - General Assembly & North Parking Space
Change No. 46A
November 8, 1950 Structural Revisions

Reference: (a) Mr. James A. Dawson's letter of November 9, 1950

Dear Mr. Dawson:

This change is supplemental to our Change No. 46, dated November 13, 1950.

On November 13, 1950, we received Reference (a) above, which reads as follows:

"On 8 November 1950 we forwarded you twenty-five (25) copies of Drawings GA-1-CS-41, dated 1 November 1950 and GA-1-CS-42, dated 4 November 1950. Drawing GA-1-CS-41 indicates the field welding of cover plates which is purely structural. Since the concrete has not yet been poured there will be no change to the contract price. Drawing GA-1-CS-42 indicates framing for the elevator guide supports which need not be fireproofed. The work shown on this drawing will cause no change to the Contract Price."

We have requested that the subcontractors involved notify us of any cost changes brought about by these revisions. We will advise you promptly if no change is involved.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/lbr

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 22, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
Headquarters Planning Office
405 East 42nd Street
New York 17, N. Y.

RE: HQ 1/82 Contract - General Assembly & North Parking Space- Change No. 44A
November 7, 1950 Structural Revisions

Reference (a) Mr. James A. Dawson's letter of November 9, 1950.

Dear Mr. Dawson:

This change is supplemental to our Change No. 44, dated November 9, 1950.

On November 13, 1950 we received your transmittal letter of November 9, 1950 (Reference a), which reads as follows:

"The angle brackets shown on GA-1-CS-40 dated Oct. 31, 1950 were indicated on contract drawing A-109, dated May 5, 1950. Therefore, no change to the Contract Price will be caused by the work indicated on this drawing. Proceed with the installation of work as shown."

We understand that the angle brackets shown on GA-1-CS-40 will be installed by the American Bridge Co. and that the above statement applies to the contiguous work at the north columns of the General Assembly.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG/PDV/lbr

Hopper
Nealy
LWJ
11/24
FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 22, 1950

RECEIVED

NOV 24 1950

United Nations Headquarters

JAMES A. DAWSON

(Co-ordinator of Construction)

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Misch. Iron
and Ornamental Metal

We are sending you herewith four (4) prints of the following Miscellaneous Iron and Ornamental Metal shop drawing submitted by General Bronze Corporation and C. E. Halback & Company:

GB-A-1, dated 11/20/50 - Explosion Type Self-Closing
Louver (G.A.)

Please note that General Bronze requests you to verify the stone opening heights as shown on their detail and to clarify the relation of the stone jamb to column No. S-26 concrete fire-proofing.

Will you please return two (2) prints of the above drawing marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C.E. Reese
Project Engineer

RECEIVED

NOV 28 1950

United Nations Headquarters
W.K. Harrison-Director of Planning

MH:eab



11/24
m. 07.

ISSUANCE OF DRAWINGS

OFFICE COPY

22 November 1950

29 November 1950

GA & North Parking

Fuller-Turner-Walsh-Slaterry

hand

Submitted by General Bronze & Halback

2 GB-A-1 20Nov'50 Explosion Type Self-Closing Louver (GA)
(APPROVED AS NOTED 29-Nov 1950 P.B. RESUBMIT)



SV 2 for

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 21, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York 17, N. Y.

Re: Contract HQ 1/82 - General Assembly
and North Parking Space - CHANGE No. 42A
November 6, 1950 Structural Revisions

Reference: (a) Mr. James A. Dawson's letter of Nov. 3, 1950
(b) Mr. James A. Dawson's letter of Nov. 14, 1950

Dear Mr. Dawson:

This Change is supplemental to our Change No. 42, dated Nov. 7, 1950.

On November 9, 1950, we received Reference (a) above, which reads as follows:

"On 3 November we forwarded you twenty-five (25)
copies of the Change Bulletin No. 4, drawing No.
GA-PS-CS-9, dated 31 October 1950.

The changes indicated in this Bulletin are not changes
which will affect the Contract Price but are rectifying
discrepancies between architectural, structural and
other drawings. Therefore, proceed with the work indicated
therein since there will be no changes to the Contract Price."

On November 15, 1950, we received Reference (b), above, which reads, in
part, as follows:

"If you find that the work indicated on Drawing
GA-S-19 affects the Contract Price in any way,
promptly notify us of the change. If there is no
change, proceed with the work."

Under the authority and requirements of the contract, we hereby request
that proper adjustment of the contract price and contract time be dealt
with under the terms and conditions of the contract. This change will be
analyzed with all interested subcontractors and detailed estimates will be
submitted to you as quickly as possible. Definite extension of contract
time for completion will be requested as soon as determination can be made
of the effect of this change on the entire job progress.

Very truly yours,
FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan, Project Manager

MJG:CER:ar
PDV

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 21, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York 17, N. Y.

RE: Contract HQ 1/82 - General Assembly
and North Parking Garage - CHANGE NO. 41 A -
November 1, 1950 Structural Revisions

Reference: (a) Mr. James A. Dawson's letter of Nov. 3, 1950.

Dear Mr. Dawson:

This Change is supplemental to our Change No. 41, dated Nov. 7, 1950.

On November 9, 1950, we received your drawing transmittal letter of Nov. 3, 1950, (Reference a), which reads as follows:

"On 1 November 1950 we forwarded you twenty-five (25) copies of each of the following drawings:

GA-2-CS-7, dated 31 October 1950, GA-4-CS-7, dated
31 October 1950, and GA-5-CS-4, dated 26 October 1950.

Drawings GA-2-CS-7 and GA-4-CS-7 are drawings indicating the additional steel for the elevator guide supports at the 56'-0" and 86'-0" levels. The steel shown on these drawings needs no fireproofing, therefore there will be no change to the Contract Price. The drawings are sent for reference and record purposes.

Drawing GA-5-CS-4 indicates a change to the bottom cover plates on Girder 24K-N. The work indicated on this drawing will cause no change to the Contract Price."

We have sent these drawings to the subcontractors involved and have asked them to notify us if the structural changes will affect their costs. We will notify you promptly if no change is involved.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG:CER:ar
PDV

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 21, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York 17, N. Y.

Re: Contract HQ 1/82 - General Assembly and
North Parking Space - CHANGE NO. 36 A -
October 30, 1950 Structural Revisions

Reference (a) Mr. James A. Dawson's letter of November 3, 1950.

Dear Mr. Dawson:

This Change is supplemental to our Change No. 36, dated Nov. 7, 1950.

On November 9, 1950, we received your transmittal letter covering drawing GA-WS-163, revised 10/27/50, which reads in part, as follows:

"On October 27, 1950, we forwarded you twenty-five (25) copies of Drawing GA-WS-163, dated October 27, 1950. This drawing is an amplification drawing; there will be no change to the contract cost due to the work shown on this drawing. It is sent you for record and reference purposes."

We have sent this drawing to various sub-contractors and have asked for their comments concerning the changes involved. We will notify you promptly if no cost change is incurred.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

M. J. Grogan
M. J. Grogan
Project Manager

MJG:CER:AR
PDV

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 21, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York 17, N. Y.

RE: Contract HQ 1/82 - General Assembly and
North Parking Garage - CHANGE No. 22 C -
Sept. 28, 1950 Architectural Plan Revisions

Reference: Mr. James A. Dawson's letter of Nov. 2, 1950

Dear Mr. Dawson:

This Change is supplemental to our:

Change No. 22, dated Oct. 6, 1950
Change No. 22A, " Oct. 13, 1950
Change No. 22B, " Nov. 7, 1950

On November 6, 1950, we received your letter of November 2, 1950,
which reads as follows:

"Please refer to the following drawings sent to
you under Revision No. 3, dated 28 Sept. 1950:
A112, A113, RA151, RA155 and RA156

The louvers and/or grilles shown on the above
drawings were marked N.I.C. These louvers
and/or grilles are included in the Heating,
Ventilating, and Air Conditioning contract and
should be so marked on these drawings which you
have in your possession. We shall change our
originals accordingly."

We will take this information into consideration in preparing our estimate
for Change No. 22.

Under the authority and requirements of the contract, we hereby request
that proper adjustment of the contract price and contract time be dealt
with under the terms and conditions of the contract. This change will be
analyzed with all interested subcontractors and detailed estimates will
be submitted to you as quickly as possible. Definite extension of
contract time for completion will be requested as soon as determination
can be made of the effect of this change on the entire job progress.

Very truly yours,
FULLER-TURNER-WALSH-SLATTERY, INC.

MJG:CER:ar
PDV

M. J. Grogan
M. J. Grogan, Project Manager

5-44-1111111111
~~Handwritten signature~~
FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 21, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York 17, New York

Re: Contract HQ 1/82 - General Assembly & North Parking Space
Sprinkler System

Dear Sir:

You recently returned to us three copies of letters dated October 18, 1950 in which the Automatic Sprinkler Corp. of America listed the names and manufacturers, catalog numbers, etc., which they propose to use on the North Parking Space and General Assembly.

These were approved with certain exceptions, one of which was that the Check Valves $2\frac{1}{2}$ " or larger were to be Kennedy, Figure #126.

Since receipt of this exception the Automatic Sprinkler Corp. of America advised by letter dated November 16, 1950 that the Kennedy Manufacturing Company no longer manufactures check valves $2\frac{1}{2}$ " or over in size. They request approval of the Walworth Check Valve for $2\frac{1}{2}$ " or larger, the same as used on the South Parking.

Please return three copies of this letter together with your approval or comments.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

CER:WWS:amc

C. E. Reese
C. E. Reese S
Project Engineer



R
11/24


FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 21, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Tolson. Files

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Misc. Iron

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawing submitted by General Bronze Corporation and C. E. Halback & Company:

H.G.P. 5-1, revised 11/17/50 - Grating at F.A.I. &
Bank "C" Exhaust at
Tunnel
(N.P.S.)

Will you please return two (2) prints of the above drawing marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH*ead



W.K. Harrison

ISSUANCE OF DRAWINGS

OFFICE COPY

21 November 1950


29 November 1950

GA & North Parking
Fuller-Turner-Walsh-Slattery

hand

Submitted by General Bronze & Halback

2 H.G.P.-5-1 30Oct'50 Gating at F.A.I. & Bank "C" Exhaust at Tunnel
(APPROVED 27 Nov 1950 R.E.N.)



F. J. Sykes

120-5-18-9

cc: Zunser
Hopper
Hannegan
Van Name
J.J.Healy
Weigel
Bohanon

21 November, 1950

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42nd Street
New York 17, New York

Attention: Mr. C. E. Reese, Project Engineer
Re: General Assembly and North Parking Space
North Half, Contract HQ 1/82 - Plumbing
Work, Floor Drains

Gentlemen:

We request that you take the necessary steps to make the following plumbing change necessitated by architectural revisions in the General Assembly and Parking Space - North Half.

Kindly refer to the Contract Specifications Part V, Section B, Page V-B4-4, Paragraph B4-04, entitled, Floor Drains, under sub-paragraph "i" and substitute Type "BB" Drain called for under sub-paragraph "j" in lieu thereof. Also, refer to Contract Drawing No. PS/P4B, Revised 22 May, 1950, for the location of the drain shown at Columns "G" to "H", north of Column 32-A.

Please notify your Plumbing Sub-Contractor, Eugene Duklauer, Inc., accordingly and resubmit for our approval and/or comments the required shop drawings for the drain involved together with a breakdown estimate of cost which will be an addition to or deduction from the Contract Price.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction

8
JJHa:mj

NOTIFICATION OF CHANGE

Date: November 20, 1950

TO: Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York 17, New York

No. C. # 3 Building General Assembly & North Parking Space

Reference Information: GA-PS-S10, dated 9/22/50 : GA-PS-S33, dated 9/22/50
S11, " 9/29/50 : S34, " 9/29/50
S12, " " : GA-WS-1, " "

Description of Change: a) Substituted Mesh for Bars to Reinforce Stadium Slab.
Structural b) Several Minor Changes.

The above contemplated change effects the branches of the work indicated by X marks. There is shown below a quick estimate of the approximate cost of the change merely to indicate its magnitude and to assist the Owner in determining whether or not the change should be made.

() F-T-W-S Inc. Work	() Construction Insulation	() Painting & Finish
() Structural Steel	() Metal Doors, Frames & Trim	() Venetian Type Blinds
X Concrete Construction Work	() Roll-up Steel Doors	() Resilient Floor
X Concrete Slabs & Fireproofing	() Metal Toilet Enclosures	Covering
Floor & Roof Fill	() Hollow Metal Partitions	() Miscellaneous
Finish Cement Work	() Marble Work	Accessories
Masonry-Mortars	() Ceramic Tile	() Heating, Ventilating &
Waterproofing (Membrane-Spandrel)	() Terrazzo Work	Air Conditioning
Waterproofing (Mastic)	() Furring & Lathing	() Plumbing
Caulking	() Plastering	() Sprinklers
Cut Stonework	() Acoustical Treatment	() Electrical
Roofing (Built Up)	Sound Conditioning	() Sheet Metal Work
Carpentry & Millwork	() Miscellaneous Iron	() Glass & Glazing
Ornamental Metal Work	() Pictorial Hardware	

The Approximate Total Cost of this Change is \$ 500.00 - DEDUCTION
(FIVE HUNDRED DOLLARS AND NO CENTS)

and the Owner's immediate decision is required, avoiding a "Stop Order" of Field Operations and permitting the work to continue without interruption.

FULLER-TURNER-WALSH-SLATERY, INC.

M. J. Perogian
Project Manager

Date 11/20/50

The Above change will not be made and the work is to proceed in accordance with the existing Contract documents.

You are hereby notified and requested that the work in accordance with the Contract documents be continued and no further action be taken under the Contract terms.

UNITED NATIONS HEADQUARTERS

CHIEF OF WORKS SECTION

By _____ Date _____

[Signature] Date 11/30/50

COPY

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT
NEW YORK

FILE

November 20, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
U. N. Planning Office
405 E. 42nd St.
New York 17, N. Y.

Re: General Ass'y. Bldg. & North Parking Garage -
Contract HQ 1/82.

Dear Sir:

We are attaching hereto original and conformed copy of our contract with Joseph Weiss Co., Inc., dated November 15, 1950, covering Cut Stone Work and Exterior Marble, General Ass'y. Bldg. & North Parking Garage, U. N. Permanent Headquarters, New York.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

H. A. Hiener
Office Manager

HAH:vh

enc.


*Sittin' down
Hopper Pumperton
Dawson*

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

Gen Files

November 20, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York, New York



Re: Contract 1/82 - General Assembly and North Parking Space
Heating, Ventilating and Air Conditioning
Ductwork Shop Drawings

Dear Sir:

We are submitting herewith six (6) copies of the National Sheet Metal Works Inc., shop drawings showing ductwork which Kerby Saunders, Inc. proposed to furnish under the heating, ventilating and air conditioning subcontract.

Drawing No. 3-20,	Ductwork in fan rooms no. 4 and no. 8
" " 2-12,	Ductwork 2nd basement North, cols. 22 to 26 and G to O
" " 2-13,	Ductwork 2nd basement North, cols. 26 to 30 and G to O
" " 2-14,	Ductwork 2nd basement North, cols. 30 to 36 and G to O
" " 2-16,	Ductwork 2nd basement North, cols. 33 to 36A and U to V

Please review the above drawings and return three (3) copies together with your approval or comments at your earliest convenience.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER:WWS:bc



[Signature]
11/21

ISSUANCE OF DRAWINGS

OFFICE COPY

21Dec.1950

GA and N. Pk. Space

Puller-Turner-Walsh-Slaterry, Inc.

Mr. Blumquist

1007 403 E. 42nd St.

messenger

3 copies each of the following:

3-20 13Nov1950 Pan Bus. 4 and 8 Col. 35 to 36A

approved as noted 18Dec.1950 resubmit A.B.

2-12 30Sept1950 2nd Bmt. W. Col. 22 to 26

approved as noted 18Dec.1950 resubmit R. Nelson

2-13 20Oct1950 2nd Bmt. W. Col. 26 to 30

approved as noted 19Dec.1950 resubmit R. Nelson

2-14 30Oct1950 2nd Bmt. W. Col. 30 to 36

approved as noted 19Dec.1950 R. Nelson

2-16 9Oct1950 2nd Bmt. W.

approved as noted 20Dec.1950 resubmit R. Nelson

National Sheet Metal dwgs. submitted by K. Saunders

S. H. Rumpel
Hoppe Rumpel
Samuel Rumpel

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 20, 1950

RECEIVED

NOV 21 1950

United Nations Headquarters
JAMES A. DAWSON
(Co-ordinator of Construction)

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Planning Office
405 East 42nd Street
New York, New York

Re: Contract HQ 1/82 - General Assembly and North Parking Space
Heating, Ventilating and Air Conditioning
Shop Drawings

Dear Sir:

We are submitting herewith six (6) copies of each of the following shop drawings for material and equipment which Kerby Saunders, Inc. proposed to furnish under the heating, ventilating and air conditioning subcontract.

Patterson Kelly Co. Drawing No.	91172,	Snow melting converter.
" " " "	" 91169,	Panel heater converter No. 1.
" " " "	" 91170,	Panel heater converter No. 2.
" " " "	" 91171,	Panel heater converter No. 3.
Spencer Turbine Co. Form	" 1094,	Dimensions of vacuum producers.
" " " "	" 1082,	Dimensions of synthetical separators. Centrifugal
" " " "	" 1076,	Dimensions of Tubular Bag separators.

Metropolitan Refining Co. Drawing no number, Dehumidifier Water treatment equipment.

Please review the above drawings and return three (3) copies with your approval or comments, at your earliest convenience.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese
C. E. Reese
Project Engineer

CER:WWS:bc



[Signature]
11/21

ISSUANCE OF DRAWINGS

OFFICE COPY

20 November 1950

7 December 1950

GA & North Parking
Fuller-Turner-Walsh-Slaterry

hand

Submitted by Kerby Saunders

3	91172	2 Nov'50	Show Melting Converter	(Patterson Kelly Dwg.)
3	91169	"	Panel Heater Converter No. 1	" " "
3	91170	"	" " " " 2	" " "
3	91171	"	" " " " 3	" " "
3	None	9 Nov'50	Dehumidifier Water Treatment Equipment (Metropolitan Refining Co. Dwg.)	

(ABOVE DWGS. "APPROVED AS NOTED" 4 Dec 1950)

(P.B. RESUBMIT)

3	1094	None	Dimensions of Vacuum Producters (Spencer Turbine Dwg.)	
3	1082	"	" " Centrifugal Separators	" " "
3	1076	"	" " Tubular Bag	" " "

(ABOVE DWGS. "RESUBMIT") (P.B. 4 Dec 1950)

NOTE: FROM SYSKA & HENNESSY

"Dwgs. 1094, 1082 and 1076 are returned without action. The Contractor is to submit data on vacuum producer, stating rating and current characteristics of motor, capacity of producer and all other information as required, in Specifications, Div. 10, Art. A10-01 to A10-10 inclusive. The Contractor in addition is to submit shop drawings showing installation of collector piping in Recording Room, Dwg. GA-H-1."

RECEIVED

DEC 12 1950

FULLER-TURNER-WALSH-SLATERRY
INCORPORATED

Ly Tyler

20 November 1950

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Northerly
Portion of the Parking Garage
Contract HQ 1/82 - Exterior Stone



Gentlemen:

Please be advised that all of the vertical expansion joints in the exterior walls on the east and west elevation must be 3/8" wide instead of 1/4" wide as previously shown on the detailed drawing RA101.

Stone shop drawings have been corrected indicating these 3/8" joints and our drawing RA101 will be corrected to agree.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction



JHe:eam
cc: Bohanon
Nelson
Weigel
Healy
Harris
Hopper
Zunser
VanName

20 November 1950

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Northerly
Portion of the Parking Garage
Contract HQ 1/82 - Structural
Steel and Concrete


Gentlemen:

As of even date we are forwarding you twenty-five (25)
copies of each of the following drawings:

GA-WS-133A, 25 Oct. 1950 - Sloping Walls
GA-WS-149, 13 Nov. 1950 - Critical Points in South
End Ceiling
GA-5-CS-3, 20 Nov. 1950 - Addds. to Roof Framing
on WS-58
GA-1CS-BL, 9 Nov. 1950 - Change Bulletin, Sheet #1
GA-1-CS-BL, 9 Nov. 1950 - Change Bulletin, Sheet #2

All of these drawings are amplification drawings
causing no change to the Contract Price. Proceed with the work
shown thereon if you agree with this statement. If not, promptly
notify us of your investigation.

Very truly yours,



cc: Bohanon
Nelson
Weigel
Healy
Harris
Hopper
Zunser
VanName
Hannegan
Ryer

James A. Dawson
Co-Ordinator of Construction

20 November 1950

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Northerly
Portion of the Parking Garage
Contract HQ 1/82
Carpentry and Millwork

Gentlemen:

Please refer to your letter of 11 October 1950 wherein you request our approval of the sample battens installed by the Murray Hill Woodworking Corporation in the 3rd Floor mock-up, as per our detail on Drawing DSK-313.

We hereby approve these sample battens.

Very truly yours,



JJH:eam
cc:Bohanon
Nelson
Weigel
Healy
Harris
Hopper
Zunser
VanName

James A. Dawson
Co-Ordinator of Construction

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 17, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Dear Mr. Dawson:

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage
Structural Steel
Cut Stone

In order for Monahan-McCann Stone Company to complete their stone details for the General Assembly, it is necessary for them to have the erection drawings of American Bridge Company since these drawings may vary from Madigan-Hyland structural plans.

It is especially important for them to have American Bridge's erection drawings showing any details of the spandrel beams ^{at} lintels. They also require the framing plans as soon as they are approved and can be released.

Will you please let us have any of the above information available as soon as possible so that we can transmit it to Monahan-McCann to complete their stone details on the General Assembly.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

PDV*ead

*P*
11/20

120 - 5 - 18 - 9
17 November 1950

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Northerly
Portion of the Parking Garage
Contract HQ 1/82 - Electric and
Heating, Ventilating and Air Conditioning

Gentlemen:

On 17 November 1950 we forwarded you twenty-five (25) copies of Drawing No. SK-GA-E-3L-2, dated 10 November 1950, and Drawing No. SK-GA-H-8-3, revised 16 November 1950.

Drawing No. SK-GA-H-8-3 was previously issued as per our letter to you dated 6 November 1950. The information as to how you should proceed is contained in that letter.

Drawing No. SK-GA-E-3L-2 has been issued at the request of the Contractor according to a transmittal we have received from the office of Syska & Hennessy, and is for information only. You will note the work indicated thereon is a suggested method of installing the boxes and conduits for the lights in the column on the main floor.

Very truly yours,


J. He:eam

cc: Bohanon
Nelson
Weigel
Healy
Harris
Hopper
Zunser
VanName
Hannegan

James A. Dawson
Co-Ordinator of Construction

Seelman Rumpeltin S & H (2) Poggi Ryer

120-5-18-9
17 November 1950

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Northerly Portion
of the Parking Garage - Contract HQ 1/82
Hollow Metal Doors, Frames & Trim
Finish Hardware

Gentlemen:

Please refer to your letter of 19 September 1950 wherein you request the proper type of hardware for the following doors:

Opening Type F4 to the Guard Room at Ramp #12
Opening Type S1 to the Guard Room at Ramp #12
Opening Type S10 to the Duct Space at Column V34.

The type of hardware for these doors has been listed in the Hardware Schedule, dated 23 October 1950, copies of which have been checked and returned to your office. On this Hardware Schedule all of the information with reference to the above three mentioned doors has been included, and for the Opening Type F4 door refer to Opening No. 3B33; for the Opening Type S1 refer to Opening No. 3B34; and for the Opening Type S10 refer to Opening 3B32.

In answer to the last paragraph of this 19 September 1950 letter, please be advised that the two (2) openings shown on drawing All8 to Stair No. 6 is the correct condition. Drawing A2B, the Floor Plan, will be revised and issued to you at a future date.

Very truly yours,


JJH:eam

cc: Bohanon
Nelson -2
Weigel
Healy
Harris
Hopper Zunser VanName

James A. Dawson
Co-Ordinator of Construction

120-5-18-9

OREGON 9-3950

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 16, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
U. N. Planning Office
405 E. 42nd St.
New York 17, N. Y.

Re: General Ass'y. Bldg. & North Parking Garage Bldg. -
Contract HQ 1/82.

Dear Sir:

We are attaching hereto signed copy, together with two (2) conformed copies of contracts with Fischbach & Moore, Inc., dated Nov. 13th, covering Electrical Work, and Monahan-Mc Cann Stone Co., dated Nov. 8th, covering Cut Stone Work, etc., on the General Ass'y. Bldg. & North Parking Garage Bldg., U. N. Permanent Headquarters, New York.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

H. A. Hiener

H. A. Hiener
Office Manager

HAH:vh

enc.



J
11/16


Mr. A. Dawson
Hoffman
Reinforcing
12 Nov. 1950
FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

November 16, 1950



Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Gentlemen:

Re: Contract HQ 1/82 - General Assembly
and North Parking Garage - Reinforcing
Steel Details

We are sending you herewith for approval six (6) copies each of the following reinforcing steel details prepared by Brennan & Sloan, Inc. and Knickerbocker Construction Corporation:

4201, corrected 11/14/50 - Bottom Slab Bar Layout
Div. #4, 1st Basement

4202, " " - Top Slab Bar Layout
Div. #4, 1st Basement

Will you please return three (3) copies each of the above drawings marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

BK*ead

*Handwritten signature/initials*

ISSUANCE OF DRAWINGS

OFFICE COPY

16 November 1950

29 November 1950

GA & North Parking

Fuller-Turner-Walsh-Slattery

hand

Submitted by Brennan & Sloan & Knickerbocker

3 4201 16Oct'50 Bottom Slab Bar Layout Div. #4, 1st Bsm.

3 4202 " Same as above except Top Slab etc.

(APPROVED 27 Nov 1950 R.E.N.)



J. V. Syler

16 November 1950

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42 Street
New York 17, New York


Re: General Assembly and Northerly
Portion of the Parking Garage
Contract HQ 1/82 - Change No. 1
Miscellaneous Metal

Gentlemen:


Refer to your letter of 13 September 1950 wherein you request instructions as to how to proceed in the matter of providing 3" x 3" x 1/4" angle brackets attached to the structural built-up channels on the 32A column line of the North Wall.

We have issued prints of drawing No. GA-1-CS-40, dated 31 October 1950 to both the American Bridge Company and your office. This drawing shows the angles in question, which will be furnished by the American Bridge Company. Refer to our letter of 9 November 1950 to you wherein we state we forwarded you twenty-five (25) copies of this drawing.

Very truly yours,



James A. Dawson
Co-Ordinator of Construction



JJHe:eam
cc: Bohanon
Nelson
Weigel
Healy
Harris
Hopper
Zunser
VanName

120-5-18-9
16 November 1950

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Wortherly
Portion of the Parking Garage
Contract Hq 1/82 - Concrete


Gentlemen:

As of even date we are forwarding you twenty-five (25) copies of our Drawing GA-PS-CS-10, dated 15 November 1950. This drawing indicates the reinforcing details for the Splice Room. If you refer to the contract drawings GA-PS-S-6, 7 and 15, you will note that the reinforcing shown on this drawing GA-PS-CS-10 is the same as indicated on these drawings, therefore, there should be no change in Contract Price.

Specifically, you will notice that on drawing GA-PS-S-15 there is a note at the portion detailed that the Splice Room wall reinforcing was to be the same as the transformer vault walls. The reinforcing for these transformer vault walls is shown on contract drawing GA-PS-S-15.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction



JJHe:eam
cc: Bohanon
Nelson -2
Weigel
Healy
Harris
Hopper
Zunser
VanName
Hannegan
Ryer

16 November 1950

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Northerly
Portion of the Parking Garage
Contract HQ 1/82 - Concrete


Gentlemen:

On 16 November 1950 we forwarded to you under separate cover twenty-five (25) copies of Drawing GA-PS-CS-11, dated 16 November 1950.


We can see no reason for a price change to the contract and, based on this assumption, we authorize you to proceed with the installation of the work shown on the drawings. Notify us if you are not in accord.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction



JJHe:eam
cc: Bohanon
Nelson -2
Weigel
Healy
Harris
Hopper
Zunser
Hannegan
VanName
Ryer



~~Stop~~
Deadly high
17 hrs

NEW YORK 17, N. Y.

17 hrs

United Nations Headquarters
JAMES A. DAWSON
(Co-ordinator of Construction)

W. H. Fick

Re: Contract HQ 1/82 - General Assembly
& North Parking Garage - Misc. Iron

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawing submitted by General Bronze Corporation and C. E. Halback & Company:

H.G.P. 3-1, revised 11/14/50 - Steel Elevator
Pit Ladders
(N.P.S.)

Will you please return two (2) prints of the above drawing marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese
Project Engineer

MH*eab

[Handwritten signature]

ISSUANCE OF DRAWINGS

OFFICE COPY

15 November 1950

22 November 1950


GA & North Parking

Fuller-Turner-Walsh-Slattery

hand

Submitted by General Bronze & Halback

2 H-GP-3-1 19Oct'50 Steel Elevator Pit Ladders (M.P.S.)
(APPROVED 22 Nov 1950 R.E.H.)



15 November 1950

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Northerly Portion
of the Parking Garage - HQ 1/82
North Parking Duct Openings in Masonry


Gentlemen:

The location of masonry openings for ducts piercing the walls of east and west duct spaces will be changed in some cases due to the relocation of the ducts as shown on Kerby Saunders' approved duct layout drawings for the above subject portion of the project.

When architectural and/or mechanical drawings disagree with Kerby Saunders' shop drawings as to the location of these above mentioned openings, use Kerby Saunders' drawings for the proper location of the holes.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction



JHe:eam
cc: Bohanon
Nelson -2
Weigel
Healy
Harris
Hopper
Zunser
VanName
Hannegan
Rumpelstin
S & H (2)

120-5-18-9
15 November 1950

Fuller-Turner-Walsh-Slattery, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Northerly
Portion of the Parking Garage
Contract HQ 1/82 - Concrete

Gentlemen:

On 15 November 1950 we forwarded you twenty-five (25) copies
of the following drawings:

GA-WS-124, Revised 10 November 1950
GA-1-CS-35, Revision No. 1, dated 15 November 1950

Drawing No. GA-WS-124 has been revised to show corrections
which do not affect the Contract Price. Drawing No. GA-1-CS-
35 has been revised to show a change to Lintel I3 which
should cause no change to the Contract Price.

Proceed with the work shown on these drawings.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction

JJHe:eam
cc: Bohanon
Nelson
Weigel
Healy
Harris
Hopper
Zunser
VanName
Hannegan
Ryer

cc: Bohanon Hopper
Nelson Zunser
Weigel VanName
Healy Hannegan
Harris Ryer

15 November 1950

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Northerly Portion
of the Parking Garage - HQ 1/82
Concrete and Structural Steel

Gentlemen:


On 14 November 1950 we forwarded you twenty-five (25) copies
of the following drawings:

- GA-WS-159, dated 22 September 1950
- GA-WS-168, dated 16 October 1950
- GA-WS-169, dated 23 October 1950.

The above three drawings are amplification drawings including
necessary information for locating structural steel. There
should be no change to the Contract Price due to the work shown
thereon, but, if you disagree with this statement, please
promptly notify us of your findings. On the same date we for-
warded you twenty-five (25) copies of drawing GA-S-29, dated
20 October 1950. This drawing is a collection of work sheets
and voids previous work sheets, the numbers of which have been
indicated on this drawing. Since the revisions shown on this
drawing are either reference changes or dimensional changes,
there should be no Contract Price change.

On 15 November 1950, we forwarded you twenty-five (25) copies
of drawings GA-WS-174C and GA-WS-175C, both dated 13 October
1950. Before proceeding with any work indicated on these draw-
ings, notify us of any cost changes to the Contract Price; if
there are no changes in cost, proceed with the installation
of the work.

Very truly yours,


JJHe:eam

James A. Dawson
Co-Ordinator of Construction

15 November 1950

Fuller-Turner-Walsh-Slattey, Inc.
403 East 42 Street
New York 17, New York

Re: General Assembly and Northerly Portion
of the Parking Garage - HQ 1/82
North Parking Rolling Shutters
J. G. Wilson Drawing No. 89-840-6


Gentlemen:

Please refer to the above subject drawing which we
returned to you on the 13th of November 1950.

You will note that we have omitted the Class "A"
labels required by the rolling shutter shown on this drawing.
Please submit for our consideration the credit for the omission
of this label. Also, inform the sub-contractor not to begin
with the fabrication of this item until we shall have received
the amount of the credit.

Very truly yours,

James A. Dawson
Co-Ordinator of Construction


cc: Bohanon
Nelson -2
Weigel
Healy
Harris
Hopper
Zunser
VanName
Ryer

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 14, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Re: Contract HQ 1/82 - General Assembly & North Parking Garage
CHANGE NO. 51 - Additional Expansion Joint at Column Line
U' 29.

References: (a) General Bronze Corporation and C. E. Halback & Co.
Shop Drawing No. HGP-35-1, "Approved as Noted" by
the United Nations, dated October 30, 1950.

(b) Mr. James A. Dawson's letter of November 3, 1950.

Dear Mr. Dawson:

On October 31, 1950 you returned prints of Reference (a) to us with your corrections showing an additional Expansion Joint running east of column line U'29 including cover plate, channels, angles and the necessary fastening members for the Joints. This Joint was not detailed on your Architectural or Structural details.

On November 9, 1950 we received your letter of November 3, 1950, Reference (b), which reads as follows:

"On 31 October 1950 we returned Drawing H.G.P.-35-1, prepared by C. E. Halback & Company, marked "Approved as Noted" and "Resubmit", dated 30 October 1950.

Note that east of U' on Column line #29 cover plates, channels, angles, and the necessary fastening members must be provided for the expansion joints.

Before your sub-contractor proceeds with the installation of this work, please submit prices for our consideration if the Contract Price is affected."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible.

Continued.....

Mr. James A. Dawson

-Page 2-

November 14, 1950

Re: Contract HQ 1/82 - General Assembly
CHANGE NO. 51

Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Yours very truly,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan
Project Manager

MJG:PDV*eab

FULLER-TURNER-WALSH-SLATTERY, INC.
UNITED NATIONS CONTRACT
403 EAST 42ND STREET
NEW YORK 17, N. Y.

November 14, 1950

Mr. James A. Dawson
Co-Ordinator of Construction
United Nations Headquarters
405 East 42nd Street
New York 17, N. Y.

Re: Contract HQ 1/82 - General Assembly & North Parking Space
CHANGE NO. 50 - Meeting Halls Details Adjacent to General
Assembly Balcony at Elevation 53'-0".

Reference: (a) UN Drawing MH-SK-342, dated 10/16/50 - "Window
Details at Balcony of General Assembly at Eleva-
tion 53'-0" at North Side of Neck".

Dear Mr. Dawson:


On October 18, 1950 we received the above Meeting Halls drawing which clarifies the arrangement of the junction of the Meeting Halls neck and the east wall of the General Assembly. We have assigned this change number to cover any change in cost involved in the General Assembly contract caused by these revised Meeting Halls details.

We have asked the subcontractors involved to notify us of any change in their costs.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.


M. J. Grogan
Project Manager

MJG:PDV*ead
