

CENTRAL REGISTRY (120-5-18-9) SG Building Construction-Working Project-General Assembly & North Parking-182-01 July 1951  
Fuller-Turner-Wash-Slatery, Inc. 17 July 1951

CLEAR

S.E. 7/04

S-0472

Box-27

File-1

(BAG-1)

*Mr. Sealy (Hawesaw)*  
*copy to H. P. (Hawesaw)*  
*my file under C.O. #232*  
FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 9, 1951

Mr. James A. Dawson  
Headquarters Planning Office  
Room 2272  
United Nations,  
New York

Re: Contract HQ 1/82 - General Assembly  
and North Parking Space

Dear Sir:

We refer to your proceed letter dated 5 July 1951, regarding the relocation of continuous drain and leaders at level + 41'-0" on column lines 32A and north of column line 36. (Drawing SK-PS-P-4B-1 dated 28 June 1951)

We do not agree with the second paragraph of your letter which reads we quote;

"Since the revision involves only changes in dimensions there should be no change in cost. Proceed with the work shown on the above drawing."

Relocating the drains as per the above drawing will require the cutting of some sixteen holes for the leaders, the plugging and patching of an equal amount of holes, since the concrete slab at these elevations has been poured for some time.

We have therefore assigned General Assembly and North Parking Change number 232 to cover the costs, and will present our estimate to you for your approval just as soon as we have received them from the subcontractors involved.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*  
C. E. Reese  
Project Engineer



## FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 9, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272  
United Nations, New York

Re: HQ 1/82 Contract - General Assembly & North Parking Space  
Change No. 115-B  
Distribution of Asphalt Tile Colors  
in General Assembly

Dear Mr. Dawson:

In your letter to us of 11 May 1951, Page No. 5 of the General Assembly Asphalt Tile List dated 1 March 1951 was deleted, which removed the asphalt tile requirements from various stair levels.

In order to avoid confusion, may we request that the architectural drawings be revised accordingly, especially in regard to the space finish symbols.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*

C. E. Reese  
Project Engineer

CER/MH/lbr

*ask*

## FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 9, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General  
Assembly and North Parking  
Garage -  
Change No. 156 - Roofing

Dear Mr. Dawson:

As requested in your letter of April 24, 1951, we are sending you herewith three (3) samples of Celotex Regular Roof Insulation in 2" thickness, submitted by New York Roofing Co. for use on the Podium at Elevation 41'-0".


Will you please return two (2) of the enclosed samples, marked with your approval and/or comments.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese  
C. E. Reese  
Project Engineer

CER/PDV/eas





## FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 9, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General  
Assembly and North Parking  
Garage - (GENERAL ASSEMBLY)  
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawings, submitted by General Bronze Corp. & C.E. Halback & Co.:

HGP-45-1 7/5/51 Bucks for Stair Doors next to  
Elevators #1, 2 3, & 4

Will you please return two (2) prints each of the above drawings, marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*

C. E. Reese  
Project Engineer

CER/MH/em



ISSUANCE OF DRAWINGS

OFFICE COPY

General Counsel  
L.F. N.S.

June 15, 1951

Messinger

C.E. Holloman

2 H6P-45-1 Bump for strain across neck to  
Cerv. vert. 1, 2, 3, & 4

(Approved by West, President, G.C.A.)

**RECEIVED**  
JUL 16 1951  
FULLER-TURNER-WALSH-SLATTERY  
INCORPORATED

BSM



FULLER-TURNER-WALSH-SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

July 9, 1951

*Files*  
*Henry*  
*7/10*  
*1951*

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272  
United Nations, New York

Re: HQ 1/82 Contract - General Assembly & North Parking  
Space (General Assembly)  
Sheet Metal Work - A.Munder & Son, Inc.

Dear Mr. Dawson:

We are sending you herewith for your information  
one print of the following sheet metal work shop drawing, as  
approved for field distribution:

<u>NO.</u>	<u>DATE</u>	<u>TITLE</u>
3	Rev. 6/15/51	Flashing Details at Elev. 41'-0"

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*  
C. E. Reese  
Project Engineer

CER/MH/lbr  
Encl. - dwg.



-9-

**COPY**

**FULLER-TURNER-WALSH-SLATTERY, INC.**

UNITED NATIONS CONTRACT  
NEW YORK

July 9, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272  
United Nations, New York

Re: HQ 1/82 Contract - General Assembly & North Parking  
Space (General Assembly)  
Sheet Metal Work - A. Munder & Son, Inc.

Dear Mr. Dawson:

We are sending you herewith for your information  
one print of the following sheet metal work shop drawing, as  
approved for field distribution:

<u>NO.</u>	<u>DATE</u>	<u>TITLE</u>
3	Rev. 6/15/51	Flashing Details at Elev. 41'-0"

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*

C. E. Reese  
Project Engineer

CER/MH/lbr  
Encl. - dwg.





-9✓

**COPY**

**FULLER-TURNER-WALSH-SLATTERY, INC.**

UNITED NATIONS CONTRACT  
NEW YORK

July 9, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272  
United Nations, New York

Re: HQ 1/82 Contract - General Assembly & North Parking  
Space (General Assembly)  
Sheet Metal Work - A. Munder & Son, Inc.

Dear Mr. Dawson:

We are sending you herewith for your information  
one print of the following sheet metal work shop drawing, as  
approved for field distribution:

<u>NO.</u>	<u>DATE</u>	<u>TITLE</u>
3	Rev. 6/15/51	Flashing Details at Elev. 41'-0"


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*

C. E. Reese  
Project Engineer

CER/MM/lbr  
Encl. - dwg.



-9✓

**COPY**

**FULLER-TURNER-WALSH-SLATTERY, INC.**

UNITED NATIONS CONTRACT  
NEW YORK

July 9, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272  
United Nations, New York

Re: HQ 1/82 Contract - General Assembly & North Parking  
Space (General Assembly)  
Sheet Metal Work - A. Munder & Son, Inc.

Dear Mr. Dawson:

We are sending you herewith for your information  
one print of the following sheet metal work shop drawing, as  
approved for field distribution:

<u>NO.</u>	<u>DATE</u>	<u>TITLE</u>
3	Rev. 6/15/51	Flashing Details at Elev. 41'-0"


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*

C. E. Reese  
Project Engineer

CER/MH/lbr  
Encl. - dwg.





## FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 6, 1951

*[Handwritten signature]*

Mr. James A. Dawson  
Co Ordinator of Construction  
Headquarters Planning Office  
Room 2272, United Nations  
New York 17, N. Y.

*[Handwritten "file"]*

Re: General Ass'y. &amp; North Parking - Cont. HQ 1/82

Dear Sir:

We are attaching hereto three (3) signed copies of these  
Change Orders:-

#2 - Addition - Monahan-McCann Stone Co. - \$ 60.00

#1 - Addition - Del Turco Bros., Inc. - 168.11

These Change Orders are on General Ass'y. & North Parking  
contract.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*[Handwritten signature: H. A. Hiener]*  
H. A. Hiener  
Office Manager

HAH:vg

enc.



FULLER - TURNER - WALSH - SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

*file*

July 6, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General Assembly and North Parking Garage -  
CHANGE NO. 218 - Revised Details of Access Doors to Rolling  
Shutter Motors

References: (a) U.N.Dwg. SK-661, dated June 19, 1951  
(b) Mr. James A. Dawson's letter 26 June 1951 to FTWS, Inc.

Dear Mr. Dawson:

On June 20, 1951 we received prints of Reference (a) and on  
June 26, 1951 we received your transmittal letter, Reference  
(b), which reads in part as follows:

"Proceed with the work shown thereon. This drawing  
simplifies details on RA-142 issued to you on 28  
September 1950. No contract price change should  
result."

The addition of the stainless steel angles and plates, however,  
probably will affect the subcontract price. Consequently, we  
have sent the above referenced drawing to the interested sub-  
contractors with the request that they advise us if this revision  
affects their subcontract price.

Under the authority and requirements of the contract, we hereby  
request that proper adjustment of the contract price and contract  
time be dealt with under the terms and conditions of the contract.  
This change will be analyzed with all interested subcontractors  
and detailed estimates will be submitted to you as quickly as  
possible. Definite extension of contract time for completion will  
be requested as soon as determination can be made of the effect of  
this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*M. J. Grogan*  
M. J. Grogan  
Project Manager

MJG/PDV/eas



FULLER - TURNER - WALSH - SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

*file*

July 6, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N. Y.

Re: Contract HQ 1/82 - General Assembly and North Parking Garage  
CHANGE NO. 69E - Standard Lighting Fixture Revisions -  
Furnishing and Installing

---

Dear Mr. Dawson:

This Change #69E is supplemental to the following changes and super-sedes them insofar as the final quantities of standard lighting fixtures are concerned.

Change #69, dated December 27th 1950  
Change #69A, dated January 24th 1951  
Change #69B, dated February 23rd 1951  
Change #69C, dated May 11th 1951  
Change #69D, dated July 5th 1951

This change #69E does not include the following:

1. Any increase or decrease in the cost of setting plaster rings.
2. Any increase or decrease in the cost of ductwork or air diffusers or the connecting up of air diffusers which may be caused due to changes in lighting fixtures.
3. Any increase or decrease in cost of wire or conduit due to added or deleted standard lighting fixtures.
4. The cost of furnishing and installing Special Lighting Fixtures.

Items 1, 2 and 3 will be covered by another Change when light location drawings are received.

Item 4 will be covered by our Estimate for Change 70.

Due to present day difficulties in obtaining materials, it became necessary to arrive at an early decision on a final quantity figure, and these final quantities as shown on the following revised lighting fixture list dated June 28th 1951, were determined at a meeting held on or about June 22nd 1951 at which Messrs. M. Harris of the United Nations Headquarters Planning Office, R. Hellegers of Syska and Hennessy and H. C. MacNary of Fischbach & Moore, Inc. were present.

Continued.....



I Revised Standard Lighting Fixture List dated 6/28/51.

118	Type "A"	Globe
1	" "B"	"
18	" "D"	"
14	" "E"	Kliegl #711A
18	" Ea	Recessed McPhilben #545H
4	" Ea	Surface
8	" Eb	Wall
1	" Eb	Ceiling
396	" G	Bright Light
55	" H	GE Lampholder
25	" K	R & S 4942
12	" L	" 6255
99	" P	P & S 5046
7	" T	Miller
8	" gg	Appleton 1517
135	" hh	Century 50029
303	" kk	Caldwell 11727 (34)
35	" ll	Holophane 1748
15	" nn	Century 2210
15	" pp	Century 50029 (Surface)
7	" qq	Art Metal
20	" ss	R & S 5045
3	" uu	Globe 502-40-03 Glass
1	" t	Lightolier D 23705
4	" AA	Gotham #2155-19"
2	" BB	Bryant 3851
4	" CC	Gotham #2155-48"
10	" VV	Gotham #FH 1696
6	" Ed	Suspended
4	" Ec	Bracket
8	" DD	and F Comb. A-F-A-F-A
10	" DD, FF	and F Comb. FF-F-A-F-FF
171	" XX	Kleigl 2677
60	" YY	Caldwell 11999
46	" TT	Caldwell K 11926
396	Stems - Aligners	

## LAMPS

4	15 Watt Fluorescent
40	20 " "
492	40 " "
2	6 " A
233	25 " A
37	60 " A
164	75 " A

Continued.....

## LAMPS

65	100 Watt	A
389	150 "	A
396	200 "	A
7	500 "	PS
150	100 "	Flood
46	S-6	Candelabra Base
60	WTB	" "

II The Contract Lighting Fixture Requirements were as follows:

54	Type A
29	" B
3	" C
40	" Ea Kliegl #690
14	" Eb " 6900
164	" F Holophane I 1774
370	" G Bright Light 200
21	" G " " 150
71	" H GE Lampholder
10	" K R & S 4942
9	" L R & S 6255
57	" P P & S 5046
40	" W Hol. F 796
38	" X 200 W. Glassteel
7	" Y 500 W. Glassteel
2	" CC Daybright 214-8B
9	" DD Hol. #9201-S
6	" GG Appleton 1517
135	" HH Century 50029
8	" DD & F Comb.
10	" EE-F-JJ Comb.
370	Stems - Aligners, etc.

## LAMPS

61	20 Watt Fluorescent
324	40 " "
108	25 " Type A
71	75 " " "
259	100 " " "
223	150 " " "
408	200 " " "
7	500 " " "

Continued.....

Mr. James A. Dawson

-4-

HQ 1/82 - CHANGE NO. 69E

The cost of this change will be based upon the difference in quantities for the furnishing and installation of standard lighting fixtures as shown on the revised list and the contract requirements as shown above. Any further revisions in standard lighting fixtures after this date will be covered under separate changes.

Any surplus fixtures will be turned over to the United Nations and credit given for the cost of installation only.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

  
M. J. Grogan  
Project Manager

MJG:WWS:tw



*Wagner*

FULLER-TURNER-WALSH-SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

July 6, 1951

Mr. James A. Dawson  
CoOrdinator of Construction  
United Nations Headquarters  
405 East 42d Street  
New York 17, New York

*WEIGLE*  
*Tyler*  
*to hqn file*

Re: Contract HQ 1/82 GA & NHPS  
General Assembly  
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawings submitted by General Bronze Corp. and C. E. Halback & Company:

<u>No.</u>	<u>Date</u>	<u>Title</u>
HGP 19-2	7/5/51	Hung Lintel At Coat Room #104

Will you please return two prints each of the above drawings marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*

C. E. Reese  
Project Engineer

CER/MH/em

cc; Grogan  
Reese  
McKee  
Del Vecchio  
Pierson  
File



ISSUANCE OF DRAWINGS

OFFICE COPY

6 July 1951

18 July 1951

GA & North Parking

Fuller-Turner-Walsh-Slattey

hand

Submitted by General Bronze & Halback

2 HGP-19-2 5 July '51 Hung Lintel at Coat Room #104

(DISAPPROVED 17 July '51 RESUBMIT FB/GRA:S.L.B.D.P.)



*L.V. Tyler*

FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

*Mrs. Tyler*

July 6, 1951

*New Files  
7/9  
WJ*

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General  
Assembly and North Parking  
Garage -  
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1) print  
of the following Miscellaneous Iron shop drawing, as approved  
for field distribution:

HGP-49-5 6/14/51 Steel Glass Screen Opening 155  
G.M.

(General Bronze Corp. & C.E. Halback & Co.-Subcontractors)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*

C. E. Reese  
Project Engineer

CER/MH/eas





-9✓

**COPY**

**FULLER-TURNER-WALSH-SLATTERY, INC.**

UNITED NATIONS CONTRACT  
NEW YORK

July 6, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General  
Assembly and North Parking  
Garage -  
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1) print  
of the following Miscellaneous Iron shop drawing, as approved  
for field distribution:

HGP-49-5    6/14/51    Steel Glass Screen Opening 155  
G.M.

(General Bronze Corp. & C.E. Halback & Co.-Subcontractors)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*

C. E. Reese  
Project Engineer

CER/MH/eas

- 9

**COPY**

**FULLER-TURNER-WALSH-SLATTERY, INC.**

UNITED NATIONS CONTRACT

NEW YORK

July 6, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General  
Assembly and North Parking  
Garage -  
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1) print  
of the following Miscellaneous Iron shop drawing, as approved  
for field distribution:

HGP-49-5    6/14/51    Steel Glass Screen Opening 155  
G.M.

(General Bronze Corp. & C.E. Halback & Co.-Subcontractors)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*

C. E. Reese  
Project Engineer

CER/MH/eas

-9-

**COPY**

**FULLER-TURNER-WALSH-SLATTERY, INC.**

UNITED NATIONS CONTRACT

NEW YORK

July 6, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General  
Assembly and North Parking  
Garage -  
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith, for your information, one (1) print  
of the following Miscellaneous Iron shop drawing, as approved  
for field distribution:

HGP-49-5    6/14/51    Steel Glass Screen Opening 155  
G.M.

(General Bronze Corp. & C.E. Halback & Co.-Subcontractors)

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*

C. E. Reese  
Project Engineer

CER/MH/eas



120-5-18-9

cc: Harrison  
McLeod  
Zunser  
Van Name  
Hopper  
Healy

6 July 1951

Fuller-Turner-Walsh-Slattery, Inc.  
403 East 42nd Street  
New York 17, N.Y.

Re: Contract HQ 1/82 - General Assembly  
and North Parking Garage - Notification  
of Change No. 55 (R.P. #42)  
Special Exit Lights Type Ec & Ed

Gentlemen:

Attached hereto is one copy of Notification of Change No. 55,  
(R.P. #42) approved by James A. Dawson for the United Nations.

This approval is given for you to proceed with the work re-  
quired by the modification with reference to Special Exit Lights Type  
Ec and Ed.

It is understood that this approval does not include the cost  
of this change as indicated in the Notification of Change No. 55, which  
is solely an approximation. It is understood, also, that the actual price  
adjustment will be made as required by the terms of the contract.

Very truly yours,

James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office

 JZ:eh

120-5-18-9-  
cc: Harrison  
McLeod  
Zunser  
Van Name  
Hopper  
Healy

6 July 1951

Fuller-Turner-Walsh-Slattey, Inc.  
403 East 42nd Street  
New York 17, N.Y.

Re: Contract HQ 1/82 - General Assembly  
and North Parking Garage - Notification  
of Change No. 54 (R. P. #33)  
Architectural Revisions No. 23, dated  
4 April 1951

Gentlemen:

Attached hereto is one copy of Notification of Change No. 54,  
(R. P. # 33) approved by James A. Dawson for the United Nations.

This approval is given for you to proceed with the work re-  
quired by the modification with reference to the Architectural Revisions  
No. 23, dated 4 April 1951.

It is understood that this approval does not include the cost  
of this change as indicated in the Notification of Change No. 54, which  
is solely an approximation. It is understood, also, that the actual price  
adjustment will be made as required by the terms of the contract.

Very truly yours,

James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office

 JZ:eh



6 July 1951

Fuller-Turner-Walsh-Slattery, Inc.  
403 East 42 Street  
New York 17, New York

Re: General Assembly and Northerly  
Portion of the Parking Garage  
Contract HQ 1/82  
Painting and Finishing

Gentlemen:

Reference is made to your letters of the 2nd and 27th of April 1951 concerning Painting and Finishing materials proposed for use under Contract HQ 1/82 and also our color requirements for certain portions of the work under the same Contract.

Our letter of 29 June 1951 approving your latest list of materials you plan to provide satisfies your request for material acceptances. Our letter of yesterday's date transmitting the Paint Finish Schedule for Studio Areas and various color chips fulfills the balance of your current request.

As construction progresses, we will provide further finish schedules and color chips of additional colors which will be required.

Very truly yours,

James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office

HBW:eam  
cc: Bohanon  
Nelson  
Weigel  
Healy  
Harris  
Hopper  
Zunser  
VanName



6 July 1951

Fuller-Turner-Walsh-Slattey, Inc.  
403 East 42 Street  
New York 17, New York

Re: General Assembly and Northerly  
Portion of the Parking Garage  
Contract HQ 1/82  
Plumbing


Gentlemen:

On 6 July 1951 we forwarded you under separate cover twenty-one (21) copies of Drawing No. SK-GA-P5-1, dated 3 July 1951, the part plan of the third floor indicating the elimination of one 3" floor drain and the steam supply and return at the liquor bar.

Proceed with the work indicated thereon and submit for our consideration the credit due to the omission of the one drain.

Very truly yours,

James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office



JJHe:eam  
cc: Bohanon  
Nelson  
Weigel  
Healy  
Harris  
Hopper  
Zunser  
VanName  
Ryer  
Hannegan  
S & H - 2

## FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 5, 1951

*must  
my  
2/11/51*

*(S)*

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272, United Nations  
New York 17, N. Y.

Re: Meeting Halls, Contract HQ 1/75 and General Ass'y. &  
North Parking, Contract HQ 1/82

Dear Sir:

We are attaching hereto three (3) copies of each of the following  
signed Change Orders:-

#5	- Addition	- John B. Kelly, Inc.	- \$ 359.06
#3	- "	- Shatz Painting Co.	- 116.15
#5	- "	- Atlantic Metal Prod.	- 1,800.04
#1	- Deduction	- New York Roofing Co.	26.10
#1	- "	- J. G. Wilson Corp.	180.00
#1	- Addition	- James Cullo & Son Marble Co., Inc.	209.99

All on General Ass'y. & North Parking contract.

#7 - Addition - New York Roofing Co. - \$3,909.03  
#12 - Addition - General Bronze Corp. - 102.24

Meeting Halls contract.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*H. A. Hiener*  
H. A. Hiener  
Office Manager

HAH:vh  
enc.





**FULLER - TURNER - WALSH - SLATTERY, INC.**  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

*file*

July 5, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General Assembly and North Parking  
Garage -  
CHANGE NO. 225 - Flashing Details at Meeting Halls Neck

References: (a) U.N. Dwg. RA-106-A dated June 26, 1951  
(b) Mr. James A. Dawson's letter 28 June 1951 to FTWS.

Dear Mr. Dawson:

On June 28, 1951 we received prints of Reference (a) and on  
June 29, 1951 we received your transmittal letter, Reference  
(b), which reads **as follows:**

"On 27 June 1951 under separate cover we forwarded  
you twenty-five (25) copies of Drawing RA-106, dated  
26 June 1951.

This drawing is an amplification drawing and should  
cause no increase to the Contract Price. Proceed  
with the work shown thereon."

Since this drawing shows many new details which may involve  
a cost change, we have sent the above referenced drawing to the  
interested subcontractors with the request that they advise  
us if this revisions affects their subcontract price.

Under the authority and requirements of the contract, we  
hereby request that proper adjustment of the contract price  
and contract time be dealt with under the terms and conditions  
of the contract. This change will be analyzed with all inter-  
ested subcontractors and detailed estimates will be submitted  
to you as quickly as possible. Definite extension of contract  
time for completion will be requested as soon as determination  
can be made of the effect of this change on the entire job  
progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*M.J. Grogan*  
M.J. Grogan  
Project Manager

MJG/PDV/eas



FULLER - TURNER - WALSH - SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

*file*

July 5, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General Assembly and North Parking Garage -  
CHANGE NO. 224 - June 28, 1951 Structural Revisions

References (a) U.N. Dwg. GA-R-CS-25C, dated June 25, 1951  
(b) " GA-S-35C, rev. No.7, dated June 27, 1951  
(c) Mr. James A. Dawson's letter 28 June 1951 to FTWS, Inc.

Dear Mr. Dawson:


On June 28, 1951 we received prints of References (a) and (b) and on June 29, 1951 we received your transmittal letter, Reference (c), which reads, in part, as follows:

"Submit for our consideration the prices which affect the Contract Price and proceed with the work shown on the above drawings."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan  
Project Manager

MJG/PDV/eas

**FULLER - TURNER - WALSH - SLATTERY, INC.**  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

*file*

July 5, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General Assembly and North Parking  
Garage -  
CHANGE NO. 223 - June 27, 1951 Plumbing Revisions

References: (a) U.N. Dwg. SK-GA-P-8-1 dated June 21, 1951  
(b) " SK-GA-P-4-1 " June 26, 1951  
(c) Mr. James A. Dawson's letter 28 June 1951 to FTWS, I

Dear Mr. Dawson:

On June 27, 1951 we received prints of References (a) and (b) and on June 29, 1951 we received your transmittal letter, Reference (c), which reads as follows:

"On 28 June 1951 we forwarded you under separate cover twenty-one (21) copies of Drawing SK-GA-P-8-1, dated 21 June 1951.

Proceed with the work shown thereon and submit for our consideration prices which affect the Contract Price.

On 28 June 1951 we also forwarded you twenty-one (21) copies of Drawing SK-GA-P-4-1 dated 26 June 1951. The Plumbing work shown thereon will cause no change to the Contract Price and you are to proceed with the work shown thereon."

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*M. J. Grogan*  
O. M. J. Grogan  
Project Manager

MJG/PDV/eas



FULLER - TURNER - WALSH - SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

*file*

July 5, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272  
United Nations 17, NEW YORK

RE: CONTRACT HQ 1/82 - GENERAL ASSEMBLY & NORTH PARKING SPACE  
ESTIMATE FOR CHANGE NO. 189  
"Revisions to Chip Collector in Recording  
Rooms No. 5 and No. 6"

References: a) United Nations Drawing SK-GA-H2-11, dated 5/25/51  
b) FTWS Letter (Grogan) to United Nations dated 6/7/51

Dear Sir:

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we claim an increase in our total guaranteed maximum cost price in the amount of THREE HUNDRED SIX DOLLARS AND EIGHTY TWO CENTS (\$306.82) for the changes in work listed herein which are required by the above "references".

Attached are three (3) copies of Kerby Saunders E.W.O. #13 (1 sheet) with supporting letter from The Spencer Turbine Co., dated 6/11/51.

Will you kindly issue a Change Order-ADDITION in the amount of \$306.82 covering the changes in work itemized above.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*M. J. Grogan*

M. J. Grogan  
Project Manager

MJG:CER:amc  
attach.



**FULLER - TURNER - WALSH - SLATTERY, INC.**  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.  
July 5, 1951

*file*

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General Assembly and North Parking Garage -  
CHANGE NO. 181A - Ductwork Added for Two (2) Additional  
Type 15-A Fixtures in Committee Rooms

Reference: (a) Mr. James A. Dawson's letter 21 June 1951 to FTWS, Inc.

Dear Mr. Dawson:

This Change is supplemental to our Change No. 181, dated June 20, 1951, which described the addition of two (2) Type 15-A fixtures in Committee Rooms Nos. 8, 9 and 10.

On June 25, 1951 we received the above references letter, which reads as follows:

"In Committee Room No. 7, two (2) type 15-A fixtures shall be substituted for two (2) type 15 fixtures. The number of fixtures has been changed from 37 to 36.

Proceed with the installation of these two (2) 15-A fixtures together with the necessary air-boxes and rings and the remainder of the work which a revised drawing No. RA-171 will show. This drawing is in the process of being revised and will be issued to you shortly.

In submitting the special fixture prices, please take into consideration the above change."

As explained in our Change No. 181, our Estimate for Change No. 181 will include the costs of the added ductwork for the above revision. The Estimate for Change No. 70 will cover the change in fixture types proper.

Under the authority and requirements of the contract, we hereby request that proper adjustment of the contract price and contract time be dealt with under the terms and conditions of the contract. This change will be analyzed with all interested subcontractors and detailed estimates will be submitted to you as quickly as possible. Definite extension of contract time for completion will be requested as soon as determination can be made of the effect of this change on the entire job progress.

Very truly yours,  
FULLER-TURNER-WALSH-SLATTERY, INC.  
*M. J. Grogan*  
M. J. Grogan  
Project Manager



*Fuller*  
*Please let me see the plan for this*  
**FULLER-TURNER-WALSH-SLATTERY, INC.**  
 UNITED NATIONS CONTRACT  
 403 EAST 42ND STREET  
 NEW YORK 17, N. Y.

*see Rosenbaum 9 July 1951 file*  
**July 5, 1951**

*9 July 51*  
**Mr. James A. Dawson**  
 Co-Ordinator of Construction  
 Headquarters Planning Office  
 Room 2272  
 United Nations 17, NEW YORK

**RE: CONTRACT HQ 1/82 - GENERAL ASSEMBLY AND NORTH PARKING SPACE**  
**ESTIMATE FOR CHANGE NO. 173**  
**"Layout of Mushroom Vents in Assembly Hall"**

**References:** a) United Nations Drawing SK-GA-H3-1, dated 4/30/51  
 b) FTWS Letter (Grogan) to United Nations dated 5/24/51

**Dear Sir:**

In accordance with the requirements and authority of Article 8(g) of our Contract HQ 1/82, we claim an increase in our total guaranteed maximum cost price in the amount of TWENTY TWO THOUSAND THREE HUNDRED NINETY EIGHT DOLLARS AND TWENTY CENTS (\$22,398.20) for the changes in work listed herein which are required by the above "references".

Attached are three (3) copies of Kerby Saunders estimate E.W.O. #18 (1 sheet) with supporting letter from National Sheet Metal Works, Inc. (1 sheet) with their photostated take-off sheets (10 sheets).

Will you kindly issue a Change Order-ADDITION in the amount of \$22,398.20 covering the changes in work itemized above.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*M. J. Grogan*

M. J. Grogan  
 Project Manager

MJG:CER:amc  
 attach.



*Copy CO + work sheets created*  
*Pat Healy*  
*9 July 51*

KERBY SAUNDERS, INC.  
630 WEST 52ND. STREET  
NEW YORK, N.Y.

UNITED NATIONS  
GENERAL ASSEMBLY

June 19, 1951  
Job 50-52

F.T.W.S. Change #173

E.W.O. #18

	<u>LABOR</u>	<u>MAT'L</u>	<u>SUBS</u>	<u>TOTAL</u>
Revision to duct work for Mushroom Vents in G.A. Hall				
Drawing #SK-QA-H3-1				
Sheet Metal Duct National Sheet Metal Works			\$19,476.69	\$19,476.69
15% Overhead & Profit				<u>2,921.51</u>
Total Charge				\$22,398.20



*National Sheet Metal Works, Inc.*

General Assembly  
Revised Dwg. SK-GA-H3-1, 4/30/51  
Orig. Dwg. GA-H-3 & GA-H6, 7/15/50

Ducts from slab to mushrooms only to have #18 ga mains and #22 ga branches, and to be lined with  $\frac{1}{2}$ " Fiberglass. All other ducts to be regular gauges and unlined.

Materials

9119 lbs. galv. iron @ 11.00 cwt.	1003.09
9634 sq.ft. $\frac{1}{2}$ " Fiberglass @22.80 per 100 sq. ft.	<u>2196.55</u>
	3199.64
10% Miscellaneous	<u>319.96</u>
	3519.60

Labor in shop

On ducts 853 hrs.	
On lining 1337 hrs.	
2190 hrs. @ 3.10 per hr.	6789.00
6% Union Funds	<u>407.34</u>
3.784% Insurance on labor	<u>256.90</u>
	7453.24
10% Manufacturing & Plant Overhead	<u>10972.84</u>
	1097.28
	12070.12

Labor on job

On ducts 1295 hrs. @ 3.10 per hr.	4014.50
6% Union Funds	<u>240.87</u>
	4,255.37
Delivery	<u>182.38</u>
	16,507.87
15% Overhead & Profit	<u>2,476.18</u>
	18,984.05
4.56% on 10,803.50 labor	<u>492.64</u>
Total Increased Cost	\$ 19,476.69

RECEIVED

JUN 6 1951

KERBY SAUNDERS INC.

Revised Orig SK-GA-H3-1 4/30/51  
Original Orig GA-H3+GAH6 dated 7/15/50

Revised

#24	#22	#18	A.F.	3R
—	4840	5334	8665	210
	1.4063	2.1563	197 (Heads)	
	6806*	11502*	8862	
6806			20	
11502			177240	
18308				
20			8862	
366160			1772	
18308			9634 AF	
3616				
21924 LBS Rev.				
12805 " Orig.				
9119 INCR. WEIGHT				

Original

#24	#22	#20	3R
7104	1410	286	210
1.1563	1.4063	1.6583	
8214*	1983*	474*	
8214			
1983	10671		
474	2134		
10671	12805		
20			
213420			



# GENERAL ASSEMBLY - REVISIONS.

## MUSHROOM VENTS & DUCTWORK.

FOR GEN. ASSEMBLY HALL.

REVISED SK-GA-H-3-1 dated 4/30/51

AS COMPARED TO ORIGINAL. GA-H-3 dated 7/15/51

LINE FT DUCT SIZE.

REVISED.

#22GA

#18GA.

MUSHROOMS

18 11' 61x7 AF 18GA.

17 11' 53x17 AF 18GA.

7 4' 17x6 AF 18GA

6 3' 10x6 AF 22GA.

9 3' 10x5 AF 22GA

4 3' 9x5 AF 22GA

4 3' 10x6 AF 22GA

5 3' 10x5 AF 22GA

14 3' 9x5 AF 22GA.

4 4' 17x6 AF 18GA

6 3' 13x5 AF 18GA.

2 3' 13x5 AF 22GA

4 3' 9x5 AF 22GA

4 3' 10x5 AF 22GA

13 3' 9x5 AF 22GA.

5 3' 9x5 AF 22GA

5 3' 10x5 AF 22GA

4 3' 9x5 AF 22GA

12 3' 9x5 AF 22GA

9 8' 42x7 AF 18GA

3+7 3' 12x6 AF 22GA

7 3' 10x5 AF 22GA

2 3' 9x5 AF 22GA

14 7' 37x7 AF 18GA.

7 3' 13x5 AF 22GA

21 3' 9x5 AF 22GA

11 6' 33x7 AF 18GA.

6 3' 16x6 AF 18GA

4 3' 14x6 AF 18GA.

7 3' 9x5 AF 22GA

1 8' 10x6 AF 22GA

4 3' 9x5 AF 22GA

6 3' 10x5 AF 22GA

16 3' 9x5 AF 22GA

13 5' 22x7 AF 18GA

5 3' 11x5 AF 22GA

12 3' 9x5 AF 22GA

3 4' 19x7 AF 18GA

2 3' 10x7 AF 22GA

18

27

12

12

15

42

6

12

12

39

15

15

12

36

30

21

6

21

63

21

3

12

18

48

15

36

6

204

199

28

16

18

75

103

74

22

14

65

13

THE THE THE THE

THE THE THE

\*NOTE - ALL AF  
LINING 1/2"



Line Ft. Sq Ft. DUCT SIZE

8	3	9x5	AF	22 GA
5	3	10x5		
13	3	9x5		
5	3	13x6		
7	3	11x6		
2	3	11x5		
19	3	9x5		
17	7	33x9	AF	18 GA.
7	6 1/2	31x8		
29	6	30x7		
3	4	16x7		
27	6	29x6		
14	6	29x6		
2	3 1/2	15x7	AF	18 GA
6	5	24x6		
18	6	29x7		
12	6	29x6		
10	3	9x4		
7	4	17x6		
6	3	12x6		
4	3	11x5		
5	3	10x5		
11	3	9x5		
5	3	11x5		
6	3	10x5		
21	3	9x5		
26	8	38x9	AF	18 GA
9	5 1/2	25x9		
10	4 1/2	20x7		
23	5 1/2	25x8		
9	4 1/2	21x7		
10	3 1/2	15x6		
5	3	11x6		
8	3	9x5		
14	3 1/2	15x6		
5	3	11x6		
4	3	10x5		
4	3	9x5		
6	3	6x11		
2	3	11x5		
12	3	10x5		
7	3	9x5		
11	3	14x6		
2	3	12x6		
12	3	11x5		
4+5	3	9x5		

- 24
- 15
- 39
- 17
- 21
- 6
- 57

- 125
- 47
- 184
- 12
- 162
- 84
- 8
- 30
- 108
- 72

30

28

- 18
- 12
- 15
- 33
- 15
- 18
- 63

- 208
- 51
- 45
- 127
- 42

- 35
- 15
- 24
- 49
- 15
- 12
- 12
- 18
- 6
- 36
- 21
- 37
- 6
- 36
- 27

MUSH ROOMS  
 III III III III  
 III III III III III  
 //

N.F.T	Sq FT	DUCT SIZE		#22 GA	#18 GA.	
11	3	10x5	AF	22 GA		
4	3	9x5				
9	4	17x6				
2	3 1/2	17x5				
5	3	10x5				
17	3	9x5				
5	3 1/2	10x5				
4	3 1/2	9x5				
13	3 1/2	14x6				
2	3	12x6				
3	3	11x5				
8	3	9x5				
23	9	45x10	AF	18 GA		
17	6 1/2	31x9				
20	6	28x9				
12	3 1/2	25x8				
10	5	23x7				
4	4 1/2	22x5				
6	5	25x7				
6	5	23x6				
23	3	12x6		22 GA.		
4	3	11x6				
6	3	9x5				
16	3	13x5				
2	3	10x5				
6	3	9x5				
4	4	17x6				
6	3	13x5				
12	3	10x5				
7	3	9x5				
17	3	13x5				
6	3	10x5				
10	3	9x5				
10	3	12x6				
7	3	10x5				
4	3	9x5				
12	3 1/2	17x5				
5	3	15x5				
5	3	10x5				
4	3	9x5				
7	3 1/2	17x5				
5	3 1/2	15x5				
4	3	10x5				
4	3	9x5				
13	3 1/2	15x5				
5	3	11x5				

- 33
- 12
- 36
- 8
- 15
- 51
- 15
- 12
- 42
- 6
- 9
- 24

- 215
- 111
- 127
- 66
- 50
- 18
- 32
- 30

- 69
- 12
- 18
- 48
- 6
- 18
- 16
- 18
- 36
- 21
- 51
- 18
- 30
- 30
- 21
- 12
- 42
- 17
- 15
- 12
- 25
- 17
- 12
- 12
- 42
- 15

MUSHROOMS  
~~THE THE THE~~  
~~THE THE THE~~  
~~THE THE THE~~



				#22 Ga	#18 Ga.	
5	3	10x5	AF 22 Ga.	15		mushrooms
4	3	9x5		12		<del>     </del>
8	3 1/2	15x6		28		<del>     </del>
4	3	11x5		12		
5	3	10x5		15		
4	3	9x5		12		
5	3	13x5		15		
2	3	9x5		6		
6	3	10x5		18		
4	3	9x5		12		
2	3	9x5		6		
5	3	13x5		15		
14	3	9x5		42		
14	3	9x5		42		
13	6	29x8	AF 18 Ga.		82	
12	5	23x7			60	
16	4 1/2	22x6			74	
6	3	11x5			18	
5	4	19x5			20	
22	3 1/2	17x5			80	
10	5	23x7			50	
10	4	17x7			40	
9	4 1/2	22x6			42	
9	4 1/2	22x5			41	
6	3 1/2	16x6			22	
7	3 1/2	16x5			25	
4	3	10x5	AF 22 Ga.	12		
14	3	9x5		42		
9	3	9x5		27		
15	3	10x5		45		
4	3	9x5		12		
6	3	10x5		18		
4	3	9x5		12		
9+9	3	10x5		54		
9+9	3	9x5		54		
2	3	9x5		6		
5	3	10x5		15		
15	3	9x5		45		
15	3	9x5		45		
8	3	10x5		24		
12	3	9x5		36		
13	3	10x5		39		
19	3	9x5		57		
22	7 1/2	37x9	AF 18 Ga.		169	
4	3 1/2	17x5			15	
11	5 1/2	25x9			63	



				#22	#18	
13	5'	23x9	AF	18 GA.		
53	6	29x6	↓		69	MUSHROOM
5	4	17x6			318	#4 TH V
4	4	18x5			20	
28	6	29x6	↓		16	
14	3	9x5	AF	22 GA.	168	
5	3	13x5	↓	42		
3	3	9x5		15		
6	3	10x5		9		
17	3	9x5		18		
6	3	15x5		51		
4	3	13x5		20		
6	3	10x5		12		
10	3	9x5		18		
1+9	3	9x5		30		
13	3	9x5		30		
*394	3	6'	↓	39		
			↓	1182		

Note: Revised takeoff  
continued on following  
sheet.

\* For collars- figured in  
as duct on original takeoff

# REVISED (WEST BOOTH)

36 4 16x8

8 4 16x7

4 3 8x6

17 3 17x6

4 3 12x6

4 3 10x6

4 3 8x6

4 3 9x6

11 3 8x6

33 5 22x7

7 4 20x7

6 3 8x6

6 4 19x7

12 4 18x7

4 4 18x6

8 3 8x6

4 3 15x6

6 7 3 8x6

4 2 30x10

10 4 20x6

3 3 16x6

5 3 11x5

23 5 22x8

12 3 8x5

8 4 20x8

3 3 12x8

7 4 19x7

12 3 15x6

22 3 15x6

22 5 22x7

6 3 12x6

9 3 8x6

6 4 20x6

10 4 18x6

4 3 16x6

8 2 3 8x6

3 3 15x5

2 13 3 8x6

3 3 14x5

9 3 8x6

AF

# REVISED (EAST BOOTH)

4 2 30x10

10 4 20x6

3 3 16x6

5 3 11x5

23 5 22x8

12 3 8x5

8 4 20x8

3 3 12x8

7 4 19x7

12 3 15x6

22 3 15x6

22 5 22x7

6 3 12x6

9 3 8x6

6 4 20x6

10 4 18x6

4 3 16x6

8 2 3 8x6

3 3 15x5

2 13 3 8x6

3 3 14x5

9 3 8x6

144

32

51

12

12

12

12

33

165

32

26

52

16

14

27

44

11

115

38

30

42

77

110

26

40

15

10

27

45

10

27

4840

5334

12

12

12

12

33

18

24

39

15

36

10

18

27

30

45

10

27

4840

5334

12

12

12

12

33

18

24

39

15

36

10

18

27

30

45

10

27

4840

5334

12

12

12

12

33

18

24

39

15

36

10

18

27

30

45

10

27

4840

5334

12

12

12

12

33

18

24

39

15

36

10

18

27

30

45

10

27

4840

5334

12

12

12

12

33

18

24

39

15

36

10

18

27

30

45

10

27

4840

5334

12

12

12

12

33

18

24

39

15

36

10

18

27

30

45

10

27

4840

5334

24

22

20

## DUCTS TO MUSHROOMS.

## ORIGINAL

48	7	33x10				
11	6	31x7			336	
11	5 <sup>2</sup>	29x7			66	
9	4	19x6		63		
10	3	14x5		36		
				30		
3	3	10x5		9		
23	3	10x5		69		
6	3	10x5		18		
10	3	14x5		30		
30	3	10x5		90		
50	3	10x5		150		
105	3	10x5		315		
20	3	10x5		60		
26	11	61x7				286
17	8 <sup>2</sup>	47x7			148	
10	6 <sup>2</sup>	35x7			67	
7	5'	27x7		37		
15	5	25x7		75		
4	4	20x6		16		
2	3'	16x5		6		
30	3	10x5		90		
40	3	10x5		120		
56	3	10x5		168		
90	3	10x5		270		
26	3	10x5		78		
54	3	10x5		162		
24	6'	30x9		144		
22	6	30x7		132		
18	3'	17x5		60		
20	3	10x5		60		
12	3	14x5		36		
18	3	10x5		54		
20	3	10x5		60		
56	5 <sup>2</sup>	29x6		318		
27	3	10x5		81		
20	3	10x5		60		
13	3	14x5		39		
5	3	10x5		15		
27	4	27x4				



			-30	31-60	61-90	91-
			24	22	20	18
16	3 <sup>2</sup>	18x5	58			
5	3	10x5	15			
21	3	14x5	63			
22	3	10x5	66			
54	5 <sup>2</sup>	29x6	306			
28	4 <sup>2</sup>	23x7	140			
15	4 <sup>2</sup>	23x6	60			
4	4	22x5	16			
60	3	10x5	180			
25	3	10x5	75			
11	3	14x5	33			
36	3	10x5	108			
25	3	10x5	75			
26	3	16x5	78			
10	3	10x5	30			
26	3	14x5	78			
58	8'	43x9		483		
48	3	10x5	144			
21	3	10x5	63			
19	3	14x5	57			
24	3	10x5	72			
43	3	10x5	129			
14	7 <sup>2</sup>	41x7		108		
50	3	10x5	150			
10	4	19x7	40			
86	3	10x5	258			
14	3	14x5	42			
10	3	10x5	30			
16	3 <sup>2</sup>	18x5	58			
12	3	14x5	36			
36	3	10x5	108			

Booths 40'x8 Draw GA-H-6 7/15/51  
ORIGINAL. (WEST BOOTH)

10	5	22x8	50
7	3	8x6	21
19	5	22x7	95
3	3	8x6	9
6	4	20x6	26
9	3	8x6	27
6	3 <sup>2</sup>	16x6	22
15	3	8x6	45
25	5'	23x8	133

DIFF

11/11

			-30	31-60	61-90	91-			
			24	22	20	18			
7	4 <sup>2</sup>	20x8	33						
4	3	8x6	12						
16	4 <sup>1</sup> / <sub>2</sub>	20x7	72						
5	3	10x6	15						
5	3	12x6	15						
5	3	8x6	15						
3	3	9x6	9						
6	3	8x6	18						
ORIGINAL (EAST BOOTH)									
6	5	24x6	30						
9	4 <sup>2</sup>	22x6	42						✓ DIF THH III
9	4 <sup>1</sup> / <sub>2</sub>	21x6	42						
4	4'	19x6	18						
3	3	8x6	9						
7	3'	14x6	23						✓ R III
6	3	12x6	18						
11	3	8x6	33						
3	3	10x6	9						
13	3	8x6	39						
2	6 <sup>2</sup>	28x12	14						
5	5	24x6	25						
2	3 <sup>1</sup> / <sub>2</sub>	15x6	7						
5	3'	14x6	17						
15	5 <sup>1</sup> / <sub>2</sub>	25x8	81						
13	3	8x6	39						
6	5'	24x8	32						
3	3	12x6	9						
7	4'	18x8	30						
13	3 <sup>1</sup> / <sub>2</sub>	15x6	45						
29	3 <sup>1</sup> / <sub>2</sub>	15x6	102						
2	3	8x6	6						
			7104	1410	286				



FULLER - TURNER - WALSH - SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

file  
July 5, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272  
United Nations 17, NEW YORK

RE: CONTRACT HQ 1/82 - GENERAL ASSEMBLY AND NORTH PARKING SPACE  
ESTIMATE FOR CHANGE NOS. 24, 24A & 24B  
"Dutch Brick Sample Layout"

References: a) United Nations Letter (Dawson) to FTWS dated 10/2/50  
b) " " " " " " " " 2/19/51  
c) " " " " " " " " 3/5/51  
d) FTWS Letter (Reese) to United Nations dated 1/29/51  
e) " " (Grogan) " " " " " 10/13/50  
f) " " " " " " " " 3/1/51  
g) " " " " " " " " 3/14/51  
h) United Nations Letter Copy (McLeod) to FTWS dated 2/8/51

Dear Sir:

In accordance with the requirement and authority of Article 8(g) of our Contract HQ 1/82, we claim an increase in our total guaranteed maximum cost price in the amount of TWO HUNDRED EIGHTY SEVEN DOLLARS AND NINETY FOUR CENTS (\$287.94) for the work itemized in this estimate as required by the above "references".

The above price is broken down as follows:

I - WORK BY FTWS INC. (Our Own Forces)

ADD

Material (Purchased by U. N.):

U.N. Check #A-164 for Dutch Brick.....\$26.00  
" " " #A-165 for Drayage of above 22.52  
\$48.52

Labor:

DWR #011672 - 1/25/51.....\$16.32  
DWR #011673 - 2/2/51..... 6.84  
DWR #011775 - 6/13/51..... 16.32  
\$39.48

F.O.A.B. & U.I..... 1.67

\$41.15..... \$41.15

Total Addition - F-T-W-S, Inc..... \$89.67..... \$ 89.67



Mr. James A. Dawson  
Re: Contract HQ 1/82 - General Assembly & North Parking  
Space - Estimate for Change Nos. 24, 24A & 24B

July 5, 1951  
page (2)

Figures(Work by FTWS, Inc.) brought forward from page (1)..... <sup>ADD</sup> \$ 89.67

II - WORK BY DEL TURCO BROS. INC.

Installation, Cleaning & Sealing of Dutch Brick Sample Panel

Installing:

16 hrs. tile setter @ \$3.07.....\$49.12  
16 hrs. tile helper @ \$2.40.....\$38.40

Cleaning & Sealing:

4/2/51 - 8 hrs. tile helper @ \$2.40.....\$19.20  
5/3/51 - 8 hrs. tile helper @ \$2.40.....\$19.20

\$125.92

Welfare & Pension Fund @ 6%..... 7.56  
\$133.48

Material:

1 YD. of Sand.....\$ 3.50  
5 BAGS of Cement @ \$1.10/bag..... 5.50  
20 LBS. of color @ \$.50/lb..... 10.00  
Trucking..... 15.00

\$167.48

O & P 15%..... 25.12

\$192.60

F.O.A.B. & U.I. @ 4 1/2%..... 5.67

Total Addition: Del Turco Bros., Inc.....\$198.27.....\$ 198.27

NET ADDITION - THIS ESTIMATE....\$ 287.94

Attached hereto are one (1) copy each of the above mentioned D.W.R.'s for F-T-W-S, Inc. work.

Will you kindly issue a Change Order-ADDITION in the lump sum amount of \$287.94 to cover the work itemized above.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



M. J. Grogan  
Project Manager

MJG:CER:anc  
attach.

## FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 5, 1951

Mr. James A. Dawson  
Headquarters Planning Office  
Room 2272  
United Nations,  
New York

Re: Contract HQ 1/82 - General Assembly  
and North Parking Space  
Heating, Ventilating & Air Conditioning

Dear Sir:

This will acknowledge your letter of 26 June 1951 in reply to our communication of 18 June 1951 regarding the fabrication of items included and/or detailed on preliminary approved or approved as noted shop drawings.

We note that you were in accord with our letter of 18 June 1951 with the proviso that we be responsible for any changes which might develop from further study of the conditions, the drawings, and/or coordination with various trades.

We are not quite clear what you mean by being responsible for any change which might develop from further study of conditions and drawings.

We of course are responsible for changes made necessary by lack of coordination with various trades, but do not agree to be responsible, for revisions brought about, by changes in Architectural plans and/or engineering features, which may arise, at a date later than the contract drawings in our possession at the time the preliminary shop drawings were made; presented, and returned approved, or approved as noted.

Changes such as these have always been shown on revised engineering and architectural drawings, and been made the subject of a change order.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*  
C. E. Reese  
Project Engineer

CER:CWB:tw





-9✓

**COPY**

**FULLER-TURNER-WALSH-SLATTERY, INC.**

UNITED NATIONS CONTRACT

NEW YORK

July 5, 1951

Mr. James A. Dawson  
Headquarters Planning Office  
Room 2272  
United Nations,  
New York

Re: Contract HQ 1/52 - General Assembly  
and North Parking Space  
Heating, Ventilating & Air Conditioning

Dear Sir:

This will acknowledge your letter of 26 June 1951 in reply to our communication of 18 June 1951 regarding the fabrication of items included and/or detailed on preliminary approved or approved as noted shop drawings.

We note that you were in accord with our letter of 18 June 1951 with the proviso that we be responsible for any changes which might develop from further study of the conditions, the drawings, and/or coordination with various trades.

We are not quite clear what you mean by being responsible for any change which might develop from further study of conditions and drawings.

We of course are responsible for changes made necessary by lack of coordination with various trades, but do not agree to be responsible, for revisions brought about, by changes in Architectural plans and/or engineering features, which may arise, at a date later than the contract drawings in our possession at the time the preliminary shop drawings were made; presented, and returned approved, or approved as noted.

Changes such as these have always been shown on revised engineering and architectural drawings, and been made the subject of a change order.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. A. Reese B.*  
C. A. Reese  
Project Engineer

CAR:GWB:tw



No-5-18-9  
OREGON 9-3950

FULLER-TURNER-WALSH-SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

*mrs. Tyler*

July 5, 1951

*150 Gen Files*

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General  
Assembly and North Parking  
Garage - (GENERAL ASSEMBLY)  
Reinforcing Steel Details

Dear Mr. Dawson:

We are sending you herewith six (6) prints of the following Reinforcing Steel shop drawings, submitted by Brennan & Sloan, Inc.:

601	7/2/51	Reinforcing Steel Details - El. 86'-0"
602	"	"
603	"	"
604	"	"

Will you please return three (3) prints each of the above drawings, marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*  
C. E. Reese  
Project Engineer

CER/BK/eas



ISSUANCE OF DRAWINGS

OFFICE COPY

5 July 1951

26 July 1951

GA & North Parking

Fuller-Turner-Walsh-Slaterry

hand

Submitted by Brennan & Sloan & Knickerbocker

3	601	2 July '51	Reinforcing Steel Details -El. 86'-0"
3	602	"	Same
3	603	"	"
3	604	"	"

(APPROVED AS NOTED 10 July 1951 J.C.B. RESUBMIT)



*J. C. B.*

*Hopper  
Ready*

FULLER-TURNER-WALSH-SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

*Mr. Haged  
Tyler  
To Gen. Fick*

July 5, 1951

Mr. James A. Dawson  
Headquarters Planning Office  
Room 2272  
United Nations,  
New York

Re: Contract HQ 1/82 - General Assembly  
and North Parking Space  
(GENERAL ASSEMBLY)  
Cut Stone

Dear Mr. Dawson:

We are sending you herewith, four (4) prints of the following Cut Stone  
shop drawings submitted by Monahan-McCann Stone Co.:

#788-10      Rev. 7/1/51      Vermont Pearl Marble -  
North Elevation

Will you please return two (2) prints each of the above drawings marked  
with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*

C. E. Reese  
Project Engineer

CER:MH:tw

RECEIVED  
JUL 10 1951  
UNITED NATIONS  
SECRET



ISSUANCE OF DRAWINGS

OFFICE COPY

5 July 1951

23 July 1951

GA & North Parking  
Fuller-Turner-Walsh-Slattery

hand

Submitted by Monahan-McCann

2      788-10      19Dec'50      Vermont Pearl Marble - North Elevation  
(APPROVED AS NOTED 23 July 1951 REN RESUBMIT)

NOTE: Resubmit Drawing as Noted: Canopy #1 to be omitted - Rev. #37 will show  
this omission: FTWS please note that Jos. Weiss are to add Granite Bases  
noted herein.

RECEIVED

JUL 23 1951

FULLER-TURNER-WALSH-SLATTERY  
INCORPORATED

*LV Tyler*

*Hoffman*  
*Nealy*

FULLER-TURNER-WALSH-SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

*WEIKKE*

July 5, 1951

*to H.M. Fick*

Mr. James A. Dawson  
Co-Ordinator of Construction  
United Nations Headquarters  
Room 2272, United Nations  
New York, N. Y.

Re: HQ 1/82 Contract - General Assembly & North Parking  
(General Assembly)  
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following Miscellaneous Iron shop drawings submitted by General Bronze Corporation and C. E. Halback & Co. -

HGP 70-1      dated 6/28/51 - "Misc. Access Panels at  
Rolling Steel Shutters,  
Frames & Grilles in Floor  
Vestibule #4"

Will you please return two (2) prints of the above drawing marked with your approval or necessary corrections.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*M.H.*  
CER/lbr

*C.E. Reese*  
C. E. Reese  
Project Engineer



ISSUANCE OF DRAWINGS

OFFICE COPY

5 July 1951

18 July 1951


GA & North Parking

Fuller-Turner-Walsh-Slatery

hand

Submitted by General Bronze & Halback

2      HGP-70-1      28 June '51      Misc. Access Panels at Rolling Steel Shutters,  
Frames & Grilles in Floor Vestibule #4  
(APPROVED AS NOTED 17 July 1951 PB/GEA RESUBMIT)

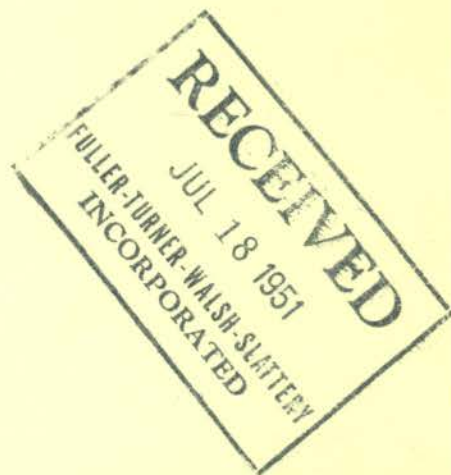

*Jv Byler*



*Fuller-Turner-Walsh-Slaterry*  
*7/5*  
*301*

FULLER-TURNER-WALSH-SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

*TVIER*

July 5, 1951

*Files*  
*Her*

Mr. James A. Dawson  
Headquarters Planning Office  
Room 2272  
United Nations,  
New York

Re: Contract HQ 1/82 - General Assembly  
and North Parking Space  
Heating, Ventilating & Air Conditioning  
Ductwork Shop Drawings

Dear Sir:

We are submitting herewith six (6) copies of the following National Sheet Metal Works, Inc. shop drawings for Ductwork being furnished under the heating, ventilating and air conditioning subcontract of Kerby Saunders, Inc.

Drawing #GA-1B-5, Fan Room #2, between columns 25 to 28  
and N to M.

Drawing #GA-1B-1, Master Control Room on 1st Basement,  
Columns N to S and 22 to 24.

Please review the above drawings and return three (3) copies together with your approval and/or comments at your earliest convenience.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*  
C. E. Reese  
Project Engineer

CER:WWS:tw

RECEIVED

JUL 5 1951

United Nations Headquarters  
W. K. Harrison-Director of Planning

ISSUANCE OF DRAWINGS

OFFICE COPY

5 July 1951

18 July 1951

GA & North Parking

Fuller-Turner-Walsh-Slatery

hand

Submitted by Kerby Saunders (Nat'l Sheet Metal Dwgs.)


3	GA-1B-5	30Mar'51	Fan Rm. #2 between cols. 25 to 28 and N to M
3	GA-1B-1	21Mar'51	Master Control Rm. on 1st Bemt. cols. N to S & 22 to 24

(APPROVED AS NOTED 16 July 1951 BDP RESUBMIT)

NOTE: FROM SYSKA & HENNESSY

"These drawings are approved, except as noted in yellow crayon."

"All approvals are subject to strict compliance with the Contract Plans and Specifications and to all Authorities having Jurisdiction."

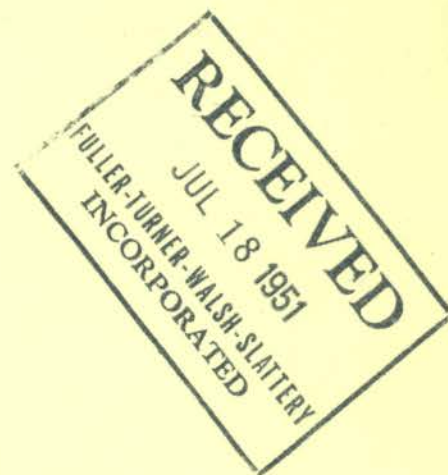

*SV Tyler*





ISSUANCE OF DRAWINGS

OFFICE COPY

5 July 1951

9 July 1951

GA & North Parking  
Fuller-Turner-Walsh-Slattery

hand

Submitted by General Bronse & Halback

2 HGP-20-1 5 July '51 Angle Trap Door Frame (Projection Booth)  
(APPROVED AS NOTED 9 July 1951 PB/GEA RESUBMIT)



*SV Tyler*

5 July 1951

Fuller-Turner-Walsh-Slattey, Inc.  
403 East 42 Street  
New York 17, New York

Re: HQ 1/82 Contract - General  
Assembly and Northerly Portion  
of the Parking Garage  
Painting and Finishing -  
Color Schedule

Gentlemen:

Today we are forwarding to you separately ten (10) prints of General Assembly Paint Schedule for Sound Studio Areas, Elevation 429'-0", dated 5 July 1951.

Our Painting and Finishing requirements for the noted areas are set forth on these sheets. The several types of paint to be employed for final coats are as set forth on the Schedules and are as approved for use as recorded in our letter to you of 29 June 1951, subject Painting and Finishing Materials. The finished color designations given on this schedule correspond to the identifying color names and numbers affixed to color chips forwarded with this communication. Three (3) chips of each different color called for are forwarded herewith.

You are to proceed with the work indicated on the referenced Schedule. As our finish requirements are developed for other areas, additional Schedules will be prepared and forwarded to you.

Very truly yours,

James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office

HBW:eam  
cc: Bohanon  
Nelson  
Weigel  
Healy  
Harris  
Hopper  
Zunser  
VanName

*Sorenson Ryan*

5 July 1951

Fuller-Turner-Walsh-Slattey, Inc.  
403 East 42 Street  
New York 17, New York

Re: General Assembly and Northerly  
Portion of the Parking Garage  
Contract HS 1/82 - Plumbing


Gentlemen:


On 3 July 1951 we forwarded you under separate cover twenty-one (21) copies of Drawing SS-43-1-4B-1, dated 28 June 1951, the relocation of continuous drain and leaders at level 4.1'-0" on Column Lines 32A and north of Column Line 36.

Since the revision involves only changes in dimensions there should be no change in cost. Proceed with the work shown on the above drawing.

Very truly yours,

James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office

  
JJH:eam  
cc: Bohanon  
Nelson  
Weigel  
Healy  
Harris  
Hopper  
Zunser  
VanName  
Ryer  
Hannegan  
S & H - 2





## FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 3, 1951

*W. Turner Walsh*  
*W. Turner Walsh*  
*W. Turner Walsh*

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272, United Nations  
New York 17, N. Y.

Re: General Ass'y. &amp; North Parking - Cont. HQ 1/82

Dear Sir:

We are attaching hereto three (3) signed copies of Change Order #11, which is an addition to the contract of Brennan & Sloan, Inc. and Knickerbocker Construction Co., dated Sept. 25, 1950 for Concrete Construction Work, General Ass'y. & North Parking, U. N. Permanent Headquarters, New York, in the amount of \$251.82.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*H. A. Hiener*  
H. A. Hiener  
Office Manager

HAH:vg  
enc.

## FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 3, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General  
Assembly and North Parking  
Garage -  
Miscellaneous Iron - Change No. 22

Dear Mr. Dawson:

Your drawing RA-128, dated September 28, 1950, shows approximately 60 L.F. of metal lined curtain pocket added on Section 23 at the Press Lounge, Elev. 68'-4".

At a meeting held at your office on November 13, 1950, an extra charge of \$972.00 was quoted by General Bronze Corp. and C.E. Halback & Co. for this added work. At this meeting, Mr. M.M. Harris instructed us to omit the curtain pocket shown since the curtains would be surface applied later under a furnishings contract.

Will you please revise your drawing RA-128 to indicate this change to agree with the decision made at the above meeting.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese  
Project Engineer

CER/PDV/eas



## FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 3, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General  
Assembly and North Parking  
Garage - (GENERAL ASSEMBLY)  
Carpentry & Millwork

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following Carpentry & Millwork shop drawings, submitted by Murray Hill Woodworking Corp.:

305 rev. 6/30/51 F.S. & Elev.-Doors 205, 207, 209, 215  
to 219, incl. - 260, 261, 262

313 dated 6/30/51 F.S. & Elev.-Doors 258-259

Will you please return two (2) prints each of the above drawings,  
marked with your approval or necessary corrections.


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese  
Project Manager

CER/MH/eas





ISSUANCE OF DRAWINGS

OFFICE COPY

3 July 1951

9 August 1951

GA & North Parking  
Fuller-Turner-Walsh-Slattery

hand

Submitted by Murray Hill Woodworking

2      305      26Dec'50      F.S. & Elev. Doors 205,207,209,215 to 219 etc.  
(APPROVED AS NOTED 9 Aug 1951 J.C.B. RESUBMIT)

NOTE: Dwg. 313 will follow

RECEIVED

AUG 10 1951

FULLER-TURNER-WALSH-SLATTERY  
INCORPORATED

*SV Pyler*

ISSUANCE OF DRAWINGS

OFFICE COPY

3 July 1951

16 August 1951

GA & North Parking

Fuller-Turner-Walsh-Slattery

hand

Submitted by Murray Hill Woodworking

2

313

30 June '51 F.S. & Elev. - Doors 258-259

(APPROVED AS NOTED 13 Aug 1951 J.C.B. RESUBMIT)



*S. V. Byler*

*Left  
Hoffa - Rumpeltin  
Hawnegar  
7/3  
LST*

FULLER-TURNER-WALSH-SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

*TYLER*

July 3, 1951

Mr. James A. Dawson  
Headquarters Planning Office  
Room 2272  
United Nations,  
New York

*Gen Files*

Re: Contract HQ 1/82 - General Assembly  
and North Parking Space  
Heating, Ventilating & Air Conditioning  
Panel Heating Riser Diagram and  
Column Chases

---

Dear Sir:

We are submitting herewith six (6) copies of Kerby Saunders, Inc. shop drawing #50-52-318 showing Panel Heating Riser Diagram and Column Chases 1st to 4th floors, dated June 25th 1951.

Please review the above drawing and return three (3) copies together with your approval or comments.


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*

C. E. Reese S  
Project Engineer

CER:WWS:tw





ISSUANCE OF DRAWINGS

OFFICE COPY

3 July 1951

15 August 1951

GA & North Parking  
Fuller-Turner-Walsh-Slattery

hand

Submitted by Kerby Saunders

3 50-52-318 25 June '51 Panel Heating Riser Diagram and Column Chases  
1st to 4th floors

(DISAPPROVED 13 Aug 1951 REN:VR RESUBMIT)

NOTE: FROM SYSKA & HENNESSY

"This drawing is approved."

"All approvals are subject to strict compliance with the Contract Plans and  
Specifications and to all Authorities having Jurisdiction."



## FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 3, 1951

Mr. James A. Dawson  
Headquarters Planning Office  
Room 2272  
United Nations,  
New York

Re: Contract HQ 1/82 - General Assembly  
and North Parking Space  
Sprinkler System  
Risers to Supply Sprinklers

Dear Sir:

We are submitting herewith six (6) copies of the Automatic Sprinkler Corp. of America Shop Drawing #Sheet 1, Job #5-1920 showing location of sleeves for risers to supply sprinklers in back of wood battens of Assembly Hall.

Please review the above drawing and return three (3) copies together with your approval or comments at your earliest convenience.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.



C. E. Reese  
Project Engineer

CER:WWS:tw



ISSUANCE OF DRAWINGS

OFFICE COPY

3 July 1951

25 July 1951

GA & North Parking  
Fuller-Turner-Walsh-Slattery

hand

Submitted by Automatic Sprinkler

3	Sheet 1	None	Location of Sleeves for Risers to supply Sprinklers in back of Wood Battens (DISAPPROVED 24 July 1951 VE:REN RESUBMIT)
---	---------	------	--

NOTE: FROM SYSKA & HENNESSY

"This drawing is approved."

"All approvals are subject to strict compliance with the Contract Plans and  
Specifications and to all authorities having Jurisdiction."



SV Tyler



## FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 3, 1951

Mr. James A. Dawson  
Headquarters Planning Office  
Room 2272  
United Nations,  
New York

Re: Contract HQ 1/82 - General Assembly  
and North Parking Space  
Electrical Distribution  
Panels for Dimmer Equipment

Dear Sir:

We are submitting herewith six (6) copies of each of the following Trumbull Electric Mfg. Co. for the Distribution Panels for the Dimmer Equipment in the General Assembly Hall:

Drawing #DNY - 141 Distribution Panels #4B &amp; 4D

Drawing #DNY - 142 Distribution Panels #4C &amp; 4E

Please review the above and return three (3) copies together with your approval or comments at your earliest convenience.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese  
C. E. Reese

Project Engineer

CER:WWS:tw

RECEIVED

JUL 3 1951

United Nations Headquarters  
W. K. Harrison-Director of Planning



ISSUANCE OF DRAWINGS

OFFICE COPY

3 July 1951

24 July 1951

GA & North Parking

Fuller-Turner-Walsh-Slaterry

hand

Submitted by Fischbach & Moore (Trumbull Elec. Dwg.)

3	DNY-141	19June'51	Distribution Panels 4B & 4D
3	142	29June'51	" " 4C & 4E

(DISAPPROVED 23 July 1951 BDP/REN RESUBMIT)

NOTE: FROM SYSKA & HENNESSY

"These drawings are returned, marked "Returned Without Action", due to the changes in the dimmer controlled lighting."

RECEIVED

JUL 24 1951

FULLER-TURNER-WALSH-SLATTERY  
INCORPORATED

*L. V. Tyler*

## FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 3, 1951

Mr. James A. Dawson  
Headquarters Planning Office  
Room 2272  
United Nations,  
New York

Re: Contract HQ 1/82 - General Assembly  
and North Parking Space  
Electrical - Interlock Wiring -  
Systems 401B-33, 401B-33A and  
Assembly Hall

Dear Sir:

We are submitting herewith six (6) copies of each of the following Trumbull Mfg. Co. shop drawings showing Interlock Wiring for above mentioned systems. This is being furnished under the electrical subcontract of Fischbach & Moore, Inc.

Drawing #137-2, Interlock Wiring for Primary System 401B-33A  
and Assembly Hall

Drawing #137-1, Interlock Wiring for Primary System 401B-33

We request the return of three (3) copies of each of the above drawings together with your approval or comments at your earliest convenience.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese  
C. E. Reese  
Project Engineer

CER:WWS:tw





ISSUANCE OF DRAWINGS

OFFICE COPY

3 July 1951

12 July 1951

GA & North Parking  
Fuller-Turner-Walsh-Slattery

hand

Submitted by Fischbach & Moore (Trumbull Elec. Dwg.

3	137-1	1 June '51	Interlock Wiring for Primary System 401B-33 (APPROVED 11 July 1951 R.E.N.)
3	137-2	"	Interlock Wiring for Primary System 401B-33A and Assembly Hall (APPROVED AS NOTED 11 July 1951 R.E.N.) (RESUBMIT)

NOTE: FROM SYSKA & HENNESSY

"Dwg. No. 137-1 is approved."

"Dwg. No. 137-2 is approved, except as noted in red crayon."

"All approvals are subject to strict compliance with the Contract Plans and  
Specifications and to all Authorities having Jurisdiction."

*L. F. Martin*  
7/12/51

*J. V. Byler*

3 July 1951

Fuller-Turner-Walsh-Slattery, Inc.  
403 East 42 Street  
New York 17, New York

Re: General Assembly and Northerly  
Portion of the Parking Garage  
Contract HQ 1/82 - Movable Partitions

Gentlemen:

On 3 July 1951 we forwarded you ten (10) copies of Drawing No. SK-663, dated 2 July 1951, indicating Hauserman solid partitions and two (2) pairs of swing doors with glass panels to be installed in the area on the First Basement floor level between Column Lines 23R and 23Q. As noted on the drawing, the doors, hardware and partitions are all to come from attic stock and to be installed by your sub-contractor.

Proceed with the work and submit for our consideration prices which may affect the Contract Price due to the installation of this work.

Very truly yours,

James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office

JJHe:eam  
cc: Bohanon  
Nelson  
Weigel  
Healy  
Harris  
Hopper  
Zunser  
VanName  
Ryer

3 July 1951

Fuller-Turner-Walsh-Slattey, Inc.  
403 East 42 Street  
New York 17, New York

Re: General Assembly and Northerly  
Portion of the Parking Garage  
Contract HQ 1/82  
Concrete - Steel

Gentlemen:


Twenty-five (25) copies of each of the following drawings were forwarded you on the dates listed:

	<u>Date of Drawing</u>	<u>Date Sent</u>
GA-E-3-1,	21 June 1951	29 June 1951
GA-CS-B-9, Rev. No.2	28 June 1951	29 June 1951
GA-4-CS-24, Rev.No.1	27 June 1951	28 June 1951
GA-4-CS-25,	27 June 1951	28 June 1951

None of the work shown on the above drawings should cause any change to the Contract Price. Proceed with the installation of the work.

Very truly yours,

James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office

  
JHE:eam  
cc: Bohanon  
Nelson  
Weigel  
Healy  
Harris  
Hopper  
Zunser  
Ryer  
VanName



3 July 1951

Fuller-Turner-Walsh-Glattey, Inc.  
403 East 42 Street  
New York 17, New York

Re: General Assembly and Northerly  
Portion of the Parking Garage  
Contract HQ 1/82  
Concrete - Steel


Gentlemen:

Under separate cover on 2 July 1951, we forwarded you twenty-five (25) copies of Drawing GA-2-CS-22, dated 29 June 1951.

Proceed with the work indicated thereon and submit for our consideration prices which may affect the Contract Price.

Very truly yours,

James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office

  
cc: Bohanon  
Nelson  
Weigel  
Healy  
Harris  
Hopper  
Zunser  
VanName  
Ryer

3 July 1951

Fuller-Turner-Walsh-Slaterry, Inc.  
403 East 42 Street  
New York 17, New York

Re: General Assembly and Northerly  
Portion of the Parking Garage  
Contract HQ 1/82  
Electric

Gentlemen:

On 29 June 1951 we forwarded you under separate cover  
twenty-one (21) copies of Drawing SK-GA-E-4L-1 dated 27 June  
1951.

Proceed with the work shown thereon and submit for  
our consideration prices which affect the Contract Price.

Very truly yours,

James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office

  
J. H. Hearn

cc: Bohanon  
Nelson  
Weigel  
Healy  
Harris  
Hopper  
Zunser  
VanName  
Ryer  
Harnegan  
Seelman  
S & H - 2

## FULLER-TURNER-WALSH-SLATTERY, INC.

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 2, 1951

*Wm. M. H. B. S.*

*file*

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272, United Nations  
New York 17, New York

Re: General Ass'y. &amp; North Parking, Contract HQ 1/82

Dear Sir:

We are attaching hereto three (3) signed copies of Change Order #10, which is a deduction to the contract of Brenman & Sloan, Inc. and Knickerbocker Construction Co., Inc., dated Sept. 25, 1950 for Concrete Construction Work, General Ass'y. & North Parking, U. N. Permanent Headquarters, New York, in the amount of \$186.07.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*H. A. Hiener*H. A. Hiener  
Office Manager

HAH:vh

enc.





**FULLER-TURNER-WALSH-SLATTERY, INC.**  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

*Cent files*

July 2, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General  
Assembly and North Parking  
Garage -  
Information Required from  
the United Nations

Dear Mr. Dawson:

We are forwarding herewith three (3) copies of each of the following:

- List No. 1 - Design Information Required from the United Nations
- List No. 2 - Mechanical & Electrical Information Required from the United Nations
- List No. 3 - Architectural Shop Drawings at United Nations for Approval
- List No. 4 - Mechanical & Electrical Shop Drawings at United Nations for Approval.

It is imperative that the missing information contained in the above lists be given to us immediately so as not to further delay the completion of the General Assembly work.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*  
C. E. Reese  
Project Engineer

CER/eas

cc/ Messrs. M. Harris  
J.J. Healy  
W. Hopper

LIST NO. 1

July 3, 1951

FULLER-TURNER-WALSH-SLATTERY, INC.  
403 East 42nd Street  
New York, N.Y.

GENERAL ASSEMBLY

DESIGN INFORMATION REQUIRED  
FROM THE UNITED NATIONS AS OF  
July 3, 1951

1. Location and design details of Directional Signs
2. Muray design for the Photosensitive Glass
3. Details of Undulant Canopy, North of Canopy 1
4. Paint Schedule for Studios
5. Reflected ceiling plans for 3rd & 4th floor (promised 24 March 1951)
6. Layout of South Portion and Details of Catwalk
7. Details and location of Alum. Rail Brackets-Stairs No. 35A, 35B, 40 & 41
8. Details of Metal Brackets behind wood battens in Assembly Hall
9. Details of Illuminated Bulletin Board - Dwg. A125
10. Details of hung lintels at counters - 1st bsmt.
11. Detail Dwgs. RA-133, RA-134 & RA-136 - referred to on A-131
12. Escalator Detail Dwgs. DSK 40; & 402
13. Marble Type Selection for Screen in South Lobby
14. Revised details of Canopies No. 1 & 2 & Vestibules No. 1 & 2
15. Revised Treatment at Coving - Transformer Vaults 1, 2, 3 & 4
16. Details of Coving on East Podium Wall
17. Redesign of Ramp Pedestals and Ramp Columns
18. Redesign of North Wall Column

FULLER-TURNER-WALSH-SLATTERY, INC.  
403 East 42nd Street  
New York, N. Y.

List No. 2

July 3, 1951

INFORMATION NEEDED FROM U. N.

ON NORTH PARKING AND GENERAL ASSEMBLY CONTRACT

- I     Schedule of Registers, Grilles and Air Diffusers  
      (for upper floors)
- II    All data not yet received on Bulletin of Change No. 1,  
      Heating and Ventilating, dated October 23rd 1950.  
      (F.T.W.S. - C.O. #40); and on Bulletin of Changes  
      No. 1, Electrical, dated October 23rd 1950 (F.T.W.S. -  
      C.O. #38.)  
      (Refer to F.T.W.S. letter dated February 12th 1951 for  
      drawing requirements.)
- III   Decision on design, layout and type of special lights in  
      Conference Room #4.



LIST NO. 3

July 3, 1951

GENERAL ASSEMBLY AND NORTH PARKING  
STATUS OF SHOP DRAWINGS SUBMITTED  
TO UNITED NATIONS FOR APPROVAL  
ON OR BEFORE - June 26, 1951

<u>Subcontractor</u>	<u>Dwg. No.</u>	<u>Title</u>	<u>Date Submitted</u>
C.E. Halback Misc.Iron	HGP-88-1	Det.Angle Outrigger to receive Furring on N/Wall Cols,	5/17/51
	40-1	Framing for Light Cove at Ceiling-Conf. Rm. 4	5/21/51
	23-2	Steel Brackets for Facia-Canopy #2	6/5/51
	51-1 to 3	Booth & Wall Framing,E/Wall Comm.Rms. 8 to 10	"
	38-1 & 2	5" Furring Channels,Conf.Rm.4, S/End and E. & W. Walls	6/12/51
	43-2	St. Railings & Angles-Stair #37	6/19/51
	51-4	F.S.Det.Booth Sash & Framing Comm.Rms. 7 to 10	6/20/51
	51-5 to 9	Booth & Wall Framing, Coom Rms. 7 & 10	"
	48-3	Cast Iron Saddles	6/22/51
	36-1	Ceiling Hangers for Retractable Screen,Conf.Rm. 4	6/25/51
	49-3	Steel & Glass Screen 1B-57/GM	"
	52-1	Counters in S.I.Booths,Lower Level, W/Wall, Conf. Rm. 4	6/26/51
	52-2	Counters in S.I.Booths,Comm.Rms. 7 & 10	"
Monahan-McCann Cut Stone	Sheet 7	Anchor Dwg.showing Type Anchors & Method used in N/Elev.	6/15/51
	Sheet 8	Anchor Dwg. showing Types used for Dwgs. 8H & 9S	6/19/51
	#22	Ramp #12 (Republic Stone)	6/22/51
	Sheet 3	Anchors,typical Wall Elev.&Sect.	6/25/51
	Sheet 4	Anchors, Method of Anchoring Parapet between Cols. O'& I',27-25	"
Atlantic Metal Doors	Sheet 55	Schedule,Book Store-Proj.Rm.	6/22/51
	D-50	Detail Sheet " "	"
Hauserman Partitions	Sheet 1	1st Bsmt.	"
General Bronze Orn. Metal	GBA-4	Alum.Int. Canopies 1&2	5/7/51
	22 & 23	Vestibule Encl. 1 & 2	"
	26 & 27	S.S.Facia,Cnaopies 1 & 2	5/29/51
	35	Light Trough Soffits in Toilets	6/26/51

Continued . . . . .

LIST NO. 3 (General Assembly & ~~2~~-  
North Parking Space

July 3, 1951

A. Munder	8	Flashing Det. @ M.H. Neck	5/24/51
Sheet Metal	3	" El. 41'-0"	6/25/51
	5 to 7	Details, Canopies 1 to 3	"
DellTurco	1	Key Plan showing Terrazzo Work	6/12/51
Terrazzo	2	Details of Terrazzo Work	"
Murray Hill Woodwork	306 to 309	Plan, Elev. & Det., Conf. Rm. 4	5/3/51

FOLLER-TURNER-WALSH-SLATTERY, INC.  
403 East 42nd Street  
New York, N. Y.

List No. 4

July 3, 1951

LIST OF NORTH PARKING & GENERAL ASSEMBLY MECHANICAL & ELECTRICAL DRAWINGS

AT U. N.

Automatic Sprinkler Corp.

None

Eugene Duklauer, Inc.

- 1) Drawing DsKF-1, details of Type "E" Lav.&Soap Disp. - sent over 6/19/51.

Fischbach & Moore, Inc.

- 1) Drawing DNY-137(Trumbull) - Interlocking wiring - sent over 5/31/51.
- 2) Print 1270-1(Edwards) Directory Frame - sent over 5/11/51.

Kerby Saunders, Inc.

- 1) Sample-High Pressure Straight Line Diffuser(Anemostat)-sent over 4/18/51.
- 2) Sample and letter re pipe insulation(change in type) - sent over 5/4/51.
- 3) Samples and letter re pipe insulation - sent over 5/28/51.
- 4) Part III - Schedule of Grilles & Diffusers(Anemostat)-sent over 6/19/51.
- 5) Dwg.D-10045-16,Orientation Dwg. for diffusers - sent over 6/19/51.
- 6) " D-10045-15, " " " " - " " "
- 7) " D-10045-17-1 Typical Conn. for diffusers - " " "
- 8) " D-10045-17-2 " " " " - " " "
- 9) Power's Schedule of Temp.Controls - sent over 6/28/51.
- 10) N.S.M. Dwg. 2B-3, Fan Room #1 - sent over 6/28/51.
- 11) " " 2B-1, 2nd Basement ductwork - sent over 6/28/51.

Otis Elevator Co.

- 1) Drawing 37-A6395A, Car Position Indicator - sent over 6/14/51.
- 2) Tyler Dwg. EQ, Elev. Entrance details - sent over 6/29/51.



FULLER-TURNER-WALSH-SLATTERY, INC.  
403 East 42nd Street  
New York, N. Y.

List No. 4

July 3, 1951

LIST OF NORTH PARKING & GENERAL ASSEMBLY MECHANICAL & ELECTRICAL DRAWINGS

AT U. N.

Otis Elevator Co. (continued)

3) Tyler Dwg. EQ-1, Elev. Entrance details - sent over 6/29/51.

4) " " EQ-2, " " " - " " "

Airmatic Systems Co.

None

**FULLER-TURNER-WALSH-SLATTERY, INC.**

UNITED NATIONS CONTRACT

403 EAST 42ND STREET

NEW YORK 17, N. Y.

July 2, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General  
Assembly and North Parking  
Garage -  
Change No. 202- Finish Hardware

Dear Mr. Dawson:

4 COPIES.

We are sending you herewith a copy of a supplementary Hardware Schedule for the General Assembly as prepared by Lockwood Hardware Mfg. Co., covering the additional hardware required by your Dwg. No. RA-127A, Rev. No. 29.

The enclosed schedule shows Lockwood's interpretation of the hardware requirements for the added hatch doors and counter in Space 1B155. They have requested, however, that when new openings are added to your plans, that you indicate the general hardware requirements, so that they may list the hardware order accordingly.

You will note on the enclosed schedule that Lockwood has shown a pair of Soss hinges No. 204 for the hinged counter top in Space 1B-155. If the thickness of the top were increased to 1" or 1-1/8", a No. 208 hinge could be used which is much heavier than the No. 204 listed.


Will you please return two (2) of the enclosed schedules marked with your approval or comments.

Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

C. E. Reese

C. E. Reese  
Project Engineer



*Hopper  
Healy*

FULLER-TURNER-WALSH-SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

July 2, 1951

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

*WELCH  
Tylan*

*John. Fick*

Re: Contract HQ 1/82 - General  
Assembly and North Parking  
Garage - (GENERAL ASSEMBLY)  
Miscellaneous Iron

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following  
Miscellaneous Iron shop drawing, submitted by General Bronze  
Copp. & C.E. Halback & Co.:

HGP-49-4 rev. 6/28/51 Steel & Glass Screen 107  
G.M.

Will you please return two (2) prints of the above drawing,  
marked with your approval or necessary corrections.


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C.E. Reese*

C. E. Reese  
Project Engineer

*M.H.*  
CER/PDV/eas





ISSUANCE OF DRAWINGS

OFFICE COPY

General Assembly July 13-51  
F W H.

Manning

C. E. Hallman Co.

2 H&P-44-1 Steel & Glass Screen

(Approved Notes - Reprint - VR)

RECEIVED

JUL 13 1951

FULLER-TURNER-WALSH-SLATTERY  
INCORPORATED

Boa

*Hopper*  
*Healy*

FULLER-TURNER-WALSH-SLATTERY, INC.  
UNITED NATIONS CONTRACT  
403 EAST 42ND STREET  
NEW YORK 17, N. Y.

*WEINER*  
*Tyler*

July 2, 1951

*To HAN, Tica*

Mr. James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office  
Room 2272 - United Nations  
New York, N.Y.

Re: Contract HQ 1/82 - General  
Assembly and North Parking  
Garage -  
Sheet Metal Work

Dear Mr. Dawson:

We are sending you herewith four (4) prints of the following  
Sheet Metal Work shop drawing, submitted by A. Munder & Son, Inc.:

4 rev. 6/27/51 Flashing Details at E. & W. Ramps  
and Exit Doors

Will you please return two (2) prints of the above drawing, marked  
with your approval or necessary corrections.


Very truly yours,

FULLER-TURNER-WALSH-SLATTERY, INC.

*C. E. Reese*

C. E. Reese  
Project Engineer

CER/MH/eas



ISSUANCE OF DRAWINGS

OFFICE COPY

2 July 1951

6 July 1951

GA & North Parking

Fuller-Turner-Walsh-Slattery

hand

Submitted by Munder

2

4

13Mar'51

Flashing Details at E & W Ramps & Exit Doors

(APPROVED 5 July 1951 P.B. /GEA)

RECEIVED

JUL 6 1951

FULLER-TURNER-WALSH-SLATTERY  
INCORPORATED

*SV Tyler*



120-5-18-9

cc; Bohanon Nelson Weigel  
Healy Harris Hopper  
Zunser VanName Hannegan  
Seelman S & H - 2

2 July 1951

Fuller-Turner-Walsh-Slattery, Inc.  
403 East 42 Street  
New York 17, New York

Re: General Assembly and Northerly  
Portion of the Parking Garage  
Contract HQ 1/52 - Electric  
Reference Drawings No. GA-E-3L  
and No. GA-E-4L

Gentlemen:


Please be advised of the following changes and proceed accordingly with the installation of the work:

Reference Drawing GA-E-3L:

- a. Substitute fixtures Type No. 103 in lieu of Type K K now called for in the passage to the south porch located between column lines I and J and column lines 18B and 20.
- b. Substitute fixtures Type No. 103 in lieu of Type K K now under the soffit of the ramp directly over Stair No. 26 located between column lines H and I and column lines 27 and 28.

The above fixtures shall be weatherproof and of aluminum as agreed upon by the office of Fischbach & Moore and Mr. Hellegers of Syska & Hennessey's office.

Reference Drawing GA-E-4L:

- 
- a. A total of twenty (20) No. 103 fixtures under the soffits of exit doors on the east and west sides of the building at elevation /53' shall be of aluminum and weatherproof type.

Please submit for our consideration the prices which affect the Contract Price.

Very truly yours,



JJH:eam

James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office

120.5-18-92  
2 July 1951

Fuller-Turner-Malsh-Slattey, Inc.  
403 East 42 Street  
New York 17, New York

Re: General Assembly and Northerly  
Portion of the Parking Garage  
Contract No. 1/82  
Electric

Gentlemen:

Please refer to Drawing GA-E-4P and proceed with installing the work as follows:

Sub-feeder No. LC1B-1-204A from Lighting Panel  
2A to Lighting Panel 2E:


a. The feeder now specified is 4/3/0 - 2 1/2" C.

Since Lighting Panel 2E has been relocated in  
accordance with our letter dated 31 May 1951,  
the feeder and conduit has been changed to 4/4 -  
1 1/2" C. This was originally sized in error. Fischbach  
and Moore have been verbally informed of this revision.

The change should result in a credit.

Very truly yours,

James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office

  
JAD:eam  
cc: Bohanon  
Nelson  
Weigel  
Healy  
Harris  
Hopper  
Zunser  
VanName  
Hannegan  
Seelman  
S & H - 2



2 July 1951

Fuller-Turner-Walsh-Slattery, Inc.  
403 East 42 Street  
New York 17, New York

Re: General Assembly and Northerly  
Portion of the Parking Garage  
Contract HQ 1/82 - Heating,  
Ventilating and Air Conditioning


Gentlemen:

Please refer to your letter of 26 June 1951 wherein you state that National Sheet Metal Company's Shop Drawing GA-1B-7, dated 1 May 1951, involves acoustical treatment of ducts passing through No. 3 fan room wall into Committee Room No. 7. In the third paragraph of the same letter, you request instructions how to proceed.

Proceed with the addition of this acoustical treatment as indicated on the returned shop drawing and submit for our consideration prices which affect the Contract Price.

Very truly yours,

James A. Dawson  
Co-Ordinator of Construction  
Headquarters Planning Office

  
cc: Bohanon  
Nelson  
Weigel  
Healy  
Harris  
Hopper  
Zunser  
VanName  
Ryer  
Hannegan  
Rumpelstin  
S & H - 2

